



PROJECT QUARTERLY REPORT

Project ID: 00106724

Reporting Period: April 2020 – June 2020





Ref: UNDP -TUR-20200724-0008681

Dear Jessie Kuykendall,

Subject: Effective Urban Waste Management for Host Communities Phase II: Strengthening Social Cohesion through Participatory Waste Management Project Quarterly Progress Report

Reference is made to the contribution agreement between United States Bureau of Population, Refugees and Migration and UNDP for the project “Effective Urban Waste Management for Host Communities Phase II: Strengthening Social Cohesion through Participatory Waste Management” effective since May 2019.

I am pleased to submit herewith the Quarterly Progress Report for the abovementioned project.

The report summarizes the progress of the project as of April 2020 and provides an overview of the achievements, challenges, lessons learned, interim financial status and way forward.

I thank United States Bureau of Population, Refugees and Migration for its contributions to UNDP and look forward to strengthening our partnership in support of development in Turkey.

Mr. Sukhrob Khojimatov
Deputy Resident Representative
UNDP Turkey

Attached:

“Effective Urban Waste Management for Host Communities Phase II: Strengthening Social Cohesion through Participatory Waste Management” Progress Report

Ms. Jessie Kuykendall
Deputy Refugee Coordinator
United States Bureau of Population, Refugees and Migration



Reporting Period	April-May-June-2020
Donor	United States Bureau of Population, Refugees and Migration (USBPRM)
Country	Turkey
Project Title	Effective Urban Waste Management for Host Communities Phase II: Strengthening Social Cohesion through Participatory Waste Management”
Project Locations	Şanlıurfa and Kilis
Project ID (Atlas Award ID)	Project ID: 00105448
Outputs (Atlas Project ID and Description)	Output ID: 00106724,
Strategic Plan and/or CPD Outcomes	The project aims to contribute to the social cohesion of Syrians under temporary protection (SuTP) with host communities in the Southeast Anatolia Region
Implementing Partner(s)	Ministry of Environment and Urbanization
Project Start Date	May 2019
Project End Date	November 2020
LPAC Date	3 July 2018
Steering Committee/Project Board Meeting Dates	N/A
SDG linkages	SDG 5, SDG 12, SDG 13
GEN marker	GEN2
(Year) Delivery to Budget Ratio	% 37.9
Total resources required	3,000,000 USD
Revenue received	<ul style="list-style-type: none"> • Regular USD • Other <ul style="list-style-type: none"> ○ Donor: 3,000,000 USD ○ Trust Fund Cost Sharing USD ○ Thematic Trust Fund C/S USD ○ Special Activities USD ○ EU funding USD • Total: 3,000,000 USD
Unfunded budget	0.00 USD
UNDP Contact Person	Sukhrob Khojimatov Deputy Resident Representative UNDP Turkey Email: Sukhrob.khojimatov@undp.org Tel.: +90 312 454 1162



I. Executive Summary

The Project aims to contribute to the social cohesion of Syrians under temporary protection and host communities in the Southeast Anatolia Region. The Project will do so through participatory waste management practices and reduce the negative impact to the local environment and public health.

The overall objective of the project is to strengthen the resilience of impacted municipalities in targeted areas to be better able to cope with and recover from the impact of the Syria crisis particularly the unprecedented increase in demand for municipal services. The project aims to strengthen recycling capacities of municipalities and local communities to improve resource recovery, including community based and participatory waste collection models.

Therefore, the project mainly aimed to establish the zero-waste management system in Şanlıurfa Haliliye and Kilis Municipalities through identifying the needs of these municipalities and preparation of distinctive roadmaps. Two roadmaps were prepared that includes all the needs and suggestions for the improvement of zero waste management in these municipalities. In line with these roadmaps and in line with the project document, it is decided to supply waste vehicles and collection equipment to the related municipalities.

For this purpose, six tenders were published for the purchase of these equipment. All contracts were signed between UNDP and the companies during the reporting period. The delivery of some of the items started in June while the rest of the equipment and waste vehicles will be delivered to the related municipalities until the end of November 2020.

The project is providing support to the beneficiaries for the establishment of Civic Amenity Centers which is obligatory for all the municipalities as per the instructions of the Ministry of Environment and Urbanization. Design and drilling work and soil investigation reports has been completed for both of the municipalities. Technical terms of references for both municipalities were prepared, and tender will be published for the construction work in July.

To better understand the level of awareness about zero waste in related cities and the impact of the project, the project focused on a Stakeholder Analysis and Social Behavior Assessment study. This activity has been started, field visits were realized to the related cities, a stakeholder analysis report was prepared, and the first-round surveys were completed. Before the closure of the project, it is decided to implement 2nd round surveys to asses the impact of the project.

The project will also provide support for the establishment of effective collection methods through conducting trainings to schoolteachers, university academicians and admin people of schools and universities and to the public staff. In line with these trainings also awareness raising activities will be implemented in parallel to support community driven recycling.

In line with the project activities, two women's cooperatives will be supported to bring livelihoods options for women through manufacturing products from recyclables.

As a result of the activities carried out during the reporting period, six tenders were awarded, planning of how to implement supporting of two women's cooperatives activity is completed, training and



awareness raising activity's tender process is closed and finalized, delivery of equipment to the beneficiaries started, 1st round surveys were conducted, for the civic amenity centers; design, drilling and soil investigation reports were prepared, technical terms of references for the construction of these centers were completed. Also, various meetings with related beneficiaries and implementing partner were conducted.

II. Background Information

Turkey hosts the largest refugee population in the world and has demonstrated strong national ownership of the refugee response. The Government of Turkey provides a rights-based legal framework through the Temporary Protection regulation, which offers access to education, health care, employment and social security to Syrians.

Currently, out of the 3,6 million registered Syrians under Temporary Protection more than 2,6 million Syrians live amongst Turkish host communities.¹ 45% of the 3,2 million Syrians under Temporary Protection are concentrated in 4 provinces in the South East. Within these provinces there are four municipalities in Turkey that are particularly impacted each hosting more than 100,000 Syrians.

In these cities, the ratio of the Syrian population to that of host communities is higher than 15%, including Kilis, Hatay, Gaziantep and Şanlıurfa.² Population have either reached or exceeded 2023 population projections. Kilis, for instance, hosts almost as many Syrians as its local population. Therefore, Turkish urban areas are under pressure due to sudden and unexpected population growth. Municipalities, with their already strained capacities, even before the arrival of the displaced Syrians, are trying to cope with the pressure on the basic public service delivery, such as waste, waste management and firefighting capabilities.

UNDP has developed a comprehensive Solid Waste Management Strategy that guides overall support to the Government of Turkey, when responding to the Syria crisis. In line with the Solid Waste Management Strategy, the project will strengthen the municipal capacities for more efficient and effective waste management services. This will be achieved through increasing social cohesion by participatory waste management, creating new and dignified livelihoods opportunities through bringing Syrians and host community members together over common economic and social interests and to increase municipal service delivery capacities of Kilis and Şanlıurfa Haliliye Municipalities.

¹ Official data Directorate General for Migration Management, Turkey, July 2020.

² Republic of Turkey – Ministry of Interior Directorate General of Migration Management, Statistics – February 2019.



III. Progress Review

Output 1: Enhancing livelihoods opportunities and social cohesion improved for Syrians and host communities as a result of skills development in the waste recycling and related sectors and strengthened municipal waste management capacities and reduced operational costs through recycling initiatives

Activity 1: Assessment of district layouts and current routes of transportation and local value chains of solid waste by the municipalities and design and initiation of public awareness campaign to support community driven recycling.

In line with project outputs and activities, firstly technical field visits was conducted together with the Project team, related municipality staffs and the Individual Consultant (IC) that was employed to identify the needs of both Şanlıurfa-Haliliye and Kilis Municipality were conducted between the dates 15-20 July 2020. This technical visit was especially made to the municipalities that has developed zero waste management system. Five municipalities; İstanbul-Esenler, İstanbul-Beykoz, İzmir-Çiğli, İzmir-Karabağlar and Antalya- Muratpaşa were visited. Good and bad experiences of these municipalities were shared by the representatives. Various topics such as participation of households, usage of outdoor and indoor equipment, waste vehicles, civic amenity centers, mobile civic amenity centers, data and information management, application to collect waste from smart phones were discussed.

After realization of these field visits in July 2019 and conduction of preliminary surveys in August 2019 IC and Project Team worked with each municipality's related staff to plan the basic needs and to establish Zero Waste System. Data and information, legislation about Zero Waste System was deeply analyzed. Specific needs analysis reports were prepared for both municipalities as a roadmap for the project.

This activity is planned according to the needs analysis reports that were prepared in September 2019 for the municipalities. Current routes and district layouts were identified together with municipality project team and UNDP in September 2019 and details of these assessments were shared inside this report. According to the needs analysis reports of both municipalities, training and awareness raising activities was planned to be given in both cities in parallel with the awareness raising activities. This activity is planned to be implemented at the beginning of Spring 2020 but cause of the pandemic resulting in restriction about group gatherings, closure of schools, universities and also adaptation of rotational work modality for public offices, this activity has to be shifted to September 2020 together with the trainings about zero waste.

Tender was published for this activity on 4 March 2020 and closed on 15 April 2020. Normally this tender closing date is firstly mentioned as 25 March 2020, but cause of Covid-19 pandemic, companies requested more time to compile their offers and extension was given until 1 April 2020. Cause of Covid-19, second and third extension was requested from companies again as the situation got worse in Turkey. As a result, UNDP Project team and Procurement Unit discussed this issue and extended the tender closing date till 15 April 2020. Contract was signed with the company and the planning of the activity has been started.



Activity 2: Design and planning of collection and incentivization models, facilitation of private sector participation by the establishment of women's collectives for handicraft/product manufacturing from recyclables.

For the design and planning of collection and incentivization models for the municipalities, it is planned to employ an IC to work with both of the municipalities to better design this system.

For the supporting of women's cooperatives activity, that is decided to be implemented in Kilis province, is aimed to increase the added value, profitability, social, environmental and economic benefits of olive pomace. Pomace is a waste of olive oil factories; it is an important biomass variety seen in Mediterranean countries. If it does not have a suitable and acceptable use, it creates environmental problems. Pomace can be considered as an alternative fuel (renewable energy) that do not contain sulfur. Efficient and appropriate use of pomace in energy generation provides solutions to 1) clean energy production, 2) the recovery of this substance, which is the waste of olive oil plants. A very high calorie (4674 kcal / kg) and low ash (1.5%) fuel can be obtained by separating the core in the pomace. The second most important product obtained from pomace is pomace oil used in cosmetics and soap industry. In addition, the remaining pulp can be processed in bioreactors and can be added to cattle feed and/or used as fertilizer. Women cooperatives can generate a sustainable income by converting olive oil to be obtained from pomace waste into soap (local olive oil soap).

In Kilis, both the development cooperative and the Olive Cooperatives and Producers Union will work cooperatively.

The Development and the Olive Oil Cooperatives has 80 members, and 60 are women. The union has about 350 members. 100 of these members are women. The facility, which belongs to the Union, currently has an olive processing capacity of 160 tons/day. In olive oil production process, an average of 25-30% oil is obtained from olives, 30% solids (pomace) and 40-45% water is produced. As a result of the support to be made by our project, the environmentally damaging pomace waste generated at the facility of the union will be processed and the olive oil to be obtained will be processed by the cooperative members and turned into soap. Thus, both the environment will be protected and a sustainable facility where women will work intensively will be established. Also, 10 women will be employed in the soap house and 20 women will work in the brine facility of the cooperative which is used for the separation of the olives and which is used for the packaging of the olives after ripening period. Again, within the scope of our project, trainings on various subjects (women's rights, communication techniques, entrepreneurship, project preparation, production techniques, sales marketing etc.) will be given to at least 40 women who are members of the Union and 60 women who are members of the cooperative. Thus, support will be provided in social, economic and cultural areas to 100 women who are members of unions and cooperatives in Kilis.

Within the scope of this activity, for Haliliye Municipality, it is decided to make composting (which is a natural fertilizer used to enrich and regulate the structure of the soil, which will be used for growing plants or flowers) that will be possible from organic wastes from 7500 households and 500 restaurants and pruning wastes (September/October and February/March) obtained from parks/gardens. The



minimum of 3 tons of vegetable and fruit waste produced daily in the marketplaces in Haliliye will also serve as an input for the compost. The compost will create more value addition when mixed with worm, animal manure or liquid fertilizers which yields a more nutritious organic fertilizer which can stimulate local agriculture which provides the largest employment for the Syrians and the host-communities in the project locations. Besides the environmentally friendly disposal and re-use of the oil pomace, the women's cooperatives will be able to generate more income by producing various seedlings and ornamental plants using these products which will significantly reduce their fertilizer cost.

The Cooperative established in Şanlıurfa has a total of 42 members. 35 of them are women and 10 of them are Syrians. This number will increase day by day. Both communities have efforts to social integration, to help women's income generating activities and to support local economic development. Cooperative members are currently growing peppers on an area of 15 hectares. It is planned to grow the seedlings of these and similar plants and to grow Geofit (bulbous and tuberous garden plants) and some ornamental plants that Haliliye Municipality needs. The cooperative will sell ornamental plants to the municipality. For this purpose, it is planned to build a 1000 m2 high tunnel (stove heated) greenhouse for the Cooperative. By sharing some of the compost and worm manure to be obtained with the Cooperative members, it is planned to support their agricultural production. The municipality will also obtain the ornamental plants it needs. In addition, the municipality, will have the opportunity to distribute poor people pepper, eggplant etc. seedlings. Thus, 20 women who are members of the cooperative will be employed in Şanlıurfa and 100 women will be provided with various training and production infrastructure opportunities, and support will be provided in social, economic and cultural areas.

This activity is planned to be started in late August 2020.

Activity 3: Support to municipal community centers for the establishment of training workshops and ateliers and implementation of specific skills training programs directed at members of Syrians and host community on recycling operations.

This activity is planned to be implemented in parallel with the establishment of Civic Amenity Centers. Textile, furniture, toy, domestic appliance recycling ateliers will be established inside these centers. Specific skills training programmes will be given to Syrians and host community members after the construction of these centers were completed. This activity is planned to be implemented after December 2020 when the ateliers and all of the equipment needed should be ready to use during the conduction of the trainings.

Activity 4: Operationalization of the participatory network with design and initiation of public awareness campaign to support community driven recycling.

This activity will be implemented in parallel with zero waste training activity. Cause of pandemic, this activity had to be postponed till September 2020.



Activity 5: Provision and installation of supplementing equipment and vehicles to support collection mechanism, including establishing smart waste collection systems.

According to the needs analysis reports of both municipalities, an IC was employed to prepare the technical specifications for the procurement of waste vehicles and supplementing equipment to the related municipalities. Three (3) tenders were published and all of the contracts were signed with the companies.

- **Procurement of Vehicles**

Tender was published on 11 February 2020 and tender was closed on 20 March 2020. Normally, the closing date of this tender was published as 10 March 2020, but due to the Covid-19 pandemic, closure date was extended till 20 March 2020. Contract was signed between UNDP and the company. 3 types of vehicles will be delivered to the related municipalities until the end of November 2020.

- **Procurement of Vegetative Oil Waste and Organic Deposit Equipment**

Tender was published on 5 March 2020 and closed on 19 March 2020. Contract was signed between UNDP and company on 7 May 2020. Equipment were delivered to the related municipalities on 10 June 2020.



Organic Waste Bin (5 lt)



Waste Vegetative Oil Recycle Bin (5 lt)



Waste Vegetative Oil Recycle Bin (20 lt)

- **Procurement of Outdoor and Indoor Equipment**

Tender was published on 20 April 2020. Contract was signed between UNDP and the company on 30 June 2020. All equipment will be delivered to the related municipalities until the end of November 2020.



Empowered lives.
Resilient nations.



Activity 6: Installation of civic amenity center(s) along with containers with sensor arrays and reverse vending automats.

According to the needs analysis reports of both municipalities, an IC was employed to identify the technical specifications needed for the procurement of automat machines and civic amenity centers. Two (2) tenders were published and all of the contracts were signed.

- **Procurement of Automat Machines**

Tender was published on 25 February 2020 and closed on 12 March 2020. Normally, the closure date of this tender was published as 9 March 2020, but cause of request for extension from the companies, closing date was extended till 12 March 2020. Contract was signed between UNDP and company on 29 May 2020. Delivery of these equipment to the related municipalities will be completed until the end of August 2020.



- **Procurement of Mobile Civic Amenity Centers**

Tender was published on 27 February 2020 and closed on 12 March 2020. Contract was signed between UNDP and the company on 20 May 2020. These centers will be delivered to the related municipalities until the end of October 2020.

Activity 7: Starting up and facilitating the community warden initiative and linking local licensed recycling companies with participatory source segregation for ensuring sustainability.

Kilis and Haliliye Municipalities will make agreements with licensed companies for the collection and sorting of recycled waste. This was included in the protocol signed between the municipalities and the ministry and became a must for municipalities. In addition, as a project team, discussions were made



with the recycling company, which already has an agreement with Kilis municipality, and a recycling company operating in Şanlıurfa.

Activity 8: Execution of Stakeholder Analysis and social behavior assessment study & Conduction of surveys

A Stakeholder Analysis and Social Behavior Assessment study is planned to be conducted in order to understand the contribution of the Project to the local people and the municipalities. This study is planned to be provided to better understand the level of awareness about zero waste management in targeted provinces. This activity is held for twice during the life of the project; one in the beginning and one before the closure of the Project.

The processes of this activity have already started since November 2019. An IC was employed. The IC realized a visit to Şanlıurfa and Kilis with Project Field Staff between the dates 15-19 November 2019 to measure the awareness and tension about zero waste. Şanlıurfa Haliliye and Kilis Municipalities, public education centers, hotels, some of the school representatives, some NGO representatives, Directorate General of Migration Management were visited.

After this visit, the IC has delivered Stakeholder Analysis report to the Project Team on 3rd of January 2020.

Conduction of 1st round surveys and in-depth interviews were planned to be implemented between 15-18 March 2020, but due to the Covid-19 pandemic, this activity had to be postponed. The IC started conducting 1st round surveys in July 2020. Around 400 surveys have been conducted in Haliliye and Kilis Municipalities.

Picture from the surveys that were conducted between the dates 2-6 July 2020





Delays and challenges in the implementation of project activities

The project was planned to be implemented between March 2019 and September 2020 according to the previous no-cost extension letter.

But through declaration of COVID outbreak as pandemic by WHO has emerged as a new challenge affecting the global society. Since the duration of this situation is unknown at the moment; it has unfortunately negative effects on the project implementation.

Currently as a response to this pandemic, official travels, attendance to meetings/workshops and organization of trainings were postponed, such meetings are being conducted via Skype, Zoom or teleconference when possible.

There is risk not to complete two of project activities on time. One of the activities of the project has to be suspended is training and awareness raising activity, the target audience of this activity is schools, universities and public staff. As the schools and universities were temporarily closed since 16 March 2020 and the opening date for schools is published as the next season, this activity has to be suspended till September 2020. The second activity is about supporting women's cooperatives to be made operational, this activity also has to be suspended. Within the scope of supporting women's cooperatives activity, researches have been conducted for a long time to identify, conceptualize, implement and

integrate this activity in a more efficient (competitive, inclusive and innovative) way. Cause of Covid-19, the women's cooperatives and related public institutions and organizations with which we will conduct the activity together were either closed or operating at a low level during the pandemic process.

In consideration of the delayed kick-off and impact of COVID-19 on project implementation, we requested extension from the United States Bureau of Population and Refugee Management (USBPRM) to extend the project completion date from 30 September 2020 to 30 June 2021.

As some of the project activities were delayed in terms of their starting date, it is foreseen that the actual starting date of the activities will take more time. With the extension of time, we will have the opportunity to implement these works, which can be integrated via exemplary, effectively and efficiently.



Empowered lives.
Resilient nations.



Indicator Based Performance Assessment

EXPECTED RESULTS	PLANNED ACTIVITIES	TIME	RESPONSIBLE PARTY
Result: <i>Improving Livelihoods and developing social cohesion for “Women Cooperatives” comprising of host community women and Syrian women by recycling and improving skills and capacity</i>	1.1 As a result of the negotiations with municipalities and women's collectives, determination of prominent recycling ideas and establishing collaborations	Completed	UNDP, Ministry of Environment and Urbanization (MoEU), Kilis ve Şanlıurfa Municipalities, Birlik, Cooperatives (1 and 2)
	1.2 Sectoral research and technical study trips with stakeholders to produce value added products suitable for the local from recycled wastes	Completed	
	1.3 Preparation of necessary machinery equipment, construction technical specifications and budgets in the light of researches and interviews	August 2020	
	1.4 Signing of protocols between MoEU and relevant women's cooperatives	August/ September 2020	
	1.5 Making tenders for construction and purchasing machinery equipment	September- October 2020	
	1.6 Construction works and purchase of machine and equipment	October- December. 2020	
	1.7 Starting to Production, Sales and Marketing	Nov/2020 - May/2021	
	1.8 Implementing awareness, skill development and training programs	October/2020-March 2021	

	for the Women's Cooperative members		
	1.9 Supporting promotion and marketing activities for the sustainability of the products to be produced	January-May 2021	





IV. Contribution to Gender Equality

Gender is a key element for this project as waste management at homes are managed mostly by women. Gender marker of the project is GEN2 which means that the project is gender responsive. Despite the project has not been specifically dedicated to gender but issues related to gender have been taken into consideration in all phases of the project. GEN 2 project refer to differentiating needs, status, rights, distribution of benefits of men and women.

In addition to understanding different approaches to and roles of men and women in waste management, one of the main activities of the project is to support women's cooperatives which will provide livelihood opportunities for women while supporting empowerment of them through basic skills trainings, increasing their awareness on gender equality, expanding their ability of organization and solidarity and facilitating their participation into decision-making mechanisms.

V. Project Risks and Issues

In line with the activities of the project, possible foreseen risks in the future are defined below:

ACTIVITY	RISKS	MITIGATION STRATEGY
Conduction of Training Activity about Zero Waste	This activity was planned to be implemented between September 2020- January 2021 but has to be postponed to later dates if a second-round pandemic starts.	Online face to face sessions can be applied, trainees can follow the sessions through online trainings.
Supporting Women's cooperatives activity	In line with this activity, specific skills trainings will be given to women, if a second pandemic occurs, this activity has to be postponed to later dates	Additional time will be needed.
Construction of Civic Amenity Centers	If a second-round pandemic starts, construction work has to be slowed down and additional time will have to be given to the company for the completion of the work.	Additional time will be needed.

VI. Monitoring Arrangements

Project Steering Committee meeting will be arranged in late September 2020 according to the availability of partners and USBPRM.



A field visit has been carried out to Kilis and Şanlıurfa between 10- 14 February 2020 by Syria Crisis Response and Resilience Portfolio (SCRPP) Manager Raged Assi, Monitoring & Evaluation Advisor Serap Öztürk and the project team. Various meetings were held with relevant stakeholders for better coordination of project activities. As a result of the monitoring visit, Project Team suggested to Haliliye Municipality to accelerate the land allocation for the civic amenity center to start the design work not to cause any delays.

Visited stakeholders are listed below:

- Kilis Anatolian Religious High School
- Saraç Mehmet Multi-Purpose Community Centre
- Kilis Chamber of Merchants and Craftsmen
- Protection of the Orphan and Refugee Women and Men, Education, Culture and Social Solidarity and Life Development Association
- Kilis Entrepreneur Women's Solidarity and Contribution Association
- Kilis Organized Industrial Zone and Visit to Some Companies on Recycling
- Kilis Provincial Directorate of Environment and Urbanization
- Kilis Municipality
- Kilis University Rector and Relevant Academicians
- Kızılırmak Recycling Company
- GAP Regional Development Administration
- Karacadağ Development Agency
- Haliliye District Directorate of National Education
- Şanlıurfa Provincial Directorate of Environment and Urbanization
- Şanlıurfa Chamber of Trade and Industry
- Haliliye District Directorate of Mufti
- Şanlıurfa Organized Industrial Zone and Visit to Some Companies on Recycling

VII. Lessons Learned

Project activities included construction of two civic amenity centres, to find more sustainable solutions for the waste management. Each construction activity involved design, drilling and soil investigation work stages. Deficiency about the mobilization of one of the partners for the establishment of civic amenity centre caused delays in the implementation period of this activity. This has caused re-organization of the beneficiary and took longer time than expected to start for the design work. Strong efforts were made to coordinate and to make required linkages between the project activities, UNDP Project Team has contacted all of the partners during the pandemic time not to cause any problems and to update relevant partners about the ongoing project activities.

VIII. Conclusions and Way Forward


Annual work plan of the project was updated according to the delays in the implementation of project activities. Upcoming project activities are defined below:



- Tender will be published for the construction work of two Civic Amenity Centers: one for Kilis and one for Şanlıurfa Haliliye Municipality at the beginning of August 2020.
- Equipment will be purchased for the recycle ateliers at the beginning of October 2020.
- Supporting women's cooperatives activity is planned to be started in September.

IX. Financial Status

The below Figure represents the current status of the project budget, expenses and the commitments as of 30 June 2020. 2nd tranche of the project payment was requested in late April 2020 from Payment Management System. 3rd tranche of the project payment is planned to be requested in September 2020.

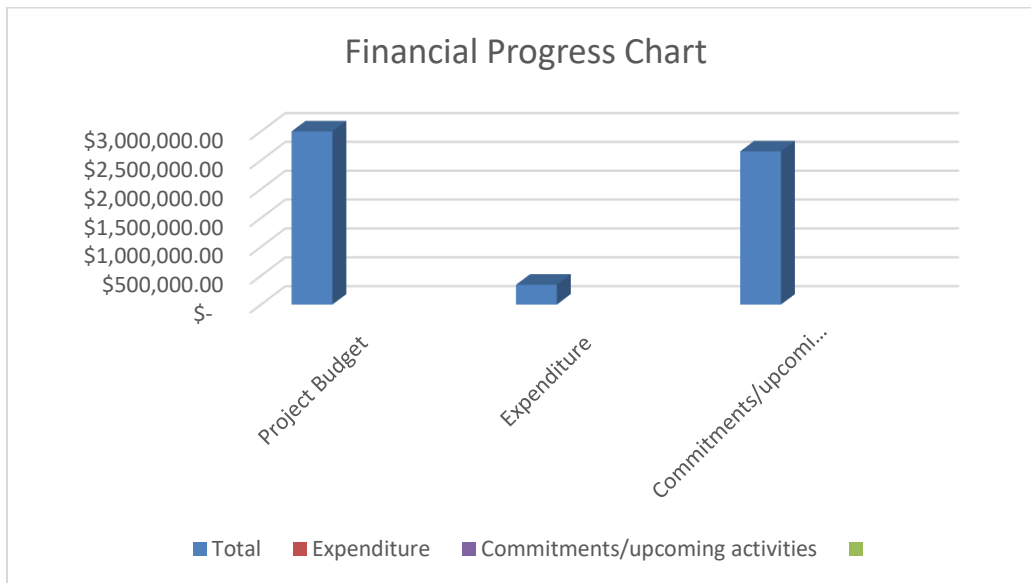

Annexes

- Annex 1: Technical Field Study Report
- Annex 2: Needs Analysis of Şanlıurfa Haliliye Municipality
- Annex 3: Needs Analysis of Kilis Municipality
- Annex 4: Stakeholder Analysis Report

Certificate Of Completion

Envelope Id: 50DB4CC632664EC0A732581EDC3FCA4B	Status: Completed
Subject: Please DocuSign: Project Quarterly Report 2 Final Version.pdf	
Source Envelope:	
Document Pages: 18	Signatures: 0
Certificate Pages: 1	Initials: 0
AutoNav: Disabled	Envelope Originator:
Envelopeld Stamping: Disabled	Violet Vural
Time Zone: (UTC-08:00) Pacific Time (US & Canada)	One United Nations Plaza
	New York, NY 10017
	violet.vural@undp.org
	IP Address: 88.240.83.168

Record Tracking

Status: Original	Holder: Violet Vural	Location: DocuSign
7/24/2020 4:02:13 AM	violet.vural@undp.org	

Signer Events

Signature	Timestamp
Violet Vural	Sent: 7/24/2020 4:02:32 AM
violet.vural@undp.org	Viewed: 7/24/2020 4:02:48 AM
UNDP Headquarters	Signed: 7/24/2020 4:05:32 AM
Security Level: Email, Account Authentication (None)	Freeform Signing
Electronic Record and Signature Disclosure: Not Offered via DocuSign	

In Person Signer Events

Signature	Timestamp

Editor Delivery Events

Status	Timestamp

Agent Delivery Events

Status	Timestamp

Intermediary Delivery Events

Status	Timestamp

Certified Delivery Events

Status	Timestamp

Carbon Copy Events

Signature	Timestamp
Violet Vural	Sent: 7/24/2020 4:05:34 AM
violet.vural@undp.org	Resent: 7/24/2020 4:05:35 AM
UNDP Headquarters	Viewed: 7/24/2020 4:06:11 AM
Security Level: Email, Account Authentication (None)	
Electronic Record and Signature Disclosure: Not Offered via DocuSign	

Witness Events

Signature	Timestamp

Notary Events

Signature	Timestamp

Envelope Summary Events

Status	Timestamps
Envelope Sent	7/24/2020 4:05:34 AM
Certified Delivered	7/24/2020 4:02:49 AM
Signing Complete	7/24/2020 4:05:34 AM
Completed	7/24/2020 4:05:34 AM

Payment Events

Status	Timestamps
