Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

United Nations Development Programme

MULTI-COUNTRY PROJECT DOCUMENT

Project Title: Management of Plastics Waste and Circular Interventions on Plastics in South, Southeast Asia, and the Pacific (Short name: TCCF Plastics Circularity Project)

Quantum Contract/Award ID: 1310085

Start Date: 1 November 2024 **End Date:** 31 October 2027 **PAC Meeting date:** 27 September 2024

Countries Participating: Bangladesh, Bhutan, Cambodia, India, Maldives, Nepal, Philippines, Sri Lanka, Vietnam and Indonesia

Country	Implementing Partner	Quantum Project ID	Outputs to be delivered by country
Bangladesh	UNDP	01003421	**Output 1:** Strengthened collaboration with stakeholders to promote plastic waste circularity. **Output 2:** Plastics Waste Market System Developed **Output 3:** Gender responsive information and plastic waste traceability mechanism established. **Output 4:** Awareness, knowledge, and capacities been developed among urban residents
Bhutan	UNDP	01003430	**Output 1:** Awareness programs developed and deployed to support behaviour change in schools, colleges, hotels and monasteries. **Output 2:** Increase plastic waste collection through deployment of best environmental practices and technologies such as compactor trucks, and value addition machines. **Output 3:** Capacity of waste handlers (formal and informal) developed in proper segregation and hygiene. **Output 4:** Project communication, advocacy and knowledge management
Cambodia	UNDP	01003431	**Output 1:** Priority business models for plastic alternatives and plastic recycling operationalized. **Output 2:** National capacity enhanced and improved awareness about the plastic crisis and its solutions among citizens and the private sector. **Output 3:** Plastic waste leakage reduced in target provinces and cities.
India	UNDP	01003432	**Output 1:** Ensured the successful enrolment of 10,000 waste workers in government social protection programmes by addressing access barriers and strengthening service linkages. **Output 2:** Enhanced awareness about rights and entitlements for 50,000 waste workers through outreach and support via Helpline. **Output 3:** Channelized 8,000 MTs of responsibly sourced plastic waste through value chain partners. **Output 4:** Strengthened national capacities and developed comprehensive guidelines for effective plastic waste management.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Indonesia	UNDP	01004820	Output 1: Increased knowledge, skills, and safety of waste workers within CBOs to enhance their role in the circular economy Output 2: Improved waste collection systems and recycling rate to support waste workers' livelihoods Output 3: Strengthened financial resilience of waste workers by improving access to funding and sustainable business models Output 4: Strengthened institutional, policy, and regulatory frameworks for integrated and collaborative plastic waste management Output 5: Effective knowledge management, outreach, and monitoring system for plastic waste management
Maldives	UNDP	01003433	**Output 1:** Conduct Waste Management Workshops with key stakeholders to showcase best practices, explore local level context (challenges and opportunities) and discuss standardization of plastic waste management. **Output 2:** Identify, document, and amplify Best Environment Practices at local level through Best Available Technology support grant(s) **Output 3:** Establish plastic processing pilot in Maldives to enhance plastic waste management and recycling in a target region. **Output 4:** Provision of electric vehicles and renewable energy infrastructure and capacity to the Waste Management Corporation for key population centres. **Output 5:** Information and Guidelines on Plastics and Waste Management Strengthened in a gender-responsive manner through development of a learning platform and training of management personnel of WAMCO. **Output 6:** Translate and upload training modules to the learning portals.
Nepal	UNDP	01003434	**Output 1:** Material Recovery Facilities (MRFs) are equipped with processing and management technologies. **Output 2:** Waste workers and communities are empowered with awareness campaigns, skills, and livelihood opportunities.
Philippines	UNDP	01003435	**Output 1:** Inclusive, sector-specific business models successfully developed and integrated into the existing waste diversion system, enhancing efficiency and sustainability in plastic waste management of the locality. **Output 2:** Local capacity to improve local plastic waste collection, recovery and recycling strengthened. **Output 3:** Plastic recovery and recycling operations of at least two GEDSI/ informal waste picker groups organized and scaled up. **Output 4:** Behavioral change modules for the targeted plastic waste sources developed and implemented.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

			Output 5: Digital application that enables waste diversion tracking with incentives or reward system deployed.
Sri Lanka	UNDP	01003436	**Output 1:** Systemic approach to plastic waste management adopted and practiced at the selected Local Authorities. **Output 2:** BAT/BEP options are introduced to implement strategies developed under Output 1 **Output 3:** Implement a phased campaign over the project period (3 years) on plastic pollution prevention and build capacity of Local Authorities and stakeholders. **Output 4:** Share lessons learned from demonstrations and interventions at the selected project locations, across LA areas.
Vietnam	UNDP	01003437	**Output 1:** Enhanced multi-stakeholder collaboration and innovation within the Viet Nam NPAP, promoting knowledge exchange and effective solutions for plastic pollution. **Output 2:** Successful deployment of waste-back-to-shore schemes in 3 fishing ports, and pilot implementation of harmonized responsible sourcing framework, enhancing working conditions and social protection for informal waste workers. **Output 3:** Support for waste sorting at source regulations, improving plastic waste management in Ha Noi through capacity building and public awareness campaigns. **Output 4:** Two national communication campaigns launched to promote waste sorting and plastic recycling.
Bangkok Regional Hub	UNDP	01002871	**Output 1:** Strengthening joint regional actions. **Output 2:** Provide technical assistance to countries. **Output 3:** Facilitating cross-pollination of knowledge and solutions. **Output 4:** Engaging partners and donors on resources mobilization and collective action. **Output 5:** Providing coordination, monitoring, evaluation, and reporting services to country-based components.

Brief Description

Brief narrative outlining the scope, outputs and management arrangement of the project for this multi-country initiative and/or south south and triangular cooperation

The TCCF Plastics Circularity Project aims to address the critical issue of plastic waste management in ten countries across Asia. This initiative targets countries with varying levels of waste management infrastructure and plastic waste challenges, including India, Bangladesh, Bhutan, Nepal, Maldives, Sri Lanka, Philippines, Cambodia, Vietnam, and Indonesia. The project is designed to support the transition to a circular economy by improving plastic waste management, promoting recycling, and reducing plastic leakage into the environment. By focusing on these targeted areas, the project will contribute to better public health, environmental protection, and the development of sustainable waste management practices. The project is expected to contribute to collect at least 69,110 tons of plastics and support 135,600 direct

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

beneficiaries during the implementation period across all ten participating countries. There are four components under the Project, namely:

1. *Stakeholder Engagement and Strategy Development.* The project will engage stakeholders to develop strategies and roadmaps for replicating and scaling up successful plastic waste management interventions. This includes the establishment of multi-stakeholder platforms to ensure gender-sensitive and inclusive participation. At the end of the project, 23 business models and/or Management Systems will be created or strengthened.

2. *Implementation of Best Environmental Practices (BEP) and Best Available Technologies (BAT).* The project will assist countries in deploying BEP/BAT for plastic waste management, including the establishment of Material Recovery Facilities (MRFs) and other processing units to improve the recycling and repurposing of plastics. At the end of project, 23 MRFs facilities will be implemented and/or strengthened.

3. *Strengthening National Capacities and Guidelines.* The project will enhance the capacities of national and subnational governments to implement plastic waste management strategies, develop guidelines, and strengthen regulatory frameworks. This includes integrating the informal sector into formal recycling systems and promoting gender-sensitive approaches. The project will generate direct benefits to72,100 people (of which 34,560 women) and contribute to strengthening national legal framework to support the plastic waste management transformation toward clean, sustainable and resilient system.

4. *Information Outreach and Knowledge Management.* Finally, the project will develop and implement comprehensive knowledge management strategies, including the documentation of best practices, capacity-building initiatives, and the dissemination of information through training, workshops, and awareness campaigns. At the end of project, 23 awareness /training programs will be delivered and a specific knowledge management platform on circular economy will be deployed and fully used.

The project will be managed through a two-tier structure comprising a Regional Component and National Child Projects in each of the nine participating countries: The regional component, managed by UNDP's Bangkok Regional hub, will coordinate the overall TCCF-UNDP partnership. It will ensure administrative synergy, provide technical assistance, and facilitate knowledge exchange among participating countries. Key activities will include monitoring and oversight, harmonizing outreach efforts, and promoting capacity-building initiatives across the region. The nine national child projects will be implemented by respective UNDP Country Offices, tailored to the specific needs and contexts of each country. National projects will focus on localized interventions such as improving plastic waste collection, piloting innovative business models for recycling, and assisting governments in strategy setting. Each Child Project will have dedicated management and operational teams to ensure effective implementation and monitoring.

This management arrangement will ensure a coordinated and integrated approach across all participating countries, with the Regional Hub providing strategic oversight and technical support while allowing for country-specific customization of interventions.

Total resources required:	USD 15,000,000	
Total resources allocated:	~~USD 15,000,000~~ USD 18,389,900	
	UNDP TRAC:	NA
	Donor (TCCF):	~~USD15,000,000~~ USD 18,389,900
	Government:	NA
	In-Kind:	NA
Unfunded:	NA	

Contributing Outcomes (UNSDCF/CPD or RPD):

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

The project results are contributing to the Regional Programme Development Outcome 1 / Output 1.4: Sustainable, scalable and innovative solutions and strategies for nature, climate and energy transformation strengthened through enhanced 'climate promise', nature-based solutions, and transitioning to clean energy and zero-carbon development.

1. **Bangladesh:** The project contributes to the Country Programme Document (CPD) Outcome 2/ Output 2.3: Government actors, the private sector and civil society demonstrate enhanced commitment and capacities to provide efficient oversight functions for environmental policies and legal frameworks, identifying financing solutions, and prioritizing green investments.

2. **Bhutan:** The project will play a critical role in managing a sustainable environment, reducing disaster risks and combating climate change. By focusing on reducing, repurposing and reduction of plastic waste, the project will address the environmental impact of plastic pollution which is a significant contributor to ecosystem degradation. The project aims to develop a circular economy business model together with the formal and informal waste handlers, private sectors and local governments to improve the waste management practices. The project contributes to UNSDCF outcome 3 (By 2028, Bhutan's Environment remains sustainably managed, and its people are more resilient to disaster risks and climate change and CDP Outcome 2.

3. **Cambodia:** The project contributes to the CPD indicator 1.2. by promoting circular economy (CE) to reduce of pollution and improved consumption behaviours and production practices.

4. **India:** The project aligns with the UNDP Strategic Plan 2022-2025 and the Country Programme Document (2023-2027), particularly focusing on: Outcome 2: No one left behind, with a focus on equitable access to opportunities and a rights-based approach to human agency and development. Particularly, the project contributes to Output 2.3: Expansion of robust and inclusive social protection systems, improving access to assets and services for vulnerable groups, including marginalized populations and waste-pickers in urban areas. UNDP will contribute to the promotion of shock-responsive social protection systems by enhancing access to government schemes and entitlements. In less extent, le project contributes to Outcome 3: Climate-smart solutions, sustainable ecosystems, and resilient development for reduced vulnerability. In line with circular economy principles, UNDP will support reform initiatives that foster a clean and sustainable urban environment. This includes contributing to the Swachh Bharat Mission, working towards phasing out single-use plastics and integrating inclusive green economy principles into the operations of local urban bodies. The programme will also focus on environmentally sound plastic waste management and explore innovative models to tackle plastic pollution, collaborating with local urban bodies and waste pickers. Under this, the project contributes to Output 3.2: Innovative solutions developed, demonstrated and upscaled at national and subnational levels for vulnerable communities and businesses to benefit from sustainable management of natural resources (land, water, air), chemicals and circular economy.

5. **Indonesia:** The project contributes to the CPD outcome 3: Institutions, communities and people actively apply and implement low carbon development, sustainable natural resources management, and disaster resilience approaches that are all gender sensitive. Under Output 3.2, the project will strengthen the capacities of institutions and communities to support an inclusive and equitable transition to a low-carbon society and circular economy, particularly by enhancing community-based waste management systems and integrating waste workers into sustainable plastic value chains.

6. **Maldives:** The project contributes to the CPD Outcome 2/Output 2.3 (Policies, regulatory frameworks and capacities at national/subnational levels strengthened for sustainable management of water and waste resources) and UNSDCF Outcome 3 (By 2026 National and subnational institutions and communities in Maldives, particularly at risk populations, are better able to manage natural resources and achieve enhanced resilience to climate change,

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

disaster impacts, natural and human-induced hazards, and environmental degradation, inclusively and in a sustainable manner).

7. **Nepal:** The project contributes to the CPD Outcome 1/Output 1.2: Expanded access to sustainable livelihoods and income for women, youth, poor and other marginalized groups. In addition, this project directly contributes to CPD indicator 1.2.4: Innovative enterprises promoted and sustained to foster green and circular development and reduced environmental pollution.

8. **Philippines:** The Project contributes to the UNSDCF, particularly on *Outcome 3: By 2028, all people benefit from just transition to low-carbon, climate-resilient development, sustainable management of environment, natural resources and biodiversity and strengthened resilience to disasters and natural hazards.* Under Output 3.2, the project will focus on strengthening the capacities of institutions and communities to facilitate an inclusive and equitable transition towards a low-carbon society and circular economy. Additionally, the Project aligns with the current CPD (2024-2028) of the CO by supporting Outcome 3.1, particularly in developing and promoting relevant policies, strategies, and local actions to support the NDC implementation. This will be achieved by enhancing the capacities to implement circular economy and sustainable urban development approaches.

9. **Sri Lanka:** The project contributes to UNSDCF Outcome 3/UNDP Outcome 2 by introducing and promoting efficient plastic waste management that will in turn contribute to enhancing community resilience to disaster risks caused by climate change. The project interventions will reduce plastic pollution and mitigates aggravation of disaster impacts (i.e., intensified floods in urban areas due to clogging of drainage systems), as well as reducing threats to environment such as biodiversity, especially fauna, contamination of environment with microplastics etc. By developing and implementing gender-sensitive, pro-poor strategies for plastic waste management, the project ensures that vulnerable communities benefit from strengthened livelihoods and increased incomes. The dissemination of lessons learned and best practices across all local authorities in Sri Lanka further supports sustainable natural resource management and biodiversity conservation. By sharing innovative practices, the project aligns with CPD Output 2.1 and 2.3, contributing to local level green growth while addressing the environmental, social, and economic dimensions of plastic waste management.

10. **Vietnam :** The project contributes to CPD Outcome 2 “Climate Change, disaster resilience and environmental sustainability”, aiming to help people in Viet Nam, especially those at risk of being left behind, will benefit from, and contribute to safer and cleaner environment resulting from effective mitigation and adaptation to climate change, disaster risk reduction and resilience building, promotion of circular economy, clean and renewable energy, and the sustainable management of natural resources. In specific, project activities are aligned with Output 2.1 “Policies and solutions designed and implemented for transformation to low-carbon development, circular economy and environmental protection.

Indicative Output(s) with gender marker[1]: GEN2

Agreed by (signatures)[2]:

[1] The Gender Marker measures how much a project invests in gender equality and women’s empowerment. Select one for each output: GEN3 (Gender equality as a principle objective); GEN2 (Gender equality as a significant objective); GEN1 (Limited contribution to gender equality); GEN0 (No contribution to gender quality). All COs are required to highlight gender requirement in their child projects set up with the guidance of CO gender focal point in each respective country during inception/implementation.

[2] Note: This document, including the signature page, may be customized as needed. Separate signature pages (one per

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

UNDP RBAP
DocuSigned by: Gerd Trogemann 82665CD7435A41B... Mr. Gerd Trogemann Manager, Regional Programme and Global Policy Network
Date: 03-Sep-2025

UNDP Bangladesh
DocuSigned by: AEE468B55716409... Mr. Stefan Liller Resident Representative
Date: 03-Sep-2025

UNDP Bhutan
DocuSigned by: Mohammad Younus 3DB0A60DCAF64AE... Mr. Mohammad Younus Resident Representative
Date: 03-Sep-2025

UNDP Cambodia
DocuSigned by: 5341BE539BD1458... Mr. Enrico Gaveglia Resident Representative
Date: 03-Sep-2025

UNDP India
DocuSigned by: Angela Lusigi 44F84A6E2B524A4... Ms. Angela Lusigi Resident Representative
Date: 03-Sep-2025

UNDP Indonesia
Signed by: 167D6562D44041D... Ms. Sara Ferrer Olivella Resident Representative
Date: 03-Sep-2025

UNDP Maldives

country) can be created and signed if needed to facilitate timely approval and budget revision if multiple countries are participating. Separate signature pages should still reflect all participating partners.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

DocuSigned by:
7A11E308E3FE4ED...
Mr. Adnan Cheema
Resident Representative

Date: 04-Sep-2025

UNDP Nepal

DocuSigned by:
8E504963B44A45A...
Ms. Kyoko Yokosuka
Resident Representative

Date: 03-Sep-2025

UNDP Philippines

DocuSigned by:
00A711Z9A59543C...
Mr. Selva Ramachandran
Resident Representative

Date: 03-Sep-2025

UNDP Sri Lanka

DocuSigned by:
169FE630BB0640B...
Ms. Azusa Kubota
Resident Representative

Date: 07-Sep-2025

UNDP Viet Nam

DocuSigned by:
F91282F9F586428...
Ms. Ramla Khalidi
Resident Representative

Date: 03-Sep-2025

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Table of Contents


I. Development Challenge 10
II. Strategy 11
III. Results and Partnerships 13
IV. Project Management 20
V. Results Framework 33
VI. Monitoring And Evaluation 66
VII. Multi-Year Work Plan By Partner Country 69
VIII. Governance and Management Arrangements 109
IX. Legal Context 112
X. Risk Management 112
XI. ANNEXES (separately) 115

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

I. DEVELOPMENT CHALLENGE

Improving waste management in Asia and the Pacific islands is among the most urgent environmental issues. According to the World Bank (2020), waste generated in the Asia and Pacific region is projected to increase from about 802 million tonnes (2016) to 1.1 trillion tonnes in 2030. This trend is driven by consumerism in Asia with the growing population. Urbanization, rapidly developing economies, and increasing spending capacities have led to a desire for improved quality of life in Asia (Asia's population is equivalent to 59.78 percent of the total world population, while the urban population is 48.1 percent, equivalent to over 2 billion people (2016)). This has led to higher material consumption of lifestyle products, food and beverages, electronics, and etc. Increasing access to the internet, e-commerce, and smartphone applications has also resulted in a boom to consumption patterns in Asia and elsewhere (UNEP, 2021).

Figure 1 – Municipal Solid Waste generated per capita, per day, in selected capitals.

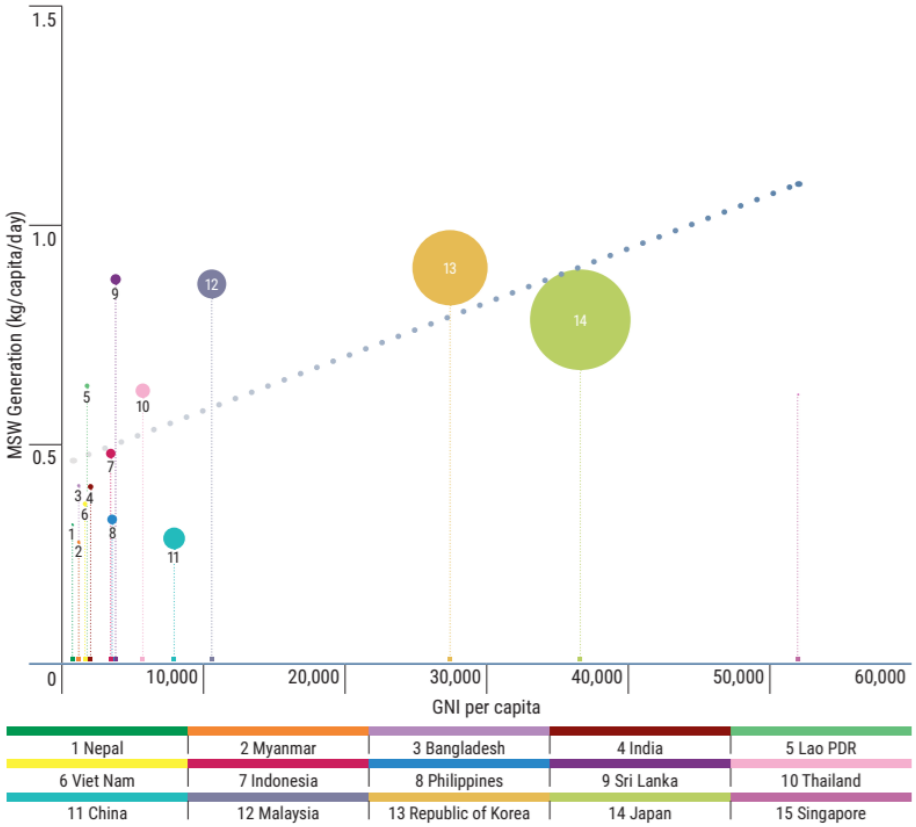

Source: UNEP, 2021.

Waste characteristics and volume are highly dependent on the socioeconomics of a country. However, within the Municipal Solid Waste (MSW) management structure, it is common that the organic (wet) waste varies between 50-70% of the total MSW generated, which requires specific actions to ensure that organic waste is properly sorted at source and disposed of properly.

The inorganic waste fraction in MSW is generally correlated with the Gross National Product index. The majority of high-income countries in Asia produce a higher percentage of inorganic waste compared to organic waste. In this specific case, it is noted that the quantity of plastics generated within the share of the total MSW is around 10-15%.

Although plastic waste is not the largest share of waste stream generated in Asia-Pacific countries, it has become a growing concern considering that these are non-degradable synthetic products, thus their negative environmental and human health-related impacts persist over generations and can be transboundary. Plastic pollution chokes wildlife contaminates soil and groundwater, and can cause serious health impacts. Humans are exposed to toxic chemicals and microplastics through

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

inhalation, ingestion, and direct skin contact, all along the plastic lifecycle, while microplastics can harm our health, and act as vessels for pathogens to enter our system, increasing the spread of diseases (IPEN 2016).

A large portion of plastic waste is either littered or inadequately disposed of. Of all plastics produced since 1950, nearly 80% ended up leaking in the environment or in landfills. In 2020, the world produced 367 million metric tons of plastic waste. Out of this, only 9% was recycled while almost 50% was landfilled, 19% incinerated, and 22% was discarded in uncontrolled sites or in the environment (land, lake, rivers and oceans, dumped in open sites or openly burned, generating emissions of greenhouse gases and hazardous chemicals substances) (OECD, 2022).

Women in the waste management sector, particularly in informal roles, face profound challenges. They are often overrepresented in lower-paying, unsafe informal jobs, frequently lacking access to social protections and safety measures. Promoting gender equality not only empowers women but also drives more inclusive economic growth, improves livelihoods, and strengthens social outcomes. By providing women with access to training, resources, and leadership opportunities in sectors like waste management, it would enhance their economic participation while increasing the overall effectiveness of sustainability initiatives. Incorporating gender equality into new generation of circular economy models for plastics waste management, ensures that everyone can contribute to and benefit from environmental solutions, fostering more equitable and resilient communities.

Strong outreach and awareness campaigns raised over the recent years have shed light over the issue. It is becoming more evident that, with no changes in the way we produce, consume, and dispose of plastics, some 33 billion tons of plastic are expected to accumulate on the planet by 2050. However, the management of the plastics waste cannot be cost-effective if not treated under a larger scope of MSW management. Given the above, approaching plastics waste management should be done within a well-structured and effective solid waste management framework.

II. STRATEGY

The Asia-Pacific region faces significant challenges in managing plastic waste due to rapid urbanization, increased consumption, and inadequate waste management infrastructure and regulations.

The accumulation of plastic waste has severe environmental and health impacts, leading to widespread pollution of land, water, and air. The informal sector, that plays a critical role in waste collection and recycling, is hindered by a lack of coordination, investment, and governance. This undermines the effective implementation of circular economy models, worsening the plastic waste crisis with tremendous social effects.

By 2030, the project funded by the Coca Cola Foundation (TCCF) aims to establish a sustainable, gender-responsive circular economy for plastics in the region, significantly reducing plastic waste leakage into the environment. The vision includes enhancing the livelihoods of waste workers, particularly vulnerable groups and women, and strengthening regional cooperation to promote shared prosperity. Achieving this requires the establishment of a robust waste management framework and infrastructure and the formal integration of the informal sector.

The pathway to change begins with creating an enabling environment and promoting policy advocacy. The project will strengthen national policies and regulatory frameworks to support the adoption of circular economy principles and infrastructure development. This will involve engaging policymakers to implement inclusive policies that incorporate Best Environmental Practices (BEP) and Best Available Technologies (BAT) into national strategies. Additionally, regional dialogues will be facilitated to harmonize policy frameworks and promote regulatory improvements. Capacity-building initiatives will be conducted for government officials and stakeholders, focusing on planning and financing waste management infrastructure.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

The second step is to develop and upgrade waste management infrastructure to support the efficient collection, processing, and recycling of plastic waste. This involves modernizing Material Recovery Facilities (MRFs) and Plastic Processing Units (PPUs) to handle larger waste volumes and improve operational efficiency. Investment in infrastructure for waste sorting, collection, and recycling will also be prioritized, with a focus on integrating informal sector workers into formal systems. Technical and financial support will be provided to national and local governments for infrastructure planning, design, and implementation, ensuring alignment with best practices and local needs.

Improving the livelihoods of waste workers, particularly women and marginalized groups, is a key objective. This will be achieved by enhancing working conditions, economic opportunities, and access to upgraded infrastructure. The project will promote the formation of women-led cooperatives in the waste management sector and provide targeted training on sustainable waste management practices. Facilitating access to markets for recycled products will ensure that local communities benefit economically from infrastructure development and improved waste management practices.

Regional cooperation and knowledge sharing are also vital for success. The project will establish a regional hub to coordinate activities across the nine participating countries, promoting collaboration and sharing best practices. Digital platforms will be utilized to facilitate continuous learning, collaboration, and the dissemination of lessons learned, particularly in infrastructure development. Successful interventions will be scaled up by sharing data, case studies, and methodologies that can be replicated in various contexts.

Three key assumptions underpin the success of the TTCF project. First, participating governments must prioritize and secure funding for waste management infrastructure and regulatory improvements. Second, local communities, including women and marginalized groups, must actively participate in and benefit from enhanced infrastructure and capacity-building initiatives. Finally, regional cooperation and knowledge sharing must drive the successful scaling of waste management and infrastructure interventions.

The project will receive multi-year partnership funding from TCCF, with specific allocations for infrastructure development. Technical expertise will be provided to support BEP and BAT for plastic waste management and infrastructure planning. Capacity building will focus on training waste workers, particularly women, in the safe and efficient use of new infrastructure for waste handling and recycling. Governments will receive assistance in developing and implementing plastic waste management policies, regulations, and infrastructure projects.

As a result, the TCCF project will enhance the capacities of national and local authorities, waste workers, and stakeholders to manage plastic waste using upgraded infrastructure. Operational guidelines will be developed and disseminated for the environmentally sound operation of MRFs and PPUs. Strengthened national policies and regulatory frameworks will align with international standards for plastic reduction and circular economy principles. Knowledge products, such as training materials, case studies, and toolkits, will support ongoing learning and infrastructure implementation.


The expected outcomes include engagement and strategy development, where stakeholders are involved, data is collected, and strategies are created to replicate successful waste management models. These models, incorporating BEP and BAT, will be replicated and scaled across countries alongside infrastructure enhancements. National capacities and infrastructure for plastic waste management will be improved in a gender-responsive manner. Public awareness and knowledge management systems will increase understanding and support continuous adaptation, sharing successes in infrastructure development.

In the long term, the TTCF project will significantly reduce plastic waste leakage into the environment, leading to cleaner and safer communities. It will create sustainable livelihoods for waste workers, promote gender equality by empowering women in the waste management sector, and accelerate the transition to a circular economy. The development of robust waste management

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

infrastructure will play a crucial role in achieving these goals, contributing to both regional and global sustainability objectives.

Figure 2: Theory of Change

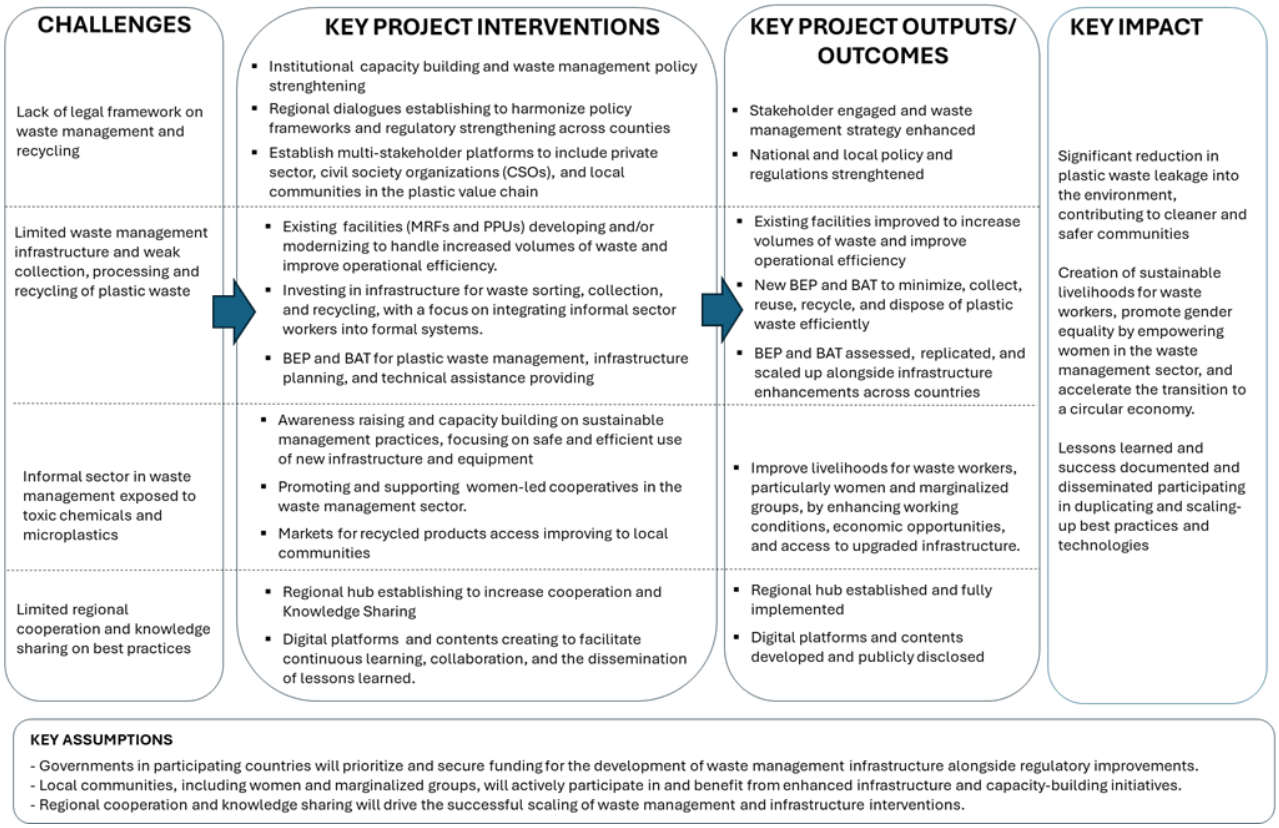

III. RESULTS AND PARTNERSHIPS

Expected Results

The TCCF-UNDP project is designed to address plastic waste management and advance circular economy initiatives across nine countries in South and Southeast Asia and the Pacific. Aligned with the theory of change, the project aims to create sustainable plastic waste systems, improve livelihoods, and reduce environmental impact. The core interventions and expected results include:

Stakeholder Engagement and Strategy Development (Outcome 1): The project will create multi-stakeholder platforms, involving the private sector, civil society organizations (CSOs), and local communities in the plastic value chain. This approach integrates gender-sensitive actions, such as supporting women-led cooperatives and engaging indigenous communities. Local roadmaps will be developed to guide plastic waste management activities, supported by data systems that track plastic generation and recycling. By engaging stakeholders and developing these roadmaps, the project ensures its interventions are sustainable and context-specific, enabling successful models to be replicated and scaled, fostering an environment conducive to circular economy practices.

Best Environmental Practices (BEP) and Best Available Technologies (BAT) Replication and Scaling (Outcome 2): The project will deploy BEP and BAT to minimize, collect, reuse, recycle, and dispose of plastic waste efficiently. This includes establishing or strengthening Material Recovery Facilities (MRFs) and Plastic Processing Units (PPUs). Gender-sensitive capacity building will also be provided to waste collectors, focusing on safe plastic handling and improved technical practices. Implementing BEP and BAT ensures that waste management systems are both environmentally sound and efficient, leading to increased recycling rates and reduced environmental contamination.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

These actions contribute to reducing plastic leakage and improving waste management as outlined in the theory of change.

Strengthening National and Infrastructure Capacities (Outcome 3): The project will provide policy and regulatory support by assisting in the creation or review of policies, guidelines, and national standards for plastic production and recycling. It will also aid in the development of Extended Producer Responsibility (EPR) systems and other frameworks. A key aspect of this outcome is the integration of informal waste collectors into formal recycling systems, ensuring their inclusion in and contribution to the circular economy. Strengthening national capacities and regulatory frameworks ensures that interventions are institutionalized and legally supported, making them scalable and sustainable. Integrating the informal sector promotes social inclusion, broadening the project's reach and impact.

Information Outreach and Knowledge Management (Outcome 4): The project will develop and disseminate knowledge products, training materials, and awareness campaigns aimed at a wide range of stakeholders, including the general public, with an emphasis on promoting behavioural change in plastic waste management. Regional workshops and conferences will also be organized to share best practices and lessons learned, facilitating cross-country collaboration and learning. Effective communication and knowledge exchange are crucial for scaling successful practices and ensuring informed, engaged stakeholders. This supports the theory of change by promoting sustainability and responsible waste management culture.

Resources Required to Achieve the Expected Results

Several key resources are required to achieve expected results:

UNDP teams: Contributions from country offices, the Bangkok Regional Hub, and HQ (as needed) are essential for project coordination, technical support, quality assurance, and communication. This includes roles for monitoring, evaluation, and knowledge dissemination.

Local and International consultants: technical experts for specific tasks such as capacity building, waste management infrastructure development, and policy formulation. Indeed, experts are required for implementing Best Available Technology (BAT) and Best Environmental Practices (BEP), as well as for conducting gender-sensitive training.

Waste Workers: formal and informal waste handlers, especially women and marginalized groups, need training and support for safe handling, segregation, and recycling processes.

Waste Management Infrastructure and equipment: Investments include the purchase of specific equipment such as compactor trucks, shredders, material recovery facilities (MRFs), and plastic processing units. To some extent, provision of personal protective equipment (PPE) for waste workers, as well as other tools needed to enhance their working conditions.

Technology for Waste Management: Digital platforms for tracking plastic waste, mobile applications for waste workers, and Geographic Information System (GIS) tools for mapping waste collection points are necessary. This includes licensing, server maintenance, and regular updates.

Communication Materials: Production of advocacy and public outreach materials to raise awareness about plastic pollution, promote behavioural change, and encourage recycling.

Partnerships

The project will collaborate with various partners to achieve its objectives. These partnerships are aimed at fostering systemic changes through policy reforms, infrastructure development, capacity building, and inclusive engagement. The project will work with national and local governments, the private sector, civil society organizations (CSOs), multinational donors, and academia, ensuring that each plays a crucial role in advancing the circular economy and reducing plastic waste.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

The national and local governments will be responsible for creating an enabling environment by developing policies, regulatory frameworks, and investing in waste management infrastructure. By integrating circular economy principles into policies at both national and local levels, governments will help ensure the project's long-term scalability and sustainability. The project assumes that governments will prioritize waste management, allocate resources, and provide the necessary policy support to strengthen plastic waste management systems.

The private sector will play a critical role in reducing plastic pollution by adopting sustainable production practices and supporting innovations in recycling and plastic alternatives. Through public-private partnerships, the private sector will contribute to infrastructure development, Extended Producer Responsibility schemes, and pilot projects for new recycling technologies. The project assumes that private companies will see the economic value in embracing circular economy principles and will actively collaborate by reducing plastic usage, investing in recycling systems, and supporting innovative solutions.

The CSOs and non-governmental organizations (NGOs) will play a critical role in engaging communities, raising awareness, and advocating for behavioural change. They will work closely with informal waste workers and promote gender-sensitive approaches, particularly empowering women, youth, and marginalized communities. It is assumed that CSOs will be effective in mobilizing communities and informal workers, helping to integrate these groups into the formal waste management system.

The TCCF will provide essential financial support for the implementation of the project, especially in areas like waste infrastructure, training, and innovation. It will also support advocacy efforts aimed at policy improvements across the participating countries. The project assumes continued donor engagement and long-term financial commitments that allow comprehensive project implementation.

The academic and research institutions will contribute by generating knowledge, conducting baseline studies, and driving technological innovations, particularly in developing and testing new waste processing and recycling technologies. The project assumes that effective collaboration with academic institutions will result in cutting-edge research and data that inform decision-making and foster innovation in plastic waste management.

In addition to these partnerships, the project will align with relevant initiatives such as National Plastics Action Plans (NPAPs) and regional efforts on circular economy practices, which support policy advocacy and institutional strengthening, key pathways for long-term impact. National frameworks like Vietnam’s National Plastic Action Partnership, for example, align with the project's goal of creating an enabling environment for circular economies. Similarly, other regional initiatives funded by international donors that promote circular economy practices across Southeast Asia and the Pacific will complement the project's objectives, fostering collaboration and reinforcing the shift towards sustainable plastic waste management.

Risks and Assumptions

The success of the TCCF project depends on several critical factors, but various risks could threaten the achievement of its intended results. These risks need to be managed through targeted mitigation strategies.

One major risk is the lack of prioritization by governments or delays in implementing policy reforms and providing regulatory support, such as Extended Producer Responsibility (EPR) frameworks. This could slow project implementation and prevent scaling up. The project assumes that national and local governments will prioritize waste management and provide necessary resources and policy backing. To mitigate this risk, the project will maintain ongoing policy dialogues with government stakeholders, foster strong partnerships, and ensure that government officials receive capacity-building support.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Engaging local governments early will promote ownership and accountability, further ensuring that this risk is addressed.

Another key risk is limited private sector engagement. Indeed, if private sector is not interested in adopting circular economy practice (such as recycling innovations or reducing plastic production), infrastructure development and innovation efforts could be hampered. While the project assumes that private sector entities will recognize the economic and reputational benefits of circular economy practices; the project must highlight economic incentives and market opportunities related to adopting sustainable practices to mitigate risk. Public-private partnerships (PPPs) will help share risks and costs, while showcasing successful business models will encourage further engagement.

The limited level of community participation can also pose a risk. If communities, and particularly informal waste workers communities, are resistant to behaviour change or unwilling to integrate into formal systems, the project's impact could be limited. It has been assumed that communities, including vulnerable and marginalized groups will actively engage in waste management initiatives. The project should work closely with civil society organizations (CSOs) and non-governmental organizations (NGOs) to promote inclusive participation and raise awareness as mitigation action. Indeed, engaging community leaders and introducing incentive programs will further encourage active participation.

Financial sustainability is another potential risk. Indeed, short funding and delayed support from donors or governments could affect project implementation and intervention. The project assumes that donors, particularly TCCF will provide sustained financial support throughout the project. The project will secure multi-year funding commitments and explore additional funding sources (including private sector contributions and international financial institutions to mitigate financial support risk. Budget flexibility will also be maintained to account for possible funding delays.

The technical and infrastructure challenges could also threaten the project's achievement. Delays in setting up or operating MRFs, plastic processing plants, or other waste management infrastructure could limit the project's capacity to strengthen waste collection and recycling. It has been assumed that the technical expertise and resources required for infrastructure development will be available and deployed effectively. The project will provide technical assistance, conduct early site assessments, and engage local governments to address potential technical issues and so, mitigate this risk. In addition, the collaboration with private sector partners will ensure sustainable equipment provision and maintenance.

The project also faces risks related to social and environmental impacts. Improper waste management practices could expose workers to health risks, pollute ecosystems, or displace informal waste workers. However, appropriate safety and environmental safeguards will be deployed and put in place. In addition, environmental and social impact assessments (ESIAs) will be conducted to identify potential issues, and measures such as providing personal protective equipment (PPE) to workers and implementing safety guidelines will be taken to address and mitigate ES risks. These risks and mitigation measures are delayed in the SESP annex.

Lastly, climate change and natural disasters pose a significant risk to the project. Events like floods or storms could disrupt waste management systems, damage infrastructure, or increase plastic leakage into the environment. It is assumed that operations will proceed without major disruptions from natural disasters. Nonetheless, climate-resilient infrastructure designs will be incorporated, and waste management systems will be built with flexibility to withstand such events. Additionally, partnerships with disaster management agencies would ensure rapid response in the event of natural disasters.

Stakeholder Engagement

The TCCF project targets a range of groups as its intended beneficiaries, each playing a crucial role in achieving the project's goals of reducing plastic waste, improving livelihoods, and promoting a

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

circular economy. The strategy to identify and engage these groups is designed to ensure inclusivity, effectiveness, and sustainability of the project's interventions.

Waste Workers (formal and informal sectors): These include individuals involved in the collection, sorting, and recycling of plastic waste, both in formal settings (employed by municipalities or waste management companies) and the informal sector (independent waste pickers, small-scale recyclers). Waste workers are at the forefront of the plastic waste management chain and are directly affected by inefficiencies in the system. Improving their working conditions, safety, and income opportunities is crucial for the success of the project.
The project will map existing waste workers, particularly those in the informal sector, to identify gaps in coverage, safety, and earnings. It will engage these workers through local associations, cooperatives, and community-based organizations. Training programs, provision of PPE, and integration into formal waste management systems will be key strategies.

Women and Vulnerable population: This group includes women, people with disabilities, and other vulnerable populations who are often underrepresented in formal employment and decision-making processes. Women and vulnerable groups are disproportionately affected by the negative impacts of plastic pollution and are often excluded from the benefits of formal economic activities. Empowering them is essential for achieving gender equality and social inclusion. The project will specifically promote the formation of women-led cooperatives and provide targeted support to marginalized groups through tailored training, access to resources, and economic opportunities. Partnerships with local NGOs and community leaders will help identify and reach these groups effectively.

Local Communities: The residents of urban and rural areas in the nine participating countries who are directly impacted by plastic waste pollution. Local communities are direct contributors to and victims of plastic waste pollution. Engaging them is critical for changing consumption patterns, improving waste sorting at the source, and fostering community-driven waste management solutions. The project will use community advocator, local leaders, and digital platforms to conduct awareness campaigns, organize community clean-up drives, and promote behavioural change initiatives. Educational workshops and incentive schemes for recycling will be implemented to encourage active participation.

Small and Medium Enterprises (SMEs) and Cooperatives in the Recycling Sector: SMEs, cooperatives, and social enterprises involved in the recycling, processing, and sale of recycled plastics. Indeed, these enterprises play a critical role in the circular economy by creating value from recycled materials. Supporting them can lead to more sustainable business models and job creation. The project will engage SMEs and cooperatives through industry associations, providing technical assistance, access to finance, and market linkages. Business development support, including digital tools for market access and product development, will be key components.

Government Officials and Policy Makers: National and local government officials responsible for waste management, environmental protection, and policy formulation. Governments are responsible for developing the enabling environment through policies, regulations, and infrastructure investments. Engaging them is essential for ensuring long-term sustainability and scalability of project interventions. The project will conduct capacity-building workshops, policy dialogues, and provide technical support to government officials. Regular consultations and involvement in project planning and implementation will ensure that government priorities are aligned with the project's goals.

Private Sector

Private actors involved in plastic production, waste management, and recycling. The private sector has significant influence over plastic production and waste management practices. Their participation is critical for adopting sustainable practices and scaling up circular economy models. The project will engage private sector entities through public-private partnerships (PPPs),

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

encouraging them to invest in infrastructure and adopt Extended Producer Responsibility (EPR) frameworks. Collaboration on pilot projects and innovations in recycling will be pursued.

DIRECT BENEFICIARIES

The estimated number of direct beneficiaries by targeted countries in the project is as follows:

Table 1: Sex-disaggregated Number of Beneficiaries by Countries[3]

Country	Total	Male	Female
Bangladesh	2,000	1400	600
Bhutan	600	300	300
Cambodia	450	200	250
India	60,000	30,000	30,000
Indonesia	65,000	26,000	39,000
Maldives	800	540	260
Nepal	1,550	950	600
Philippines	750	375	375
Sri Lanka	1,200	600	600
Viet Nam	3,250	2,500	750
Total	**135,600** ~~**70,600**~~	**62,865** ~~**36,865**~~	**72,735** ~~**33,735**~~

South-South and Triangular Cooperation

This project will enable South-South and Triangular Cooperation not only among the nine countries through capturing of good lessons but also beyond, through regional technical assistance in developing regional work plans/briefs/policy papers/ and organization of webinars and/or South-South Exchange Dialogues for a global audience, to serve as a platform for broader resource mobilization. Some COs have already developed technical guidance notes that will be shared throughout project implementation. In addition, the results of this project will contribute to sharing knowledge, skills and expertise across and beyond the nine countries.

As the proposed project covers nine countries, there is a need for a regional coordination mechanism for better coordination and articulation, as well as to promote effective communication and exchange of experiences between countries. The Regional Project Management team will be responsible for consolidated implementation support services and will be the main liaison with the TCCF team. The regional project management team will allow for greater sharing of experiences and good practices among programme countries and is best managed at regional level, with potential for replication in other countries in the region and sub-region and possibly beyond the project scope to other regions. The impact and visibility could be broader if managed regionally, taking advantage of UNDP organizational structure and presence in other regions.

This project will enable South-South and Triangular Cooperation not only between the nine countries through capturing of good lessons, but also beyond, through regional technical assistance in developing regional work plan/briefs/policy papers/ and organization of webinars for a global audience, to serve as a platform for wider resource mobilization, and across similar projects at the Hub.

[3] India needs to address gaps for no. of male beneficiaries from 5,000 to 30,000 and no. of female beneficiaries from 5,000 to 30,000;

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Digital Solutions[4]

The project will use various digital technologies and solutions to improve the target beneficiaries and partners' experiences as well as address some of key development challenges identified.

Waste Tracking and Management Systems: The project will develop and deploy mobile applications that allow waste workers, particularly those in the informal sector, to log and track the collection, sorting, and processing of plastic waste in real time. These apps will provide data on waste quantities, types, and locations, enabling more efficient collection routes, reducing operational costs, and increasing transparency across the waste management chain.

The Geographic Information System (GIS) technology will be used to map existing waste management facilities, collection points, and areas with high plastic waste generation. This mapping will help local governments and waste management companies optimize resource allocation, plan new infrastructure developments, and identify areas where interventions are most needed.

Digital Platforms for Knowledge Sharing and Capacity Building: The project will create e-learning platforms that offer courses on BEP and BAT for waste management. These modules will be accessible to waste workers, local government officials, and community members, allowing them to learn at their own pace. This approach not only democratizes access to knowledge but also ensures that training can be scaled across different regions.

To facilitate ongoing learning and collaboration, the project will host regular webinars and virtual workshops. These sessions will bring together stakeholders from the nine participating countries, enabling the exchange of best practices, discussion of challenges, and co-creation of solutions. The use of digital communication tools helps overcome geographical barriers and promotes regional cooperation.

Finally, the project will establish a digital hub that connects stakeholders across the nine participating countries. This platform will facilitate collaboration on joint initiatives, share knowledge and resources, and coordinate regional actions. The hub will include features like virtual meeting rooms, document sharing, and collaborative project management tools.

Market Access and Economic Empowerment Tools: The data collected through digital waste tracking apps and GIS systems will be analysed to inform policy decisions and infrastructure planning. Local and national governments can use these insights to identify trends, measure the impact of interventions, and make evidence-based decisions. For example, data on waste flows can guide the placement of new MRFs or inform the development of EPR policies.

Knowledge

The project will produce a variety of specific knowledge products besides evaluations, aimed at capturing and sharing valuable insights and lessons learned from project implementation. Indeed, the project will generate reports, case studies, and strategic briefs that document best practices, project progress, and the impact of interventions. These publications will be disseminated to stakeholders, including government officials, civil society, and private sector partners, to promote sustainable plastic waste management practices.

A digital platform will be established for tracking plastic waste and documenting the progress of waste management efforts across participating countries. These platforms will store data on waste collection, processing, and recycling activities, offering a repository of information to guide future waste management initiatives.

In addition, the project will create communication materials, including advocacy videos, blogs, and social media campaigns, to raise awareness on the importance of proper plastic waste management

[4] *Please see the Guideline "Embedding Digital in Project Design".*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

and circular economy practices. Gender-sensitive awareness materials will target diverse audiences to ensure inclusivity in the messaging.
Some training materials and educational content will be produced to facilitate the capacity building of waste workers, policymakers, and local communities. This includes e-learning platforms and training modules on best environmental practices and technologies for plastic waste management.

Finally, a dedicated digital hub will be developed to facilitate regional collaboration and knowledge exchange among the nine participating countries. This hub will host webinars, workshops, and virtual meetings, enabling stakeholders to share insights, challenges, and solutions for waste management.

Sustainability and Scaling Up

The project will use relevant national systems by aligning with existing national policies and regulatory frameworks, such as National Plastics Action Plans (NPAPs), to integrate circular economy principles into national and local waste management strategies.
By leveraging established waste management systems, government agencies, and EPR frameworks, the project will ensure that infrastructure improvements and policy reforms are embedded into the national context, allowing for smooth implementation and scalability.

To sustain and scale-up results, the project will adopt transition arrangements, including institutionalizing BAT and BEP into the national regulatory systems. The project will also strengthen partnerships with the private sector to support ongoing innovation and infrastructure investments beyond the project duration.

Capacity-building efforts will focus on enhancing the technical expertise of government officials and waste management personnel, ensuring they are equipped to manage and scale waste management interventions effectively.

Indeed, national capacities will be strengthened through comprehensive training programs targeting informal sector, waste workers, government officials, and other stakeholders. This will involve gender-sensitive training on waste management practices, infrastructure operation, and policy implementation. National systems will be supported by establishing robust monitoring and evaluation frameworks to track progress and ensure that capacities are continuously enhanced and adapted.

Finally, national ownership will be ensured by closely engaging government agencies in the planning and implementation phases of the project. Local authorities and communities will be involved in decision-making processes, ensuring that the interventions align with national priorities and can be sustained by local systems. Regular consultations and stakeholder engagement will foster a sense of ownership, while capacity-building initiatives will empower national institutions to continue implementing and scaling the project's interventions post-completion.

IV. PROJECT MANAGEMENT

Cost Efficiency and Effectiveness

The strategy is expected to deliver maximum results with available resources by leveraging several key approaches that have proven effective in similar contexts.

First, the project has explored through a theory of change analysis and development, different pathways to achieve its objectives efficiently.

This analysis helps ensure that resources are targeted towards interventions that have the highest impact on reducing plastic waste and promoting circular economy principles. It involves identifying

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

the critical steps needed to address plastic waste, such as improving infrastructure, strengthening policy frameworks, and promoting gender-sensitive waste management practices. The theory of change allows the project to focus its resources on interventions that are most likely to lead to long-term, sustainable results, reducing plastic leakage and improving the livelihoods of waste workers, particularly vulnerable groups and women.

Second, the project will adopt a portfolio management approach to improve cost-effectiveness by coordinating activities with other initiatives in the region. By working in conjunction with national governments, civil society organizations, and private sector partners, the project maximizes synergies and avoids duplication of efforts. This coordination allows the project to build on existing infrastructure, policies, and resources, ensuring that interventions are aligned with national priorities and ongoing projects, such as the National Plastics Action Plans (NPAPs) and similar circular economy initiatives in Southeast Asia and the Pacific.

Third, the project will share resources and expertise with other waste management and circular economy projects, particularly in the areas of data collection, monitoring of outcomes, and procurement of waste management equipment. By pooling resources for joint operations, the project can reduce overhead costs and streamline operations, ensuring that more funds are directed towards impactful on-the-ground activities.

These approaches are informed by evidence from similar projects and good practices, particularly in the areas of infrastructure development, policy reform, and community engagement in waste management. For example, previous projects in South and Southeast Asia have demonstrated the importance of engaging informal waste workers and promoting inclusive policies to improve waste collection and recycling rates. By building on these lessons learned, the project can avoid common pitfalls and focus on proven strategies for success.

The selected pathway is the most efficient and effective option because it integrates a comprehensive, multi-stakeholder approach, combining policy advocacy, infrastructure development, and community-level engagement. This holistic strategy ensures that all key elements of the plastic waste management ecosystem are addressed simultaneously, leading to more sustainable and scalable results.

Project Management

Project Implementation

The project will be implemented following UNDP's Direct Implementation Modality (DIM). The Project will be implemented as multi-country project by ten UNDP COs in India, Bangladesh, Bhutan, Nepal, Maldives, Sri Lanka, Philippines, Cambodia, Vietnam, and Indonesia with overall coordination and technical management support from the regional project management unit based in Bangkok Regional Hub.

The COs have capable and professional teams with adequate experience in implementation and compliance with UNDP regulations and policies for Programme and Project Management (PPM). The COs are well structured to address the two complementary areas of project implementation and financial management as well as application of Rules and Regulations on Programme and Operations Policies. Each country will implement the project under the DIM modality, with dedicated project teams in each country. The regional project management unit, housed in BRH E&E team will provide technical, coordination and communications advisory services. The BRH partnership specialist will be providing dedicated support to coordinate with TCCF.

Project teams in country offices will work closely with operation support team, led by Operations Manager, who is supported by a Head of Finance, a Head of Human Resources and a Head of Procurement. The CO project teams also work closely with programme staff members in different thematic clusters, Partnerships team, Communications team, Innovation teams, Gender teams to seek additional support in cross-cutting areas of the project.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Oversight and assurance

BRH Regional Programme Management Unit provides support on oversight and assurance for regional activities and support the organization of a joint regional Project Board. Country offices' Programme Management Unit/Programme Officers/ M&E officers provide oversight and assurance for their respective country project. Oversight and assurance activities will ensure operational and financial management of the projects are in compliance with UNDP's procedures, rules and regulations.

The CO's HACT focal points oversees HACT compliance of project implementing and responsible partners (Executing Partners). On an annual basis, regular spot checks and project audits are conducted for all projects, in line with UNDP POPP and the Assurance Plan approved by the CO's Resident Representative. The COs are also bound to comply with UNDP´s PPM Policies and the UNDP´s Financial Regulation 16.02 and Financial Rule 116.02.

Implementation Modality in Country Offices

Bangladesh

The project will be implemented following the Direct Implementation Modality (DIM). UNDP Bangladesh CO will manage this initiative under the direct leadership of the UNDP RR and DRR. The project's technical implementation will be led by a Project Manager and supported by a project team consisting of national experts and staff. The Project Board at the Regional Level will recommend key aspects of the project's execution, including work plans and budget revisions, selection and agreements with Responsible Parties, external engagements, and messaging. The Project Board will convene on at least a biannual basis.

Funding and financing for scaleDepending on the output and impact of the interventions of this project, as well as context and requirements from the Government and interest of other Development Partners (International Finance Institutions (IFIs), bilaterals, private sector, etc), UNDP will mobilize resources for scaling and expanding through new programs/projects.

Potential partnerships, including Responsible Parties: The key stakeholders, partners and/or responsible parties of this project will include the Ministry of Environment, Forest and Climate Change (MoEFCC), Bangladesh Investment Development Authority (BIDA), Ministry of Local Government, Rural Development and Co-operatives (MoLGRDC), Federation of Bangladesh Chambers of Commerce & Industries (FBCCI) and any other institution deemed necessary during this project's lifecycle. For field-level activities, UNDP will engage NGOs/CBOs, academic/research institutions, Local Government Institutions (LGIs) and government departments through appropriate execution modalities.

Bhutan

Leadership

The senior management of UNDP Bhutan Country Office (CO) as a member of the Regional Project Board will provide overall guidance required for implementing this multi-country project. At the CO level, oversight will be provided by the Environment and Livelihood Program team lead with the project manager operating under the Environment cluster managing the project. Additional guidance will be provided by the National Technical Working Group, which include representatives from the Ministry of Infrastructure and Transport (MoIT), the Ministry of Finance, the Ministry of Energy and Natural Resources (MoENR), Paro district, Gelephu Municipality and UNDP.

Compliance

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

The implementation of the project will comply with the UNDP's Program and Operations Policy and Procedures (POPP), Financial Regulations, Programme and Project Management Quality Standards, and RPAC guidance/guidelines. The project will also comply with existing national waste policy and guidelines.

Implementation

The project will be implemented following Direct Implementation Modality (DIM). The UNDP Bhutan Country Office will lead the project with the Ministry of Infrastructure and Transport as the main Responsible Party for implementation. The representative from two project landscape (Paro and Gelephu) will be equally involved and consulted during the implementation. Project implementation assurance will be supported by RBM team and innovation team in the Country Office. UNDP Operations team will support the procurement, HR recruitment, administrative and logistics support.

Stakeholder Engagement

To ensure strong country ownership, stakeholder engagement at the activity level includes the following:

Output	***Stakeholder***
1. Awareness programs developed and deployed to support behaviour change in schools, colleges, hotels and monasteries	*1. Department of Environment and Climate Change, MoENR* *2. Department of Human Settlement, MoIT* *3. Paro District Administration* *4. Gelephu Municipality* *5. Private sectors (Clean Bhutan and Greener Way)* *6. Schools, colleges, business enterprise and monasteries.* *7. Local Government*
2. Increase plastic waste collection through deployment of best environmental practices and technologies such as compactor trucks, and value addition machines.	*1. Department of Human Settlement, MoIT* *2. Paro District Administration* *3. Gelephu Municipality*
3. Capacity of 600 waste handlers (formal and informal) developed in proper segregation and hygiene.	*1. Department of Human Settlement, MoIT* *2. Department of Environment and Climate Change (MoENR)* *3. National Statistics Bureau* *4. Local Government* *5. Informal/formal waste handlers*
4. Project communication, advocacy and knowledge management	*1. Department of Human Settlement, MoIT* *2. Paro District Administration* *3. Gelephu Municipality*

Reporting and communications

Reports on project activities and implementation progress shall be prepared in accordance with the existing reporting channels under DIM project implementation guided by the RBM team. The Country Office Communication team will support all visibility and Knowledge Management product development and dissemination.

Cambodia

Project Advisory Group

The Project Advisory Group (PAG) will be established under UNDP Cambodia at the start of the project implementation and will be led by the Project Management Specialist, who will manage the project and project team including the project officer and project assistant to implement the TCCF

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

plastic circularity project. The PAG will serve as the secretary to the TCCF plastic circularity project at the country office and will be accountable to the board to ensure the delivery and quality of activities and outputs and to draft annual budgets for approval.


Project Management

A Project Management Specialist will be responsible for the management of the project, managing all project inputs, supervising project staff, responsible parties, consultants, and sub-contractors as well as coordinating the procurement and in country coordination. The Project Management Specialist will present key deliverables and documents to the board for their review and approval, including progress reports, annual work plans, adjustments to tolerance levels, and risk registers.

Project implementation

A Project Officer will be responsible for the day-to-day implementation of the project activities, delivering all project inputs, coordinating with responsible parties, consultants, and sub-contractors as well as coordinating the procurement and in close consultation with the Project Management Specialist and other relevant units. The Project Officer will present key deliverable progress and achievements to the Project Management Specialist for their review and approval, including progress reports, annual work plans, and adjustments to the project activities in line with UNDP's rules and regulations.

A Project Assistant (Admin and Finance) will be responsible for ensuring effective and high-quality support on project administrative and financial management including but not limited to: 1) contributing to day-to-day support for the project implementation and ensuring conformity to expected results, outputs, objectives, and work plans, 2) ensure effective local purchases in line with UNDP procurement procedures, 3) ensure effective management of financial and administrative aspects of project assets and financial resources to meet satisfactory outcomes of the annual audit of the project, and 4) provide support in preparing quarterly and annual financial reports.

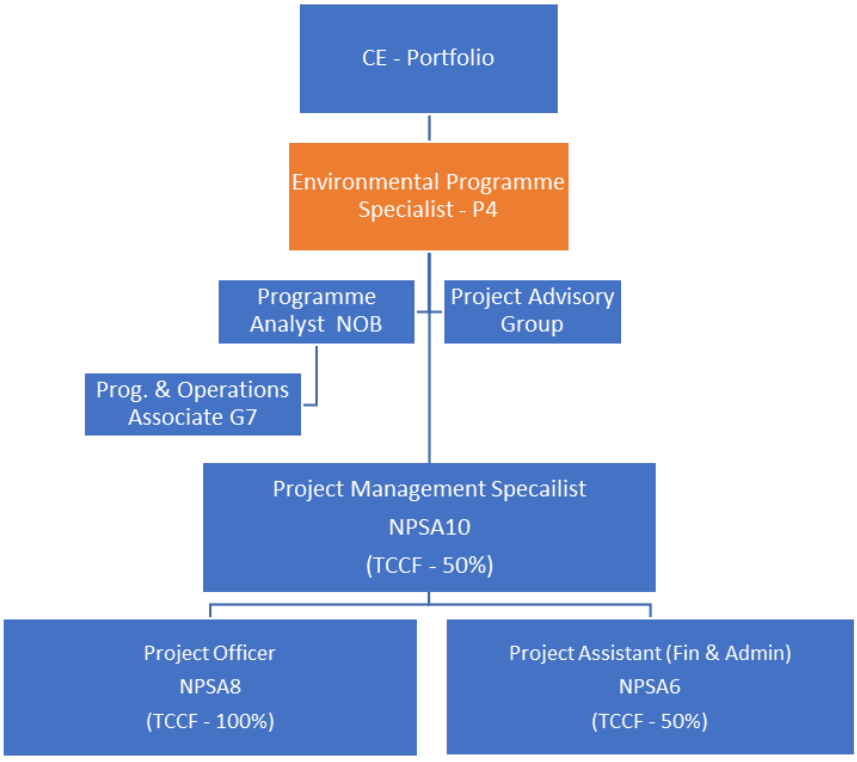

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

India

Project Management

Under the Direct Implementation Modality of UNDP, the programme will be executed with UNDP serving as the lead implementing entity, leveraging its expertise, systems, and resources to ensure effective delivery of the project's outcomes. UNDP will take full responsibility for project management, including the planning, coordination, and supervision of activities across multiple stakeholders.

Implementation

To achieve **Output 1** and **Output 2**, UNDP will work in close collaboration with central ministries such as Ministry of Housing and Urban Affairs (MoHUA), Ministry of Social Justice and Empowerment (MoSJE), local governments, and civil society organizations to address access barriers and facilitate the enrolment of waste workers in social protection schemes. This will include the establishment of service linkages, capacity building of relevant stakeholders, and awareness campaigns through both physical outreach and helpline services to enhance the visibility of rights and entitlements among 50,000 waste workers.

For **Output 3** and **Output 4**, UNDP will collaborate with private sector partners, recycling value chain actors, and relevant national institutions and ministries such as Ministry of Environment Forest and Climate Change (MoEFCC), Central Pollution Control Boards (CPCB), to develop standards, framework to streamline responsible plastic waste collection, sorting, and processing across the value chain. Moreover, UNDP will lead efforts in building national capacities and developing guidelines, working closely with government ministries and regulatory bodies to institutionalize best practices and strengthen policy frameworks.

Gender mainstreaming will be a key focus throughout the project, ensuring that the specific challenges faced by women waste workers are addressed. Given that women often encounter greater barriers to accessing social protection and economic opportunities, the project will adopt a gender-sensitive approach in its outreach, enrolment processes, and capacity-building efforts. Tailored interventions will ensure that women have equal access to social protection schemes, information on their rights, and opportunities within the plastic waste value chain. The project will also prioritize addressing issues like workplace safety and ensuring that women's voices and needs are central to the programme's implementation.

Monitoring and evaluation

Monitoring and evaluation mechanisms will be embedded throughout the project cycle to ensure adherence to environmental, social, and gender-sensitive standards, and continuous improvement based on lessons learned.

Indonesia

Project Management

The project will be implemented under the Direct Implementation Modality (DIM) by UNDP Indonesia, ensuring effective management and oversight. UNDP will execute the internal control framework and provide regular updates to the project board, including financial and other reports, in line with UNDP's reporting procedures and guidelines.

The project will also establish an accessible Grievance Redress Mechanism (GRM) to uphold accountability and transparency. Any individual or group who feels affected by the project may submit a grievance directly or through an authorized representative. Grievances can be filed through multiple channels, such as meetings, phone calls, SMS, email, or written submissions, with support from PB institutions, local government, and CSOs to ensure accessibility. Complaints may start with

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

minimal information, and the GRM will follow up as needed to clarify details. All cases will be documented and addressed at the project level, and, if necessary, escalated further to the relevant authority with the mandate to address them.

Implementation


To achieve Outputs 1 and 2, UNDP will work in close collaboration with local governments, community-based organizations (CBOs), academic institutions, and civil society organizations to strengthen the knowledge, skills, and occupational safety of waste workers across seven target locations. This will include the development and dissemination of educational materials, provision of personal protective equipment (PPE), and implementation of safety training using a train-the-trainer model. Waste workers will be empowered through capacity building on sustainable waste management practices and circular economy principles, supported by tailored handbooks, online modules, and localized training sessions. These efforts will ensure that over 65,000 waste workers, particularly women and those operating in informal settings are better equipped, safer, and more actively engaged in community waste systems.

For Outputs 3 and 4, UNDP will collaborate closely with community-based organizations (CBOs), private sector actors, financial institutions, and national and subnational government agencies such as the Ministry of Environment, Coordinating Ministry for Food Affairs, Poverty Reduction Agency, and the Ministry of Social Affairs to facilitate a just and inclusive transition toward a circular economy. This will be achieved by strengthening the technical and organizational capacity of waste workers and CBOs, piloting and scaling inclusive waste collection models, and developing blended finance mechanisms to ensure long-term sustainability. UNDP will also engage with platforms such as the TKN PSL Secretariat to promote regulatory reform, worker protections, and market access for recycled materials. The project will prioritize policy alignment, capacity development, and digital innovation to institutionalize best practices, promote ethical supply chains, and ensure waste workers are recognized and supported as key actors in Indonesia's plastic waste management system.

For Output 5, UNDP will lead the development of an integrated digital platform and robust knowledge management system to support real-time monitoring, data-driven decision-making, and public engagement in plastic waste management. Working closely with local authorities, private sector partners, and existing systems such as SIMBA and GRADASI, the platform will enhance data visibility and coordination among stakeholders. In parallel, UNDP will implement targeted awareness campaigns through social media, community forums, and educational workshops to increase participation in responsible waste practices and amplify the visibility of waste workers' contributions. These efforts aim to foster behavioural change, institutional learning, and inclusive innovation across the waste value chain.

To effectively deliver these activities, the project will adopt a organizational structure that ensures efficient coordination and accountability at both national and field levels. The structure is led by a Programme Manager and a National Project Manager, supported by two Project Coordinators who oversee technical and field implementation. Dedicated officers, including Communications, Monitoring and Evaluation, IT, and Waste Management, will provide specialized expertise, while Project Associates and Project Assistants will ensure smooth administration, procurement, and logistical support. Field Coordinators will be deployed in each project location to maintain close engagement with waste workers, local governments, and community-based organizations. This structure promotes strong linkages between national oversight and local implementation, ensuring that project activities are well-coordinated, inclusive, and responsive to community needs.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

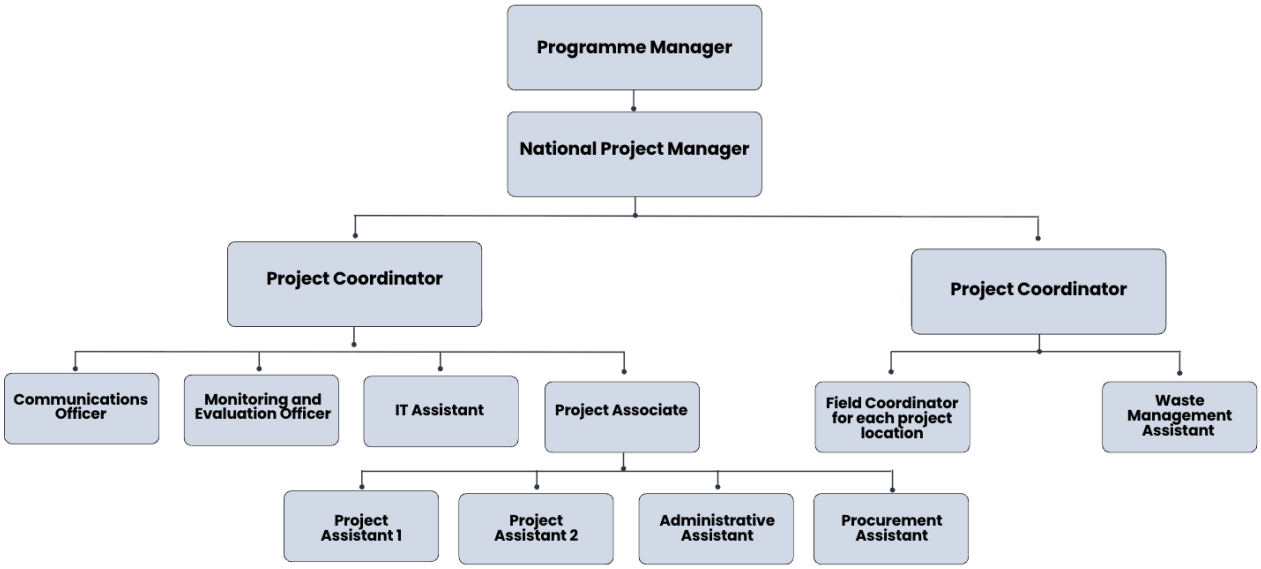

Monitoring and Evaluation

Monitoring and evaluation mechanisms will be embedded throughout the project cycle to ensure adherence to environmental, social, and gender-sensitive standards, and continuous improvement based on lessons learned.

Maldives

Under UNDP's Direct Implementation Modality (DIM), the programme will be led by UNDP, utilizing its expertise, systems, and resources to ensure the effective achievement of project outcomes. UNDP will assume full responsibility for project management, overseeing planning, coordination, and the supervision of activities among multiple stakeholders.
Implementation

For Outputs 1 and 2, UNDP will work closely with the Waste Department of the Ministry of Climate Change, Environment, and Energy (MCCEE) and the Waste Management Corporation (WAMCO). Additionally, the UNDP Country Office (CO) will collaborate with Local Councils in the target atolls and islands to ensure comprehensive data collection, enabling informed government decisions on waste management at both national and sub-national levels.

For Output 3, UNDP CO will partner with the Bangkok Regional Hub (BRH) and local authorities (MCCEE, WAMCO, and Local Councils) to draw on global best practices and expertise, creating locally tailored capacity-building tools and modules.

Gender Mainstreaming
A central focus of the project will be gender mainstreaming, addressing the unique challenges faced by women in waste management, particularly as primary household waste handlers. Advocacy and outreach efforts will be designed to engage this demographic. Furthermore, recognizing the potential for waste management to enhance women's livelihoods, the project will promote gender-sensitive workplace policies, outreach, and training programs to support women in the waste sector.

Monitoring and Evaluation
Monitoring and evaluation mechanisms will be integrated throughout the project cycle to ensure compliance with environmental, social, and gender-sensitive standards, with continuous improvement based on lessons learned.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Nepal

Project management

Under the Direct Implementation Modality of UNDP, the project will be implemented under the Green Economy portfolio following UNDP's portfolio approach. The Project board of the Green Economy Portfolio will function as the Project Advisor committee at country level for this project. The programme will be executed with UNDP serving as the lead implementing entity, leveraging its expertise, systems, and resources to ensure effective delivery of the project's outcomes. UNDP will take full responsibility for project management, including the planning, coordination, and supervision of activities across multiple stakeholders.

Implementation

UNDP will work in close collaboration with the Selected municipalities and private sector companies to establish and strengthen Material Recovery Facilities (MRFs). UNDP will partner with the private companies to introduce new technologies to increase the volume of the recovery of plastic waste and its best use for recycling and upcycling. Additionally, the support will also be provided to strengthen the institutional capacity of the selected MRFs including the development of business models and Standard Operating Procedures (SOPs). For the output 2, UNDP will work with qualified training institutions to deliver the trainings to the waste workers on occupational safety as well as on skill trainings for their livelihood opportunities. For the awareness campaigns, under the guidance of selected municipalities, UNDP will carry out awareness campaigns in targeted communities through the selected service providers.

To create enabling policy environment for the private sector and communities, UNDP will engage with selected municipalities for necessary policy and legal reforms as well as to improve the capacity of the officials. As necessary, UNDP will also engage with the federal ministries for policy advocacy.

Gender and social inclusion cuts across all outputs and activities. The strategies and activities related to outreach, skill development and awareness campaigns will be designed to tackle the barriers encounters by women and people from disadvantaged groups.

Monitoring and evaluation

Monitoring and evaluation mechanisms will be embedded throughout the project cycle to ensure adherence to environmental, social, and gender-sensitive standards, and continuous improvement based on lessons learned.

Philippines

The Philippines will be implementing the TCCF Plastics Circularity Project through the Direct Implementation Modality. The Direct Implementation (DIM) is the modality whereby UNDP takes on the role of Implementing Partner and has the technical and administrative capacity to assume the responsibility for mobilizing and applying effectively the required inputs in order to reach the expected outputs. Through DIM, the Country Office assumes overall management responsibility and accountability for project implementation while following all policies and procedures established for its own operations.

The Country Office will also explore the implementation of an Innovation Challenge and a Responsible Party Agreement (RPA) under the TCCF Plastics Circularity Project. The Innovation Challenge aims to organize and solicit innovative ideas and solutions to develop business models on waste diversion and collection that can be implemented in the communities under Output 1 (Inclusive, sector-specific business models successfully developed and integrated into the existing plastic waste diversion system, enhancing efficiency and sustainability in plastic waste management


Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

of the locality). Further, a Responsible Party Agreement may also be executed with a Non-Governmental Organization (NGO) to support in the implementation of Outputs 3 (Plastic recovery and recycling operations of at least two GEDSI/ informal waste picker groups organized and scaled up) and Output 5 (Digital application that enables waste diversion tracking with incentives or reward system deployed).

Sri Lanka

The project will be directly implemented by UNDP Sri Lanka country office in partnership with the Ministry of Provincial Councils and Local Government, Waste Management Authority of the Western Province and Local Authorities in the Colombo District under the Direct Implementation Modality (DIM) with the overall guidance and direction of the Resident Representative. A project management team led by the Programme & Policy Specialist and Team Leader, Climate & Environment, with the Programme Coordination Specialist for Energy & Waste (Also the Project Manager), will lead project interventions.

A National Advisory Committee will serve as the advisory body for the project at the national level, providing guidance and oversight. The National Advisory Committee will be established with the participation of relevant stakeholders. This Committee will be chaired by the Resident Representative of UNDP Sri Lanka and will include national partners, such as the donor (Coca-Cola's representative in Sri Lanka) and beneficiaries, including Ministry of Provincial Council and Local Government, Waste Management Authority of the Western Province and Local Authorities where the project interventions will be carried out.

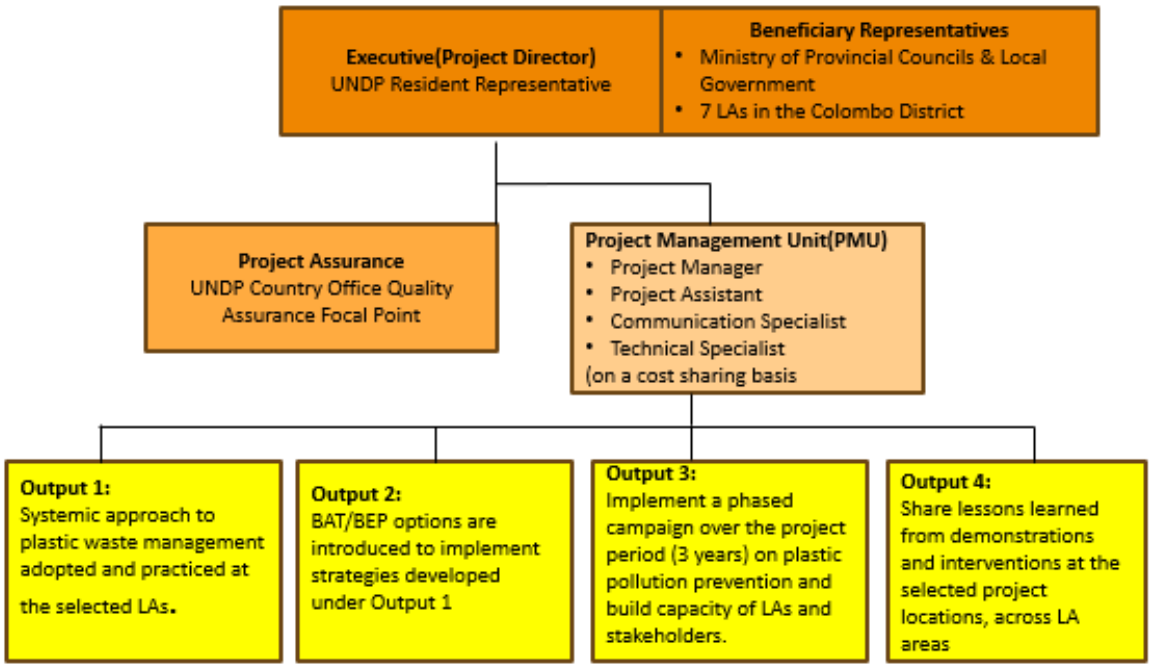

The implementation team will be comprised of existing staff of the Climate and Environment Team on a cost sharing basis as well as dedicated short-term consultants, to carry out specific tasks related to the outputs. The project will be operational in the Colombo District.

The Project Manager will oversee the implementation, whose primary responsibility is the timely delivery of project interventions in line with the approved work plan, budget management, and to ensure that results are achieved. The Technical Specialist will provide overall technical input for project implementation, including support for the development of ToRs, procurement, MRV. A

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Finance & Admin Associate, Project Associate and a Communications & Reporting Officer will be available, on a shared basis, to carry out financial monitoring and management as well as communications and visibility functions.

UNDP Country Office staff will provide operational support services to the project in the areas of finance, procurement, human resources, travel and logistics, results management, communication, advocacy, and other related support, and will be charged for their time directly attributable to the project.

The UNDP country office will perform oversight and quality assurance functions (independent of the implementation team), which will be led by the Programme Quality and Design Analyst for the Climate and Environment Team, and supported by the Results and Resources Management Team, and overseen by the UNDP Deputy Resident Representative.

The stakeholder engagement modality for the project adopts a collaborative and inclusive approach, involving key stakeholders including Local Authorities (LAs) from seven municipalities in the Colombo District, national government agencies such as Ministry of Provincial Councils and Local Government, Ministry of Environment and Central Environmental Authority (CEA), private sector companies involved in recycling and waste management, civil society organizations, and community groups. LAs will lead the on-ground implementation of waste management systems and oversee Material Recovery Facilities (MRFs), while the Ministry of Environment and CEA provide regulatory oversight. Private sector partners will contribute to technology and financial resources to enhance recycling operations, while civil society organizations drive community engagement and awareness campaigns. Informal waste collectors and recycling businesses will be integrated into the system, ensuring inclusive economic opportunities. Continuous feedback loops and consultations will ensure stakeholder concerns are addressed, ensuring long-term project sustainability.

UNDP employs a results-based management (RBM) approach, with the project having clearly defined and verifiable results that are aligned to the outcomes of the Country Programme Document, the UN Sustainable Development Cooperation Framework, and UNDP's Global Strategic Plan.

Vietnam

Project Management


This project will be directly implemented by UNDP Viet Nam, in partnership with the Ministry of Natural Resources and Environment (MONRE) and local authorities in several provinces of Viet Nam. It will benefit from strong in-house management, technical expertise, and skills for project oversight and financial management.

The Project Implementation Team at CO will be from the Climate Change and Environment Unit (CCEU). The National Advisory Committee, which will provide guidance and oversight, will be established with the participation of relevant stakeholders. This Committee will be chaired by the Deputy Representative of UNDP Viet Nam and will include national partners, such as the donor (Coca-Cola's representative in Viet Nam) and beneficiaries, including MONRE (International Cooperation Department) and local provinces where the project interventions will be piloted (tentatively Binh Thuan province).

The project is designed to engage multiple stakeholders in dialogues and collaborations to streamline and strengthen commitments on plastic pollution mitigation. This will cover various topics, such as single-use plastics, EPR schemes, and sustainable consumption, and will involve local innovators and start-ups through incubation and acceleration activities. Additionally, the project will engage the private sector, including brands and businesses, to pilot activities on harmonized plastic

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

responsible sourcing, waste recovery from fishing trips, and waste classification at source programs. Furthermore, the project seeks co-financing opportunities with existing plastic projects in Viet Nam to expand its impact and increase plastic waste collection and recycling.The Project Team will be structured as shown below.

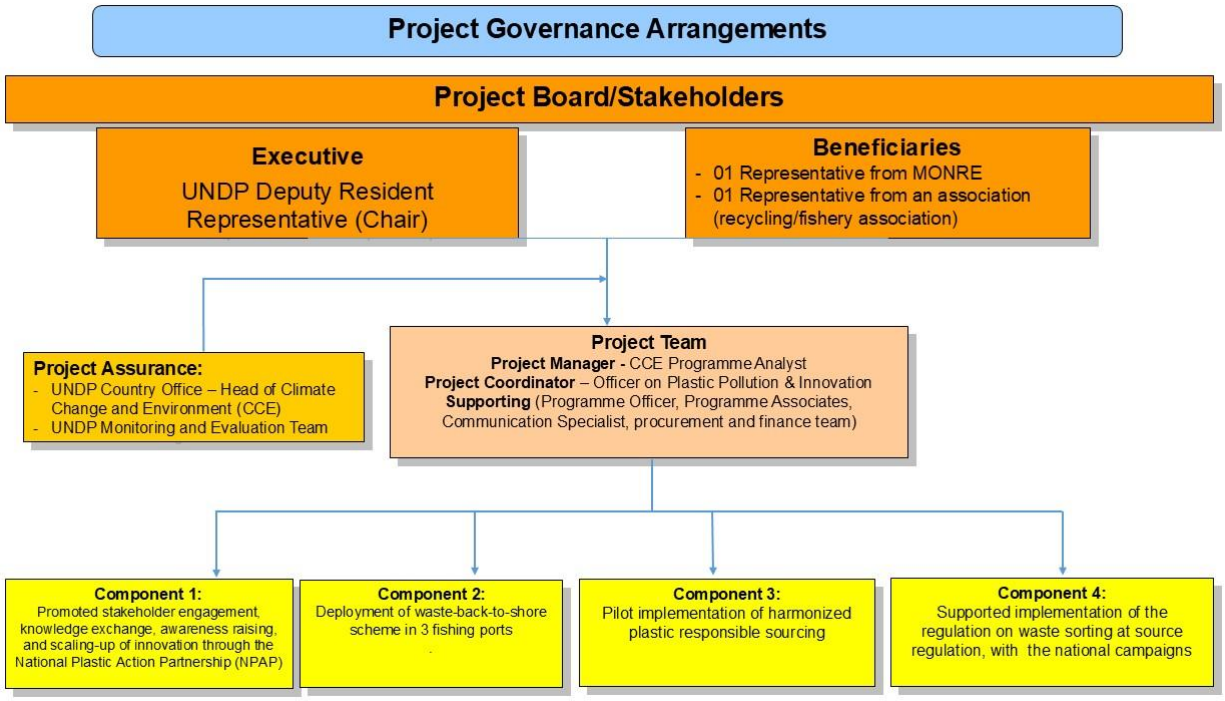

Project Manager

The project manager is responsible for reviewing and approving the project work plan and disbursement plan; taking the lead in decision-making for all project activities. The Project Manager will be responsible for overseeing the implementation of the annual work plans as well as the yearly progress and final reports. The Project Manager will review the TORs for studies, surveys, consultancies, equipment procurement, etc.; review outputs produced by project consultants and subcontractors and approve for payment; maintain regular contact with project's national focal points.

Project Officers

The project officers will be responsible for the day-to-day management and all aspects of quality management oversight of the project. The Project Officers will draw up and update project work plan, propose adjustments as needed and submit them to the Project Manager; coordinate with the technical officer in local and internationals consultants to prepare TORs for studies, surveys, consultancies, procurement of equipment etc.; review outputs produced by project consultants and subcontractors and according to the quality and relevance of these outputs in accordance with agreed terms of reference and the project objectives; support to implement all administrative procedure and support services related to the preparation of the project's activities; and engage and/or maintain regular contact with local focal points and relevant authorities for the project activities.

The Programme Associate

The programme associate will undertake project management support, predominantly on a part-time basis, including financial, administrative, procurement, monitoring and evaluation tasks, and communication activities.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

The roles of relevant stakeholders in the project is detailed in Table below

National Advisory Committee and stakeholders	▪ Provide direction and orientation to the Project implementation, to be in line with legal context of the country, in the region and donor's perspective. ▪ Review the project progress and approve overall planning for recommendation to the Regional Project Board. ▪ Approve recommendations regarding substantial changes regarding objectives and outcomes of the project for consideration by the Regional Project Board ▪ National Advisory Committee to meet annually and meet upon request.
Project Team at UNDP Viet Nam	▪ Responsible for the day-to-day management and all aspects of the project implementation; Implement project activities according to the Annual Work Plan. ▪ Draw up and update project work plan, propose adjustments as needed and submit them to the Project Manager; coordinate with the technical officers in local and internationals consultants to prepare TORs for studies, surveys, consultancies, procurement of equipment etc.; ▪ Review and approve outputs produced by project consultants and subcontractors and according to the quality and relevance of these outputs in accordance with agreed terms of reference and the project objectives; support to implement all administrative procedure and support services related to the preparation of the project's activities; ▪ Support administrative and financial procedures in bidding and disbursement ▪ Prepare progress reports to submit to the Project Steering Committee through annual meetings
Project Assurance	▪ Performs the quality assurance and supports the Project Board and Project Management Unit by carrying out objective and independent project oversight and monitoring functions. ▪ Ensures appropriate project management milestones are managed and completed, and conflict of interest issues are monitored and addressed.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

V. RESULTS FRAMEWORK[5]

Intended Outcome as stated in the Regional Programme Results and Resource Framework: Outcome 1: Inclusive and sustainable structural transformations accelerated to reduce poverty, inequality, and vulnerabilities towards the achievement of SDGs and inclusive, sustainable, resilient and digital transitions. Output 1.4: Sustainable, scalable and innovative solutions and strategies for nature, climate and energy transformation strengthened through enhanced 'climate promise', nature-based solutions, and transitioning to clean energy and zero-carbon development.
Outcome indicators as stated in the Regional Programme Results and Resource Framework, including baseline and targets: Indicator 1.4.1. Number of countries adopting scalable and innovative clean energy solutions and strategies for low-carbon development, as well access to affordable energy. Baseline (2021): 0 Targets (2025): 8 Indicator 1.4.2. Number of countries supported with nature-based solutions for inclusive and sustainable development (modified from IRRF 4.1.1) Baseline (2020): 0 Target (2025): 8 Indicator 1.4.3. Number of countries supported with climate actions to meet the Paris target including implementation of nationally determined contributions and National Adaptation Plan support. Baseline (2021): 27 Target (2025): 32 Indicator 1.4.4. Number of countries participating in transboundary and regional strategic cooperation for sustainable natural resources management Baseline (2020): 0 Target (2025): 20
Applicable Output(s) from the UNDP Strategic Plan: Outcome 1: Structural transformation accelerated, particularly green, inclusive, and digital transitions. IRRF 4.1.1 Number of people directly benefitting from initiatives to protect nature and promote sustainable use of resources. IRRF 4.1.2 Natural resources that are managed under a sustainable use, conservation, access, and benefit-sharing regime.
Project title and Quantum Project Number: Management of Plastics Waste and Circular Interventions on Plastics in South, Southeast Asia, and the Pacific (Short name: TCCF Plastics Circularity Project) Project Number: 01002871

[5] Multiple countries/IPs can contribute to the same output and can share the same indicators. UNDP publishes its project information (indicators, baselines, targets and results) to meet the International Aid Transparency Initiative (IATI) standards. Make sure that indicators are S.M.A.R.T. (Specific, Measurable, Attainable, Relevant and Time-bound), provide accurate baselines and targets underpinned by reliable evidence and data, and avoid acronyms so that external audience clearly understand the results of the project.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

PARTNERSHIP IMPACT INDICATORS[6]	DATA SOURCE	BASELINE		TARGETS				DATA COLLECTION METHODS & RISKS
		Value	Year	Year 1	Year 2	Year 3	FINAL	
Plastic Collected (metric tonnes)	Project report (Bangladesh Output 2, Indicator 2.2; Bhutan Output 2, Indicator 2.2; Cambodia Output 3, Indicator 3.2; India Output 3.2, Indonesia Output 2.1 Indicator 3.2.5; Maldives Output 3; Nepal Output 1, Indicator 1.2; Philippines Output 2, Indicator 2.1; Sri Lanka Output 1, Indicator 1.1; Vietnam project objectives; Indonesia Output indicator 1.4)	0	2024	~~10,300~~ 13,300	~~22,150~~ 25,650	~~26,660~~ 30,160	~~59,110~~ 69,110 (TCCF Target ~~53,930~~ 63,930)	UNDP No likelihood of Risk in Data Collection
Direct Beneficiaries (men)	Project report (Target gender breakdown needed: Bangladesh Output 4, Indicator 4.1; Bhutan Output 3, indicator 3.1; Cambodia Output 1, indicator 1.3; India output 2.3 indicator 2.3.1; Indonesia Output 1.1 and 1.2 Maldives Output 5; Nepal Output 2, indicator 2.1; Philippines Output 4, indicator 4.3; Sri-Lanka Output 1, indicator 1.3; Vietnam Project objectives, core indictor 2, 3; Indonesia Output indicator 2.1)	0	2024	~~7,537~~ 13,537	~~13,787~~ 23,787	~~15,541~~ 25,541	~~36,865~~ 62,865 (TCCF Target ~~36,365~~ 62,365)	UNDP No likelihood of Risk in Data Collection
Direct Beneficiaries (women)				~~6,863~~ 15,863	~~12,613~~ 27,613	~~14,259~~ 29,259	~~33,735~~ 72,735 (TCCF Target ~~33,235~~ 72,235)	
Material Recovery Facilities Implemented	Project report (Bangladesh Output 2, Indicator 2.1; Bhutan Output 2, Indicator 2.1; Cambodia, not identified as a separate output, refer to output 3, Indicator 3.2; Maldives Output 3; Nepal Output 1,	0	2024	8	7	8	23 (TCCF Target 22)	UNDP No likelihood of Risk in Data Collection

[6] It is recommended that projects use output indicators from the Strategic Plan IRRF, as relevant, in addition to project-specific results indicators. Indicators should be disaggregated by sex or for other targeted groups where relevant.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

	Indicator 1.2; Philippines Output 3, Indicator 3.2; Sri-Lanka Output 2, Indicator 2.1)							
Business Models / Management Systems Created or Strengthened	Project report (Bangladesh Output 3 indicator 3.1; Bhutan Output 3, Indicator 3.2 and 3.3; Cambodia Output 1, Indicator 1.1; India Output 3.1, indicator 3.2.2; Maldives missing; Nepal Output 1, Indicator 1.3; Philippines Output 1, Indicator 1.2; Sri-Lanka Output 2, Indicator 2.3, but not explicitly mentioned; Vietnam Output 3.6, Indicator 1; Indonesia Output indicator 2.3)	0	2024	~~8~~ 10	~~11~~ 14	~~4~~ 6	~~23~~ 30 (TCCF Target ~~19~~ 26)	UNDP No likelihood of Risk in Data Collection
Awareness / Training Programmes Launched	Project report (Bangladesh Output 4, Indicator 4.2; Bhutan Output 1, Indicator 1.1; Cambodia Output 2, Indicator 2.2 and Output 3, Indicator 3.4; India Output 3.1, Indicator 3.1.1; Maldives Output 6, needs verification; Nepal Output 2, Indicator 2.2; Philippines Output 4, Indicator 4.1, needs verification; Sri-Lanka Output 3, Indicator 3.3; Vietnam Output 3.6, Indicator 2; Indonesia Output indicator 4.2)	0	2024	~~14~~ 16	~~11~~ 14	~~23~~ 26	~~48~~ 56 (TCCF Target ~~47~~ 55)	UNDP No likelihood of Risk in Data Collection

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Child Project Results Framework

Regional Component

EXPECTED OUTPUTS	OUTPUT INDICATORS	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 1: Strengthening joint regional actions.	*Project launch*	*UNDP*	0	2024	*1*	NA	NA	*1*	*UNDP No likelihood of Risk in Data Collection*
	No. of COs supported in policy review and assessment	*National governments, UNDP COs*	0	2024	*3*	3	3	*9*	*Interviews No likelihood of Risk in Data Collection*
	No. of national and regional bodies engaged	*National governments, UNDP COs*	0	2024	*5*	5	3	*13*	*Interviews No likelihood of Risk in Data Collection*
Output 2: Provide technical assistance to countries.	*No. of trainings supported (including through provision/enhancement of technical materials)*	*National governments, UNDP COs, training respondents*	0	2024	*3*	3	3	*9*	*UNDP No likelihood of Risk in Data Collection*
	No. of knowledge materials developed/revised	*National governments, UNDP COs*	0	2024	*1*	1	1	*3*	*UNDP No likelihood of Risk in Data Collection*
Output 3: Facilitating cross-pollination of knowledge and solutions.	*No. of working groups organized*	*National governments, UNDP COs*		2024	*1*	1	1	*3*	*UNDP No likelihood of Risk in Data Collection*
	No. Of virtual meetings held	*National governments, UNDP COs*	0	2024	*4*	4	4	*12*	*UNDP No likelihood of Risk in Data Collection*
	No. Of regional conferences	*National governments, UNDP COs*	0	2024	*1*	1	1	*3*	*UNDP No likelihood of Risk in Data Collection*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 4: Engaging partners and donors on resources mobilization and collective action.	*Stakeholder mapping conducted*	*National governments, UNDP COs*	0	2024	*3*	3	3	*9*	*UNDP* *No likelihood of Risk in Data Collection*
	No. of strategic partnerships developed	*National governments, UNDP COs*	0	2024	*1*	1	1	*3*	*UNDP* *No likelihood of Risk in Data Collection*
	No. Of travels/learning missions conducted	*National governments, UNDP COs*	0	2024	*1*	1	1	*3*	*UNDP* *No likelihood of Risk in Data Collection* *Note: each year, UNDP joints TCCF for a learning mission in one of the project countries.*
Output 5: Providing coordination, monitoring, evaluation, and reporting services to country-based components.	*No. Of PSC held*	*National governments, UNDP COs*	0	2024	*1*	1	1	*3*	*UNDP* *No likelihood of Risk in Data Collection*
	No. of annual coordination and supervision missions	*National governments, UNDP COs*	0	2024	*1*	1	1	*3*	*UNDP* *No likelihood of Risk in Data Collection*
	No. of M&E reports completed	*National governments, UNDP COs*	0	2024	*4*	4	5	*13*	*UNDP* *No likelihood of Risk in Data Collection* *Note: 4 quarterly reports each year. Y3 also includes a terminal evaluation.*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

BANGLADESH

EXPECTED OUTPUTS	OUTPUT INDICATORS[7]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 1 *Strengthened collaboration with stakeholders to promote plastic waste circularity*	***1.1** Youth and women-led plastics waste recycling Startups/SMEs enhanced capacities (received Financial/Technical support) through plastics waste Circularity Hub.*	*National and local report, project document and progress report, monitoring data*	0	2024	*10*	10	10	*30*	*Interviews, FGDs, Surveys, City/Municipal reports* *No likelihood of Risk in Data Collection*
Output 2 *Plastics Waste Market System Developed*	*2.1 Capacity enhancement of MRF/ collection/ reverse-distribution centers implemented*	*Govt. /City/Municipal report, project document and progress report, monitoring data*	0	2024	*0*	0	1	*1*	*Interviews, FGDs, Surveys, City/Municipal reports* *No likelihood of Risk in Data Collection*
	2.2 Plastics waste Circulated (in MT)		*0*	*2024*	*3000*	*5000*	*7000*	*15000*	*Interviews, FGDs, Surveys, City/ Municipal reports* *No likelihood of Risk in Data Collection*
Output 3 Gender responsive information and plastic waste traceability	*3.1 Plastics waste market systems developed, and plastics waste value chain actors onboarded to digital marketplace*	*Govt. /City/Municipal report, project document and progress report, monitoring data*	*0*	*2024*	*1*	*1*	*1*	*3*	*Interviews, FGDs, Surveys, City/Municipal reports* *No likelihood of Risk in Data Collection*

[7] It is recommended that projects use output indicators from the Strategic Plan IRRF, as relevant, in addition to project-specific results indicators. Indicators should be disaggregated by sex or for other targeted groups where relevant.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS[7]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
mechanism established.									
Output 4 Awareness, knowledge, and capacities been developed among urban residents.	*4.1 Better livelihood, Health and safety arrangement of plastic waste workers (especially women) are achieved*	*Govt. /City/Municipal report, project document and progress report, monitoring data*	*0*	*2024*	*600 (400 males; 200 females)*	*700 (500 males; 200 females)*	*700 (500 males; 200 females)*	*2000 (1400 males; 600 females)*	*Interviews, FGDs, Surveys, City/Municipal reports* *No likelihood of Risk in Data Collection*
	4.2 Awareness/ Training program initiated		*0*	*2024*	*2*	*2*	*2*	*6*	

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

BHUTAN

EXPECTED OUTPUTS	OUTPUT INDICATORS[8]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 1 Awareness programs developed and deployed to support behavior change in schools, colleges, business enterprises and monasteries.	*1.1 Number of awareness programs provided to schools, colleges, hotels and monasteries*	*Project report*	0	2024	*2*	2	2	*6*	*Awareness program report*
Output 2 Increase plastic waste collection through deployment of best environmental practices and technologies such as compactor trucks, and value addition machines.	*2.1 Number of compactor trucks deployed*	*Project report*	0	2024	*3*	3	3	*9*	*LG stock inventory record*
	2.2 Metric tons of plastic waste (including PET and single use plastic) collected	*Project report*	*0*	*2024*	*2000*	*2000*	*1500*	*5500*	*LG monitoring report*
Output 3 Capacity of waste handlers (formal and informal) developed in proper segregation and hygiene.	*3.1 Individuals provided with PPEs, sorting and cleaning training and health camps and hygiene training*	*Training record, UNDP*	*0*	*2024*	*200*	*200*	*200*	*600*	*Gender segregated Training record (M 300: F 300)*
	3.2 Business model and system developed/strengthened	*District/ Municipal report*	*0*	*2024*	*1*	*0*	*0*	*1*	*District/municipality record*

[8] It is recommended that projects use output indicators from the Strategic Plan IRRF, as relevant, in addition to project-specific results indicators. Indicators should be disaggregated by sex or for other targeted groups where relevant.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS[8]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
	3.3 Geographic distribution of plastic waste distribution mapped	*GIS report, UNDP*	*0*	*2024*	*0*	*1*	*0*	*1*	*GIS report*
Output 4 Project communication, advocacy and knowledge management	*5.1 Number of advocacy and communication materials produced*	*Project report, UNDP*	*0*	*2024*	*1*	*0*	*1*	*2*	*Project report*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

CAMBODIA

EXPECTED OUTPUTS	OUTPUT INDICATORS[9]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 1 Priority business models for plastic recycling and alternatives operationalized	1.1 **Green financing and economic instruments are designed**, to support innovative business solutions (e.g., alternatives, reuse, refill, recycling). *Measured by number of plastic recycling and plastic alternatives innovations supported.*	*Project report (annual and quarterly report)*	11	2024	*2*	3	0	*5*	Reviews of documents
	1.2 **Circular Economy measures** to reduce the usage of SUPs **in the hospitality sector are implemented.** *Measured by number of hotels and restaurants implementing plastic reduction measures.*	*Project report (annual and quarterly report)*	*65 (cumulatively in PP, SHV, SR)*	*2024*	*50*	*50*	*50*	*150*	Reviews of documents and field monitoring
	1.3 **Livelihood of informal waste collectors is improved** by integrating them into the plastics value chain, especially in collection and recycling. *Measured by number of waste workers supported with inclusion mechanisms such as basic social services, formalization, provision of personal protective equipment (PPE), etc.*	*Project report (annual and quarterly report)*	*0*	*2024*	*150*	*150*	*150*	*450 (>= 250 female)*	Reviews of documents and field monitoring
Output 2 National capacity enhanced and improved	2.1 **Gender-sensitive strategic communication and awareness raising** using social media and websites **are conducted.** *Measured by:*	*Project report (annual and quarterly report)*	a) 30 b) 8.14M	2024	*a) 12 b) 250K*	*a) 12 b) 500K*	*a) 12 b) 250K*	*a) 36 b) 1000K*	Reviews of documents and social media monitoring

[9] It is recommended that projects use output indicators from the Strategic Plan IRRF, as relevant, in addition to project-specific results indicators. Indicators should be disaggregated by sex or for other targeted groups where relevant.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS[9]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
awareness about the plastic crisis and its solutions among citizens and the private sector.	*number of gender sensitive awareness raising materials developed and disseminated to the public.* *a) Number of gender-sensitive awareness raising materials on plastic management (messages on social media) developed and disseminated to the public* *b) Number of people reached by awareness raising communication on plastic waste management (gender disaggregated)*								
	2.2 **Awareness among the public and private sector** to promote 4Rs is **increased.** *Measured by qualitative and quantitative data gathered through final survey targeting main stakeholders impacted by project activities. This may include students, teachers, sub-national government, and general public.*	*Project report (annual and quarterly report)*	*1*	*2024*	*0*	*0*	*1*	*1*	Reviews of documents and field monitoring
	2.3 **Outreach activities implemented** in schools and temples through schools and pagoda schemes. *Measured by number of awareness/training programs launched and implemented in schools and pagodas.*	*Project report (annual and quarterly report)*	*80*	*2024*	*10*	*10*	*10*	*30*	Reviews of documents and field monitoring
Output 3 Plastic waste leakage reduced in target provinces and cities.	3.1 **Plastic waste equipment** (water filtration equipment, bins, water dispensers…etc) to implement circular plastic initiatives **to support waste segregation, collection and recycling are installed**. *Measured by number of water filtration systems provided to schools and pagodas.*	*Project report (annual and quarterly report)*	*90*	*2024*	*0*	*0*	*0*	*1*	Reviews of documents and field monitoring

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS[9]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
	3.2 **A material recovery facility (MRF) is established** for the collection and processing of plastic waste. *Measured by amount of plastic waste (metric tonnes per year) collected and processed.*	*Project report (annual and quarterly report)*	*3,000*	*2024*	*1,000*	*2,000*	*1,500*	*4,500*	Reviews of documents and field monitoring
	3.3 **A "Beat Plastic Pollution Innovation Challenges"** for the promotion of alternatives and recycling **is implemented**. *Measured by number innovation challenges implemented.*	*Project report (annual and quarterly report)*	*3*	*2024*	*0*	*1*	*0*	*1*	Reviews of documents and field monitoring
	3.4 **Knowledge and capacity of subnational governments** for sound waste management **is enhanced.** *Measured by number of events organized and/or attended to disseminate project achievements and increase knowledge and capacity for sound waste management.*	*Project report (annual and quarterly report)*	*11*	*2024*	*1*	*1*	*2*	*4*	Reviews of documents and field monitoring

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

INDIA

EXPECTED OUTPUTS	OUTPUT INDICATORS[1]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 2.3: *Expansion of robust and inclusive social protection systems and improved access to assets and services for poor and vulnerable groups such as tribal, migrants, people infected or affected by HIV, PWD, LGBTIQ etc.*	***Indicator 2.3.1: Number of beneficiaries from social protection schemes, other inclusive development schemes and enabling legislations [SP IRRF: 1.2.1 & 1.2.2]***	*Ministry of Social Justice and Empowerment; Ministry of Tribal Affairs and reports published on other government portals, Project Reports*	12000 (social protection scheme linkage for waste workers)	2024	*2,000 (1,000 female)*	3,000 (1,500 female)	5,000 (2,500 female)	*10,000 (5000 female)*	Central and state governments; district administration; Private sector; civil society; volunteer networks; community-based organizations; think tanks; media;
	TCCF Project Indicator: *1. successful enrolment of waste workers in government social protection programmes by addressing access barriers and strengthening service linkages.* *2. Enhanced awareness about rights and entitlements for waste workers through outreach and support via Helpline.*	*Ministry of Social Justice and Empowerment; Ministry of Tribal Affairs and reports published on other government portals, Project Reports, Helpline Call Centre CRM Reports*	25000 (awareness on rights and entitlements through Helpline)	2024	*10,000 (5,000 female)*	20,000 *(10,000 female)*	20,000 *(10,000 female)*	*50,000 (25,000 female)*	
Output 3.1 Institutional and policy frameworks developed and strengthened to address climate change, enhance	***Indicator 3.1.1: Number of climate and gender-responsive development strategies (policies, schemes, programmes, and action plans) informed, through***	*Reports published in collaboration with Ministry of Environment, Forest and Climate Change/ Ministry of Housing and*	0	2024	1	1	1	3	*Central and state governments; district administration; Private sector; civil society; volunteer networks;*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

green recovery, prevent environmental degradation and promote conservation and circular economy.	***technical / advisory support, for achieving national priorities and global commitments under multilateral environmental agreements (global, national, subnational level) [SP IRRF: 3.1.1]*** ***TCCF Project Indicator:*** *Comprehensive guidelines developed for effective plastic waste management through responsible sourcing practices.*	*Urban Affairs/ Ministry of Social Justice and Empowerment, UNDP Reports*							*community-based organizations; think tanks; media;*
	Indicator 3.2.2: Number of technologies and ecosystem-based solutions developed and upscaled for sustainable management of ecosystems and resource utilization and natural resource efficiency [SP IRRF: 4.1.2] ***TCCF Project Indicator:*** *Business Model Developed for Responsibly Sourcing of Plastic Waste.*	*Government records / Project reports*	0	2024	0	0	1	1	*Central and state governments; district administration; Private sector; civil society; volunteer networks; community-based organizations; think tanks; media;*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Output 3.2 Innovative solutions developed, demonstrated and upscaled at national and subnational levels for vulnerable communities and businesses to benefit from sustainable management of natural resources (land, water, air), chemicals and circular economy.	***Indicator 3.2.5: Amount of waste channelized into circular economy [SP IRRF: 4.2.1]*** ***TCCF Project Indicator:*** *MTs of plastic waste responsibly sourced*	*Urban local bodies; CPCB; State and Central government reports*; Project Reports; Recyclers Reports	0	2024	2,000	3,000	3,000	8,000	*Central and state governments; district administration; Private sector; civil society; volunteer networks; community-based organizations; think tanks; media;*

[1] It is recommended that projects use output indicators from the Strategic Plan IRRF, as relevant, in addition to project-specific results indicators. Indicators should be disaggregated by sex or for other targeted groups where relevant.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

INDONESIA

EXPECTED OUTPUTS	OUTPUT INDICATORS	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)					DATA COLLECTION METHODS & RISKS
					Year 1		Year 2		FINAL	
			Value	Year	2025 (Aug-Dec)	2026 (Jan-Sep)	2026 (Oct-Dec)	2027 (Jan-Oct)		
Output 1: Increased knowledge, skills, and safety of waste workers within CBOs to enhance their role in the circular economy.	**Indicator 1.1 Baseline assessment conducted across all project locations**	Community-Based Organizations; Local Government	0	2025	1	0	0	0	1 Baseline assessment conducted across all project locations	**Data:** Reports from CBOs and Local Governments. **Risk:** Delays in material development and distribution due to funding or regulatory approvals; Variability in worker participation due to socioeconomic constraints and lack of incentives. **Anticipation:** Collaboration with educational institutions and digital platforms to accelerate content creation; Providing stipends, protective equipment, and incentives for participation through CBO partnerships.
	Indicator 1.2 Number of educational materials	Community-Based Organizations;	0	2025	30	30	10	30	100 educational materials	

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

	developed and distributed	Local Government								
	Indicator 1.3 Number of waste workers trained in sustainable waste management.		0	2025	15000 (9,000 Female)	17000 (10,200 Female)	8000 (4,800 Female)	25000 (15,000 Female)	65,0000 (39,000 Female) waste workers trained	
	Indicator 1.4 Number of waste workers provided with safety training and better equipment.	Community-Based Organizations; Local Government	0	2025	5000 (3,000 Female)	7000 (4,200 Female)	3000 (1,800 Female)	10000 (6,000 Female)	25,000 (15,000 Female) waste workers provided with safety training	
Output 2: Improved waste collection systems and	**Indicator 2.1 Number of plastic waste collected, recycled, and**	Community-Based Organizations;	0	2025	3.000	2.000	1.500	3.500	10,000 metric tons of plastic waste	**Data:** Reports from CBOs, Local Government, and Waste Management Facilities. **Risk:** Delays in funding,

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

recycling rate to support waste workers' livelihoods.	**diverted from landfills.**	Local Government								material distribution, and regulatory approvals; Variability in worker participation due to socioeconomic constraints and lack of incentives. **Anticipation:** Collaboration with private sectors/NGOs; Providing stipends, protective equipment, and incentives for participation through CBO partnerships.
	Indicator 2.2 Number of waste workers directly involved in collection and recycling improvements.	Community-Based Organizations; Local Government	0	2025	5000 (3,000 Female)	7000 (4,200 Female)	3000 (1,800 Female)	10000 (6,000 Female)	25,000 (15,000 Female) waste workers involved	
	Indicator 2.3 Number of Pilot waste collection and recycling initiatives implemented in 7 cities.	Local Government	0	2025	2	2	1	2	7 pilot projects	
Output 3: Strengthened financial	**Indicator 3.1 Number of waste-based**	Financial reports from funding	0	2025	15	13	7	15	50 waste-based social enterprises/CBOs	**Data:** Reports from funding institutions, waste-based enterprises, and CBOs.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

resilience of waste workers by improving access to funding and sustainable business models.	**social enterprises/CBOs supported with funding access.**	partners, CBO records, grant distribution reports								**Risk:** Limited availability of financial resources and potential delays in disbursement of funding support; Lack of commitment from stakeholders and difficulty in aligning goals among multiple actors. **Anticipation:** Establishing clear funding mechanisms with public and private sector contributions to ensure sustainable financing; Strengthening multi-stakeholder engagement through structured collaboration frameworks, incentive mechanisms, and ongoing facilitation.
	Indicator 3.2 Number of new partnerships established between waste workers, private, and government agencies.	MoUs, partnership agreements, government and private sector reports	0	2025	5	5	2	8	20 new partnerships established	
Output 4: Strengthened institutional, policy, and regulatory	**Indicator 4.1 Number of policy gaps identified and aligned with national labor**	Policy review reports	0	2025	1	1	1	0	3 policy gaps identified and aligned with national and international best practices	**Data:** Policy analysis reports, government agency records, and regulatory frameworks. **Risk:** Delays in policy

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

frameworks for integrated and collaborative plastic waste management.	**laws, environmental regulations, and international best practices**									development and approval processes due to bureaucratic constraints; potential resistance from stakeholders regarding policy changes. **Anticipation:** Engaging key policymakers early in the process, providing capacity-building for government agencies, and fostering stakeholder consensus through consultations and advocacy efforts.
	Indicator 4.2 Strengthened capacity of the TKN PSL Secretariat for regulatory advocacy.	Presidential Regulation Number 83/2018 regarding Marine Debris Management	0	2025	2	2	1	3	8 capacity-building activities conducted	
	Indicator 4.3 Expanded labor protections for waste workers through policy integration.	Official policy documents, government publications, labor law amendments	0	2025	1	1	1	0	3 new or expanded labor protection policies	
Output 5: Effective knowledge management,	**Indicator 5.1 Number of active users (waste workers,**	User activity logs, platform analytics, government	0	2025	50	100	50	100	300 active users engaged in waste tracking, coordination, and transactions	**Data:** Platform usage analytics, reports from implementing partners, and government engagement

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

outreach, and monitoring system for plastic waste management.	**communities, government agencies, private sector actors) utilizing the platform for waste tracking, coordination, and transactions.**	and private sector reports								records. **Risk:** Low adoption rate of digital tools among waste workers and local communities; potential technical issues with the platform. **Anticipation:** Providing digital literacy training, ensuring mobile-friendly accessibility, and partnering with local community leaders to encourage platform usage.
	Indicator 5.2 Number of knowledge management system established to capture lessons learned, best practices, and research findings related to plastic waste management.	Local Government; CBOs; NGOs; Private Sectors	0	2025	1	0	1	1	Fully operational knowledge management system with documented research and best practices	
	Indicator 5.3 Number of social media campaigns, workshops, and forums	Records from campaign reports, workshop attendance	0	2025	5	7	3	15	30 community engagement activities (social media campaigns,	

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

	conducted to engage communities.	lists, forum documentation							workshops, and forums)	
	Indicator 5.4 Increased visibility of waste workers' contributions and the circular economy through media coverage and community discussions.	Local Government; CBOs.	0	2025	3	4	1	8	16 documented media articles and community discussions highlighting waste workers' role	

MALDIVES

EXPECTED OUTPUTS	OUTPUT INDICATORS	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 1 Conduct Waste Management Workshops with key stakeholders to showcase best practices, explore local level context (challenges and opportunities) and discuss standardization of plastic waste management.	Waste management workshops conducted	WAMCO	0	2024	1	1	1	3	Workshop reports and signed attendance sheets. Videos and photographs.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 2 Identify, document, and amplify Best Environment Practices at local level through Best Available Technology support grant(s)	Number of BEP initiatives highlighted	WAMCO	0	2024	0	3	0	3	Videos and blogs.
	Number of local initiatives supported with BAT grants	WAMCO	0	2024	0	0	1	1	Grant report. Videos and photographs.
Output 3 Establish plastic processing pilot in Maldives to enhance plastic waste management and recycling in a target region.	Number of plastic processing facilities established	WAMCO	0	2024	0	1	1	2	Field reports, photographs. Handover documents.
	Plastics Collected (metric tons)	WAMCO		2024	0	4,500	4,500	9,000	Collection reports by WAMCO.
Output 4 Provision of electric vehicles and renewable energy infrastructure and capacity to the Waste Management Corporation for key population centers.	Number of electric vehicles in Waste Management Fleet	WAMCO	2	2024	9	0	0	9	Field reports, photographs. Handover documents.
	Number waste management centers with solar power infrastructure	WAMCO	0	2024	0	1	2	3	Field reports, photographs. Handover documents.
Output 5 Information and Guidelines on Plastics and Waste Management Strengthened in a gender-responsive manner through development of a learning platform and training of management personnel of WAMCO.	Number of learning management systems established	WAMCO	0	2024	0	1	0	1	LMS manuals, online verification.
	Number of waste management personnel trained (male, female) in waste management practises	WAMCO	0	2024	0	0	800 (260 female)	800 (260 female)	Training report and signed attendance sheet and/or LMS data.
Output 6 Translate and upload training modules to the learning portals.	Number of modules uploaded to learning portals	WAMCO	0	2024	0	0	2	2	Online verification and LMS data.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

NEPAL

EXPECTED OUTPUTS	OUTPUT INDICATORS[10]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 1 *MRFs are equipped with processing and management technologies*	1.1 # of MRFs supported with technology and other management support	Project/ Activity Report	0	2024	*3*	2	1	*6*	
	1.2 total plastic waste in tonnes recovered through MRFs	Project/ Activity Report	*0*	2024	*500*	*400*	*250*	*1150*	
	1.3 # of business plans/management system developed/strengthened	Project/ Activity Report	*0*	2024	*2*	*1*	*1*	*4*	
Output 2 *Waste workers and communities are empowered with awareness campaigns, skills and livelihood opportunities.*	2.1 # of waste workers received support for safety and livelihood options	Project/ Activity Report	0	2024	550 (213 female)	550 (213 female)	450 (174 female)	1550 (600 female)	
	2.2 # of awareness campaigns conducted	Project/ Activity Report	0	2024	*1*	*2*	*1*	*4*	

[10] It is recommended that projects use output indicators from the Strategic Plan IRRF, as relevant, in addition to project-specific results indicators. Indicators should be disaggregated by sex or for other targeted groups where relevant.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

PHILIPPINES

EXPECTED OUTPUTS	OUTPUT INDICATORS[11]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 1 Inclusive, sector-specific business models successfully developed and integrated into the existing waste diversion system, enhancing efficiency and sustainability in plastic waste management of the locality.	1.1 Number of startups, MSMEs, women-owned businesses, and/or NGOs engaged in the development of inclusive business models	Project reports	0	2024	2	3	0	5	Programme Monitoring Visits, Project Evaluation
	1.2 Number of innovative and financially sustainable business models developed	Project reports	0	2024	2	2	0	4	Post-activity reporting
	1.3 Pilot implementation of inclusive business models	Project reports	0	2024	0	1	1	2	Programme Monitoring visit
	1.4 Number of barangays engaged in the pilot implementation	Project reports	0	2024	1	1	0	2	Programme monitoring visit
Output 2 Local capacity to improve local plastic waste collection, recovery and recycling strengthened.	2.1 Total amount (in metric tons) of plastic waste collected in partner LGU	Project reports	0	2024	300	250	910	1,460	Monitoring and reporting of waste collection
	2.2 Number of local policies enacted to enhance plastic waste collection, recovery, and recycling	LGU and Barangay issuances	0	2024	0	1	1	2	Review of issuances
	2.3 Number of barangays capacitated and supported	Evaluation report	0	2024	2	2	2	6	Programme monitoring visit
Output 3 Plastic recovery and recycling operations	3.1 Number of GEDSI groups capacitated and trained	Project/ Activity Report	0	2024	2	0	0	2	Post-activity reporting, documentation

[11] It is recommended that projects use output indicators from the Strategic Plan IRRF, as relevant, in addition to project-specific results indicators. Indicators should be disaggregated by sex or for other targeted groups where relevant.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS[11]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
of at least two GEDSI/ informal waste picker groups organized and scaled up.	3.2 Number of storage/recovery facilities established	Project reports/	0	2024	2	0	0	2	Programme monitoring visit
	3.3 Number of GEDSI groups, including the informal sector, supported and provided with seed capital	Project/ Activity Report	0	2024	2	0	0	2	Programme monitoring visit, project evaluation
Output 4 Behavioral change modules for the targeted plastic waste sources developed and implemented.	4.1 Number of customized behavioral change module/toolkit developed	Project reports	0	2024	3	0	1	4	Inventory of knowledge products
	4.2 Number of institutions partnered for trainings and seminars	Project reports	0	2024	2	2	1	5	Post-activity reporting, documentation
	4.3 Number of individuals trained (450 women, 300 men)	Project reports	0	2024	200 (100 female)	300 (100 female)	250 (250 female)	750 (375 female)	Post-activity reporting, documentation
	4.4 Stakeholders' knowledge, perception, and attitude on plastic recovery and recycling improved	Project reports/ testimonials	0	2024	1	2	2	5	Formal surveys; focus group discussions
Output 5 Digital application that enables waste diversion tracking with incentives or reward system deployed.	5.1 Number of digital applications deployed to support tracking of waste diversion and incentivizing of plastics collection and recovery	Project Report	0	2024	1	0	0	1	Project evaluation
	5.2 Number of barangays engaged and trained in the use of the digital application	Project Report	0	2024	2	2	2	6	Post-activity reporting, documentation
	5.3 Number of incentive programs for plastic collection and recovery established alongside the digital app deployment	Project Report	0	2024	1	0	0	1	Project evaluation

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

SRI LANKA

EXPECTED OUTPUTS	OUTPUT INDICATORS	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 1 - Systemic approach to plastic waste management adopted and practiced at the selected local authorities.	1.1Quantity of plastic Waste Collected (in Metric tons)	MRF records of LAs	15-18	2024	*500*	3000	3500	*7000*	*Annual waste collection reports of LAs* *Risks: Low level of local engagement*
	1.2 No of Resource banks established/strengthened	*Survey reports, Local Authority reports, UNDP reports*	40	2024	*10*	100	150	*300*	*Site visits, agreements between LAs* *Risks: Low level of commitment and engagement of the stakeholders*
	1.3 No of people directly benefitted		160	2024	*100 (50 male, 50 female)*	200 (100 male, 100 female)	900 (450 male, 450 female)	*1200 (600 male, 600 female)*	
Output 2 - BAT/BEP options are introduced to implement strategies developed under Output 1:	2.1 Number of MRF facilities established.	*UNDP Procurement reports, Local Authority reports, UNDP project reports*	1	2024	*0*	1	1	*2*	*Site visits, agreements between LAs* *Risk: Less interest of Local Authorities in engaging private sector to operate MRF facilities*
	2.2 Number of MRF facilities strengthened	*UNDP Procurement reports, Local Authority reports, UNDP project reports*	*1*	*2024*	*0*	*0*	*1*	*1*	

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
	2.3 Number of digital solutions, introduced to improve the efficacy of circular economic interventions	*UNDP Procurement reports, Local Authority reports, UNDP project reports*	*0*	*2024*	*0*	*1*	*1*	*2*	*Technical specifications prepared for digital solutions* *Risk: Low level of commitment of the local authorities.*
Output 3 - Implement a phased campaign over the project period (3 years) on plastic pollution prevention and build capacity of LAs and stakeholders.	3.1 Number of campaign plans developed	*UNDP Reports*	*0*	*2024*	*1*	0	0	*1*	*UNDP Reports* *Risk: Changes in waste management plans at the local authority level due to political interest*
	3.2. Number of people trained and capacitated	*UNDP Reports, Programme Agendas, Attendance sheets*	*0*	*2024*	*500 (250 male, 250 female)*	*500 (250 male, 250 female)*	*500 (250 male, 250 female)*	*1500 (750 female, 750 male)*	*Interviews, Training programme Reports* *Risk: Low level of engagement and commitment of the local authorities and the communities.*
	3.3 Number of training and capacity building programmes conducted	*Programme Agendas, Attendance sheets*	*0*	*2024*	*4*	*2*	*4*	*10*	
Output 4 - Share lessons learned from demonstrations and interventions at the selected project	**4.1** No: of LAs targeted by knowledge sharing plans	*UNDP Reports*	*0*	*2024*	*10*	*200*	*141*	*341*	*Interviews, Site visits* *Risks: Low level of local engagement and change of priorities (including local authorities and other relevant stakeholders)*
	4.2 Knowledge-sharing material and strategies/plans developed	*UNDP Reports*	*0*	*2024*	*1*			*1*	

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
locations, across LA areas.									

VIET NAM

EXPECTED OUTPUTS	OUTPUT INDICATORS[1]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Project objectives Create an enabling environment and promote circular interventions throughout the plastic lifecycle to support the achievement of national targets for reducing plastic pollution	***Core Indicator 1****: tons of plastic waste collected*	*Project reports, surveys, workplan and provincial reports, outputs from relevant projects/initiatives*	*0*	*2024*	*1,000*	*2,000*	*4,000*	*7,000*	*Review and verify reports and baseline studies/surveys.* *Risks: Low engagement level of fishing boats, recyclers and local stakeholders in project interventions; and changes in national directions and policies in tackling plastic pollution*
	Core Indicator 2*: # of male participants benefited from the project activities*		*0*	*2024*	*500*	*1,000*	*1,000*	*2,500*	
	Core Indicator 3*: # of female participants benefited from the project activities*		*0*	*2024*	*150*	*300*	*300*	*750*	

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS[1]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
Output 1.2 Promote stakeholder engagement, knowledge exchange, awareness raising, and innovation	***Indicator 1.*** *# locally led innovations that incubated, accelerated and scaled up to tackle plastic innovation challenge in local areas*	*Project report, workplan and lesson learnt briefs*	*0*	*2024*	*2*	*2*	*2*	*6*	*Direct consultation, collation and analysis of project reports* *Risk: Disruption in participation of selected innovators and low-level of engagement from local authorities in supporting these innovations*
Output 2.1. Deployment of waste-back-to-shore scheme in 03 fishing ports	***Indicator 1.*** *# of fishing boats signing up to plastic-waste-back-to-shore schemes after baseline assessment*	*Local authorities' reports, workplan and baseline surveys*	*0*	*2024*	*50*	*100*	*50*	*200*	*Review and verify reports, direct consultation from local authorities (DARDs)* *Risk: Low level of commitments from local participants and affects from tourism sectors*
	Indicator 2. *# of fishing ports endorsed to deploy the plastic-waste-back-to-shore interventions*	*Project reports, technical guideline and procedures*	*0*	*2024*	*1*	*1*	*1*	*3*	
Output 2.2. Pilot implementation of harmonized plastic responsible sourcing	***Indicator 1.*** *# of stakeholders in a local plastic value chain implemented harmonized*	*Baseline surveys, consultation workshop materials and minutes, outputs*	*25*	*2024*	*25*	*10*	*15*	*50*	*Review and verify reports, direct consultation from local authorities*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS[1]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
	responsible sourcing framework	*from UNDP's RSI pilot project*							*Risk: Low level of commitments from local participants; limited access to IWWs network at local areas*
Output 3.6. Support the implementation of the regulation on waste sorting at source regulation	***Indicator 1.** # of management system created/strengthened for implementing the national waste classification programme*	*Provincial reports and news, project reports*	*0*	*2024*	*0*	*1*	*4*	*5*	*Review and verify reports, direct consultation from local authorities* *Risk: Low level of engagement from local authorities; changes in local planning and development plans*
	***Indicator 2.** # of national campaigns promoting waste sorting at sources conducted in local cities*	*Provincial reports, campaign workplan and materials, campaign surveys*	*0*	*2024*	*0*	*1*	*1*	*2*	*Review and verify reports and existing waste systems, direct consultation from local authorities* *Risk: Changes in national plans regarding solid waste management*
Output 4.5. Two national communication campaigns	***Indicator 1.** Number of participants raised awareness on plastic*	*Communication materials, campaign survey*	*0*	*2024*	*300*	*300*	*400*	*1,000*	*Review and verify reports, direct*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	OUTPUT INDICATORS[1]	DATA SOURCE	BASELINE		TARGETS (by frequency of data collection)				DATA COLLECTION METHODS & RISKS
			Value	Year	Year 1	Year 2	Year 3	FINAL	
	pollution and changed behaviours on waste classification through communication campaigns and engagement workshops in selected cities	*reports, workshop materials media posts*							*consultation from local authorities* *Risks: Not availability of equipment and facilities for plastic waste transportation and recycling at local levels*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

VI. MONITORING AND EVALUATION

In accordance with UNDP's programming policies and procedures, the project will be monitored through the following monitoring and evaluation plans:

Monitoring Plan

Monitoring Activity	Purpose	Frequency	Expected Action	Partners (if joint)	Cost (if any)
Track results progress	Progress data against the results indicators in the RRF will be collected and analysed to assess the progress of the project in achieving the agreed outputs.	Quarterly, or in the frequency required for each indicator.	Slower than expected progress will be addressed by project management.		
Monitor and Manage Risk	Identify specific risks that may threaten achievement of intended results. Identify and monitor risk management actions using a risk log. This includes monitoring measures and plans that may have been required as per UNDP's Social and Environmental Standards. Audits will be conducted in accordance with UNDP's audit policy to manage financial risk.	Quarterly	Risks are identified by project management and actions are taken to manage risk. The risk log is actively maintained to keep track of identified risks and actions taken.		
Learn	Knowledge, good practices and lessons will be captured regularly, as well as actively sourced from other projects and partners and integrated back into the project.	At least annually	Relevant lessons are captured by the project team and used to inform management decisions.		
Annual Project Quality Assurance	The quality of the project will be assessed against UNDP's quality standards to identify project strengths and weaknesses and to inform management decision making to improve the project.	Annually	Areas of strength and weakness will be reviewed by project management and used to inform decisions to improve project performance.		
Review and Make Course Corrections	Internal review of data and evidence from all monitoring actions to inform decision making.	At least annually	Performance data, risks, lessons and quality will be discussed by the project board and used to make course corrections.		

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Project Report	A progress report will be presented to the Project Board and key stakeholders, consisting of progress data showing the results achieved against pre-defined annual targets at the output level, the annual project quality rating summary, an updated risk long with mitigation measures, and any evaluation or review reports prepared over the period.	Annually, and at the end of the project (final report)			
Project Review (Project Board)	The project's governance mechanism (i.e., project board) will hold regular project reviews to assess the performance of the project and review the Multi-Year Work Plan to ensure realistic budgeting over the life of the project. In the project's final year, the Project Board shall hold an end-of project review to capture lessons learned and discuss opportunities for scaling up and to socialize project results and lessons learned with relevant audiences.	Annually, and at the end of the project (final report)	Any quality concerns or slower than expected progress should be discussed by the project board and management actions agreed to address the issues identified.		
Co-Financing Reporting	The project co-financing will be closely monitored during the project implementation. The COs are required to report at least annually the co-financing mobilized from other funding sources against the agreed targets as indicated in the table below. The regional coordination will consolidate the information received and report to donor in the annual report and at the end of project report.	Annually, and at the end of the project (final report)			

Co-financing Target

No.	Child Project	Co-financing Target (USD)	Potential Co-financing Source (to be updated by the COs, with target breakdowns)
1	**Bhutan**	600,000	TBD
2	**Nepal**	500,000	KOICA, New private partner
3	**Viet Nam**	3,500,000	In kind co financing NAP, Netherlands, Private sector
4	**Philippines**	4,500,000	Private sector, Existing or new donors

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

5	**Cambodia**	30,440,000	MOE, WB issued co-financing for plastics, cash co-financing (Japan and GEF 8)
6	**Maldives**	1,650,000	Healthcare waste management, WAMCO
7	**Bangladesh**	2,710,000	Private sector, FBCCI in kind co-financing, Other
8	**India**	2,500,000	Existing pipeline, MoSJE
9	**Sri Lanka**	500,000	Private sector, Existing or new donors
10	**Regional**	TBD	To be determined during implementation
11	**Indonesia**	14,648,998.60	Norwegian MFA1,550,669.55 Uni Arab Emirates 4,500,000.00 State budget 138,193.65 Local budget 3,800,000.00 Religious Organizations, Indonesia's National Zakat Agency (BAZNAS) 1,518,195.40 National Waqf Agency 3,141,940.00
Total		~~**46,900,000**~~ **61,548,998.6**	

Evaluation Plan

Evaluation Title	Partners (if joint)	Related Strategic Plan Output	UNSDCF/CPD Outcome	Planned Completion Date	Key Evaluation Stakeholders	Cost and Source of Funding
End of Project Evaluation				June 30, 2027		Covered under from TCCF regional component at US$ 50,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

VII. MULTI-YEAR WORK PLAN BY PARTNER COUNTRY[12][13]

A separate, subsidiary multi-year work plan must be prepared for each partner country with an Implementing Partner. ***Only the contribution by one country/IP should be present in any one subsidiary work plan.*** *Joint results are included in the joint Results Framework. All workplans together will yield the joint results framework. The respective work plans may be annexed to the project document. All anticipated programmatic and operational costs to support the project, including development effectiveness and implementation support arrangements, need to be identified, estimated and fully costed in the project budget under the relevant output(s). This includes activities that directly support the project, such as communication, human resources, procurement, finance, audit, policy advisory, quality assurance, reporting, management, etc. All services which are directly related to the project need to be disclosed transparently in the project document.*

EXPECTED OUTPUTS	Total Budget			
	Y1	Y2	Y3	**Total**
Bangladesh				
Output 1: Strengthened collaboration with stakeholders to promote plastic waste circularity	45,000	55,000	41,220	141,220
Output 2: Plastics Waste Market System Developed	256,000	418,000	182,220	856,220
Output 3: Gender responsive information and plastic waste traceability mechanism established,	110,000	170,000	66,220	346,220
Output 4: Awareness, knowledge, and capacities been developed among urban residents	172,000	220,000	306,220	698,220
Project Management Cost	97,018	97,018	97,018	291,055
DPC 3%	17,490	25,890	22,675	66,055
General Management Support (8%)	55,801	78,873	57,246	191,919
Levy (1%)	7,533	10,648	7,728	25,909
Grand Total	**760,842**	**1,075,429**	**780,548**	**2,616,819**

[12] Cost definitions and classifications for programme and development effectiveness costs to be charged to the project are defined in the Executive Board decision DP/2010/32

[13] Changes to a project budget affecting the scope (outputs), completion date, or total estimated project costs require a formal budget revision that must be signed by the project board. In other cases, the UNDP programme manager alone may sign the revision provided the other signatories have no objection. This procedure may be applied for example when the purpose of the revision is only to re-phase activities among years.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Bhutan				
Output 1: Stakeholder consultation Awareness programs developed and deployed to support behavior change in schools, colleges, business enterprises and monasteries	40,000	25,000	25,000	90,000
Output 2: BEP/BAT Increase plastic waste collection through deployment of best environmental practices and technologies such as compactor trucks, and value addition machines	120,000	211,515	186,515	518,030
Output 3: National Capacities and guidelines Capacity waste handlers (formal and informal) developed in proper segregation and hygiene	50,000	76,991	61,000	187,991
Output 4: Information, outreach and knowledge management Project communication, advocacy and knowledge management	26,000	21,000	29,000	76,000
DPC 3%	5,880	10,890	10,200	26,970
General Management Support (8%)	19,350	27,632	24,937	71,919
Levy (1%)	2,612	3,730	3,367	9,709
Grand Total	**263,843**	**376,758**	**340,019**	**980,619**
Cambodia				
Output 1: Priority business models for plastic alternatives and plastic recycling operationalized,	28,230	75,380	62,215	165,825
Output 2: National capacity enhanced and improved awareness about the plastic crisis and its solutions among citizens and the private sector,	9,501	102,560	132,655	244,716
Output 3: Plastic waste leakage reduced in target provinces and cities,	6,570	319,850	79,485	405,905
Output 4: Project Management Costs	13,310	32,360	59,005	104,675

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

DPC 3%	1,728	16,141	10,001	27,870
General Management Support (8%)	4,747	43,703	27,469	75,919
Coordination Levy (1%)	641	5,900	3,708	10,249
Grand Total	**64,727**	**595,894**	**374,538**	**1,035,159**
India				
Output 1: Stakeholders engaged to scale up and replicate success results in a gender-sensitive manner,	457,068	359,637	182,785	999,490
Output 2: Best Environmental Practices and Best Available Technologies for plastics waste management and circular approaches piloted,	342,588	368,469	257,757	968,814
Output 3: National Capacities, Information and Guidelines on Plastics and Waste Management Strengthened, Gender marker: Gen 2	63,376	51,394	51,394	166,164
Output 4: Information, Outreach and Knowledge Management (including 3% DPC)	295,257	258,502	310,764	864,523
General Management Support (8%)	92,663	83,040	64,216	239,919
UNRCO Levy (1%)	12,510	11,210	8,669	32,389
Grand Total	**1,263,461**	**1,132,253**	**875,585**	**3,271,299**
Indonesia				
Output 1: Increased knowledge, skills, and safety of waste workers within CBOs to enhance their role in the circular economy		565,000	255,000	820,000
Output 2: Improved waste collection systems and recycling rate to support waste workers' livelihoods		567,141	284,347	851,488

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Output 3: Strengthened financial resilience of waste workers by improving access to funding and sustainable business models		200,000	102,715	302,715
Output 4: Strengthened institutional, policy, and regulatory frameworks for integrated and collaborative plastic waste management		340,000	170,000	510,000
Output 5: Effective knowledge management, outreach, and monitoring system for plastic waste management		356,000	177,000	533,000
DPC (3%)		61,144	29,372	90,516
General Management Support (8%)		167,943	80,675	248,618
UNRCO Levy (1%)		22,672	10,891	33,563
Grand Total		2,289,900	1,100,000	3,389,900
Maldives				
Output 1: Stakeholders engaged, data collected, strategies developed and roadmaps established to replicate and scale up successful results from previous TCCF interventions in a gender-sensitive manner,	25,000	25,000	45,000	95,000
Output 2: Best Environmental Practices (BEP) and Best Available Technologies (BAT) for plastics waste management pilot and circular approaches to plastics management assessed, replicated, and/or scaled up, and the accompanying capacities strengthened,	15,000	306,059	465,000	786,059
Output 3: Information, Outreach built, and knowledge management implemented,	10,000	10,000	33,500	53,500
DPC 3%	37,000	41,627	35,805	114,432
General Management Support (8%)	6,960	30,615	46,344	83,919
Coordination Levy (1%)	940	4,133	6,256	11,329

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Grand Total	**94,900**	**417,434**	**631,905**	**1,144,239**
Nepal				
Output 1: Material Recovery Facilities (MRFs) are equipped with processing and management technologies	217,000	184,000	142,000	543,000
Output 2 - Waste workers and communities are empowered with awareness campaigns, skills and livelihood opportunities,	55,000	55,415	51,076	161,491
Project management	56,788	44,352	36,564	137,704
DPC	31,792	32,428	33,076	97,296
Social and Environmental Safeguards Compliance	9500			9,500
General Management Support (8%)	29,606	25,296	21,017	75,919
Coordination Levy (1%)	3,997	3,415	2,837	10,249
Grand Total	**403,683**	**344,906**	**286,571**	**1,035,159**
Philippines				
Output 1: Inclusive, sector-specific business models successfully developed and integrated into the existing waste diversion system, enhancing efficiency and sustainability in plastic waste management of the locality,	70,732	33,732	31,735	136,199
Output 2: Local capacity to improve local plastic waste collection, recovery and recycling strengthened	30,000	30,000	10,000	70,000
Output 3: Plastic recovery and recycling operations of at least two GEDSI/ informal waste picker groups organized and scaled up,	95,833	68,333	25,833	189,999
Output 4: Behavioral change modules for the targeted plastic waste sources developed and implemented,	23,856	23,856	23,858	71,571

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Output 5: Digital application that enables waste diversion tracking with incentives or reward system deployed,	24,000	17,500	17,000	58,500
Project Management	123,315	123,661	125,746	372,722
General Management Support (8%)	29,419	23,767	18,734	71,919
Coordination Levy (1%)	3,972	3,208	2,529	9,709
Grand Total	**401,127**	**324,057**	**255,435**	**980,619**
SRI LANKA				
Output 1: Systemic approach to plastic waste management adopted and practiced at the selected LAs,	46,125	9,000	8,625	63,750
Output 2: BAT/BEP options are introduced to implement strategies developed under Output 1	9,300	675,191	59,000	743,491
Output 3: Implement a phased campaign over the project period (3 years) on plastic pollution prevention and build capacity of LAs and stakeholders,	53,250	33,300	20,000	106,550
Output 4: Implement a phased campaign over the project period (3 years) on plastic pollution prevention and build capacity of LAs and stakeholders,	43,750	77,250	58,700	179,700
Evaluation *(as relevant)*			5,500	5,500
General Management Support (8%)	12,194	63,579	12,146	87,919
Coordination Levy (1%)	1,646	8,583	1,640	11,869
Grand Total	**166,265**	**866,903**	**165,611**	**1,198,779**
VIET NAM	Y1	Y2	Y3	

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Output 1,2: Promote stakeholder engagement, knowledge exchange, awareness raising, and innovation	70,633	70,633	70,634	211,900
Output 2,1: Deployment of waste-back-to-shore scheme in 3 fishing ports	154,666	109,667	108,658	372,991
Output 2,2: Pilot implementation of harmonized plastic responsible sourcing	110,000	40,000	59,600	209,600
Output 3,6, Support the implementation of the regulation on waste sorting at source regulation	15,000	137,000	-	152,000
Output 4,5: Two national communication campaigns	50,000	50,000	-	100,000
Output 4,6, Project Monitoring and Evaluation	11,000	-	18,900	29,900
Direct implementation	40,867	40,867	40,866	122,600
General Management Support (8%)	36,173	35,853	23,893	95,919
Coordination Levy (1%)	4,883	4,840	3,226	12,949
Grand Total	**493,222**	**488,860**	**325,777**	**1,307,859**
Regional				
1: Strengthening joint regional actions.	196,666	46,667	46,666	289,999
2: Provide technical assistance to countries.	46,667	46,667	46,666	140,000
3: Facilitating cross-pollination of knowledge and solutions.	51,667	51,667	51,666	155,000
4: Engaging partners and donors on resources mobilization and collective action.	115,153	115,153	115,153	345,459
5: Providing coordination, monitoring, evaluation, and reporting services to country-based components.	105,000	90,000	155,000	350,000
DPC (3%)	10000	10000	10000	30,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

General Management Support (8%)	42,012	28,812	34,012	104,837
Coordination Levy (1%)	5,672	3,890	4,592	14,153
Grand Total	**572,837**	**392,856**	**463,755**	**1,429,448**
Total Levy	**44,300**	~~**59,557**~~ **82,249**	~~**44,658**~~ **55,549**	~~**148,515**~~ **182,078**
GRAND TOTAL PROJECT	**4,474,279**	~~**6,015,243**~~ **8,305,143**	~~**4,510,478**~~ **5,610,478**	~~**15,000,000**~~ **18,389,900**

Multi-year Budget Breakdown by Outputs and Planned Activities

Regional Component Budget

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3		Funding Source	Budget Description	Amount in USD
1: Strengthening joint regional actions.	1.1 Organize a Project Launch inviting all COs, national stakeholders and TCCF	150,000	0	0		TCCF	Venue and travel	150,000
	1.2 Support COs in their national policy review and assessment and provide technical quality assurance review.	10,000	10,000	10,000		TCCF		30,000
	1.3 Engage dialogues with targeted national and regional counterparts	10,000	10,000	10,000		TCCF		30,000
	1.4 Support regional cooperation to align plastics and wastes policies and regulatory framework	10,000	10,000	10,000		TCCF		30,000
	1.5 Technical assistance and oversight	16,667	16,667	16,667		TCCF		50,000
2: Provide technical assistance to countries.	2.1 Develop and deliver targeted trainings and technical materials to support countries capacity building	10,000	10,000	10,000		TCCF		30,000
	2.2 Develop and propose knowledge and materials to support countries in formulating and/or revising strategies and policies	20,000	20,000	20,000		TCCF		60,000
	2.3 Technical assistance and oversight	16,667	16,667	16,667		TCCF		50,000
3: Facilitating cross-pollination of knowledge and solutions.	3.1 Create and operationalize Thematic Working Groups	-	-	-		TCCF		-
	3.2 Conduct regular virtual meetings & webinars	-				TCCF		-
	3.3 Conduct annual Regional Conferences	25,000	25,000	25,000		TCCF		75,000
	3.4 Online Knowledge-Sharing initiatives	10,000	10,000	10,000		TCCF		30,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3		Funding Source	Budget Description	Amount in USD
	3.5 Technical assistance and oversight	16,667	16,667	16,667		TCCF		50,000
4: Engaging partners and donors on resources mobilization and collective action.	4.1 Stakeholder Mapping and Analysis	40,000	40,000	40,000		TCCF		120,000
	4.2 Support the development of strategic partnership	40,000	40,000	40,000		TCCF		120,000
	4.3 Partnership travel	20,000	20,000	20,000		TCCF		60,000
	4.4 Technical assistance and oversight	15,153	15,153	15,153		TCCF		45,459
5: Providing coordination, monitoring, evaluation, and reporting services to country-based components.	5.1 Project Coordination	55,000	55,000	55,000		TCCF		165,000
	5.2 Terminal Evaluation	-	-	50,000		TCCF		50,000
	5.3 Travel	15,000	15,000	30,000		TCCF		60,000
	5.4 IT Equipment	15,000	0	0		TCCF		15,000
	5.5 Project Assistant	20,000	20,000	20,000		TCCF		60,000
GMS (8%)								104,837
UN Levy (1%)								14,153
DPC								30,000
Total Regional								1,429,449

BANGLADESH

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year							
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount in USD
Output 1: Strengthened collaboration with stakeholders to promote plastic waste circularity Gender marker: GEN2	1.1 Establishing Circularity Hub in collaboration with Industry association and Govt agencies.	-	40,000	-	-	Project + Implementing Partner	TCCF	A central Innovation center (with Public and Private sector partners)	40,000
	1.2 Workshop and policy dialogues on plastic waste management "Addressing the gender issue".	30,000	-	-	-		TCCF	Cost for 3 workshops in three cities	30,000
	1.3 Communication/PR materials production for Communication campaign	15,000	15,000	41,220			TCCF	Comm. /PR material production for 3 cities	71,220

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year							
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount in USD
	Sub-Total for Output 1								
Output 2: Plastics Waste Market System Developed Gender marker: GEN2	2.1 Business model development, and market linkage for CMSMEs involved in plastic waste recycling	100,000	100,000	100,000	-	Project + Implementing Partner	TCCF	cost for business model development and market linkage for 3 cities	300,000
	2.2 Support Waste Collection private organizations to improve the quality and efficiency of waste collection activities	6,000	18,000	32,220	-		TCCF	Cost for capacity enhancement of 10 waste collection organization	56,220
	2.3 Support to Privately owned Materials sorting and segregation facilities	100,000	200,000	-	-		TCCF	cost for equipments	300,000
	2.4 Deliver gender-sensitive training on BEP for plastic collector, sorting and recycling stakeholders to improve capacities to identify and inprove technical practices in handling storing, recycling and disposing of plastic contaminated with POPs flame retardants or other hazardous wastes.	50,000	100,000	50,000	-		TCCF	capacity enhancement of the workforce in plastic waste value chain	200,000
	Sub-Total for Output 2								
Output 3: Gender responsive information and plastic waste traceability mechanism established. Gender marker: GEN2	3.1 Baseline Study on the plastic waste situation in 03 Cities (Chattogram, Cox's Bazar & Tangail)	30,000	60,000	-	-	Project + Implementing Partner	TCCF	3 studies in three cities	90,000
	3.2 Plastic Waste informal sector analysis in the cities including Market Value Chain analysis.	20,000	40,000	-	-		TCCF	3 valuechain analysis in 3 cities	60,000
	3.3 Technology platform (ecopia: online marketplace for plastic waste) development and Maintenance for 3 years including Server	20,000	20,000	36,220	-		TCCF	Cost for server and licensing, upgradation and maintenance	76,220
	3.4 Plastic Waste valuechain actors	30,000	30,000	30,000	-		TCCF	Marchant acquisition drive in 3 cities	90,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year							
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount in USD
	onbording drive to technology platform								
	3.5 Conduct gender analysis (In 03 Cities Chattogram, Cox's Bazar & Tangail) of waste value chain	10,000	20,000	-	-		TCCF	3 studies in three cities	30,000
	Sub-Total for Output 3								
Output 4: Awareness, knowledge, and capacities been developed among urban residents Gender marker: GEN2	4.1 Enhancing Health and safety arrangements of plastic waste worker specially women (and their children) engaged in the plastic waste value chain	50,000	50,000	100,000	-	Project + Implementing Partner	TCCF	Health insurance coverage for PW workers in 3 cities	200,000
	4.2 Gender- Sensitive communication and outreach	52,000	70,000	100,000	-		TCCF	Area specific campaign in 3 cities	222,000
	4.3 Environmental Stewardship Campaign (Community-level Awareness development, including private sector, NGO, local administration)	70,000	100,000	106,220	-		TCCF	Cost for engaging all acrors and citizens of Chattogram, Cox's bazar and Tangail District	276,220
	Sub-Total for Output 4								
Project Management Cost	HR, Administrative support, Quality Assurance								291,055
Sub-total Programme Cost (all Outputs)									2,332,935
DPC (3%)									66,055
General Management Support (8%)									191,919
Levy (1%)									25,909
Grand Total									2,616,819

BHUTAN[14]

[14] Bhutan needs to adjust its annual work plan to match the schedule of transfer from TCCF, that is Year 1-3. There would not be Year 4.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year in USD				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
Output 1: ***Stakeholder consultation*** *Awareness programs developed and deployed to support behavior change in schools, colleges, business enterprises and monasteries.* ***Gender marker: GEN2***	1. *Stakeholder consultation to develop strategy for effective plastic recovery*		10,000	15,000	15,000		*TCCF*	*National consultant to coordinate consultations with private sectors and LGs. and develop*	40,000
	1.2 Promote plastic circular landscape in Bhutan with efficient and effective plastic waste management system in place		30,000	10,000	10,000		*TCCF*	*To provide advocacy programs in 4 hotels, 4 schools, 2 colleges, and 2 monasteries. Each advocacy program will cost USD 5000.*	50,000
	Sub-Total for Output 1								**90,000**
Output 2: BEP/BAT *Increase plastic waste collection through deployment of best environmental practices and technologies such as compactor trucks, and value addition machines.* ***Gender marker: GEN2***	*2.1 Strengthen and upgrade capacity of the existing mini-MRF procured and deployed (waste trucks & shedder machines).*	120,000	211,515	186,515			*TCCF*	*$55000 per truck * 9 nos* *USD 35000 for shedders machines*	518,030
	Sub-Total for Output 2								**518,030**
Output 3: National Capacities and guidelines *Capacity waste handlers (formal and informal) developed in*	*3.1 Develop GIS database for plastic waste supply chain nationwide*	*40,000*	10,000	10,000	10,000		*TCCF*	*Geo-coding of existing waste facilities in year 1 and track plastic waste collection*	70,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

proper segregation and hygiene. ***Gender marker: GEN2***	*3.2 Develop capacity of informal waste collectors (who are mostly women) by integrating them into the plastics value chain, especially in collection and recycling*	*0*	48,000	10,500	10,500		*TCCF*	*Collection, recovery, sorting, value addition (Roughly 600 waste handlers 300 female and 300 male-scrapers license holders*	69,000
	3.3 Develop and implement business model	10,000	18,991	10,000	10,000		*TCCF*	*SOP/MoU between municipalities and waste handlers on the operation and management of compactors and equipment*	48,991
	Sub-Total for Output 3								**187,991**
Output 4: Information, outreach and knowledge management *Project communication, advocacy and knowledge management* ***Gender marker: GEN2***	*4.1. Project communication, advocacy and knowledge management*	2,500	2,500	5,000	5,000		*TCCF*	*Travel for launch event*	15,000
	4.2. Project Management cost, Monitoring and Evaluation	13,500	18,500	14,500	4,500		*TCCF*		51,000
	4.3 Conduct SESP and ESMP of the project	10,000							10,000
	Sub-Total for Output 4								**76,000**
DPC (3%)									**26,970**
General Management Support (8%)									**71,919**
Levy (1%)									**9,709**
TOTAL									**980,619**

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

***CAMBODIA*[15]**

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
Output 1: Priority business models for plastic alternatives and plastic recycling operationalized. ***Gender marker: GEN2***	*Activity 1.1. Support design of green financing and economic instruments to support innovative business solutions (e.g., alternatives, reuse, refill, recycling including mixing plastic waste into asphalt production)*	8,400.00	19,600.00	-	-	*001981-UNDP*	*TCCF*	*International Consultants*	28,000.00
		3,600.00	8,400.00	-	-	*001981-UNDP*	*TCCF*	*Local Consultants*	12,000.00
		2,130.00	12,780.00	12,780.00	9,585.00	*001981-UNDP*	*TCCF*	*Contractual Services - Individuals*	37,275.00
		7,500.00	1,000.00	1,000.00	1,000.00	*001981-UNDP*	*TCCF*	*Supplies*	10,500.00
	1.2. Implement CE measures to reduce the usage of SUPs in the hospitality sector	450.00	2,700.00	2,700.00	2,025.00	*001981-UNDP*	*TCCF*	*Contractual Services - Individuals*	7,875.00
		-	3,000.00	-	-	*001981-UNDP*	*TCCF*	*Supplies*	3,000.00
		-	5,000.00	5,000.00	5,000.00	*001981-UNDP*	*TCCF*	*Training, Workshops and Conference*	15,000.00
		2,000.00	2,000.00	2,000.00	2,000.00	*001981-UNDP*	*TCCF*	*Travel and Meeting*	8,000.00
	1.3. Improve the situation of informal waste collectors (who are mostly women) by integrating them into the plastics value chain, especially in collection and recycling	450.00	2,700.00	2,700.00	2,025.00	*001981-UNDP*	*TCCF*	*Contractual Services - Individuals*	7,875.00
		2,700.00	4,200.00	4,200.00	4,200.00	*001981-UNDP*	*TCCF*	*Miscellaneous Expenses*	15,300.00
		-	10,000.00	-	-	*001981-UNDP*	*TCCF*	*Training, Workshops and Conference*	10,000.00
		1,000.00	4,000.00	4,000.00	2,000.00	*001981-UNDP*	*TCCF*	*Travel and Meeting*	11,000.00

[15] needs to adjust its annual work plan to match the schedule of transfer from TCCF, that is Year 1-3. There would not be Year 4.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
	Sub-Total for Output 1	**28,230.00**	**75,380.00**	**34,380.00**	**27,835.00**	**-**	**-**	**-**	**165,825**
Output 2: National capacity enhanced and improved awareness about the plastic crisis and its solutions among citizens and the private sector. ***Gender marker: GEN2***	*2.1. Conduct gender sensitive strategic communication and awareness raising using social media and websites*		22,500.00	15,000.00	7,500.00	*001981-UNDP*	*TCCF*	*Local Consultants*	45,000.00
		2,410.00	14,460.00	14,460.00	10,845.00	*001981-UNDP*	*TCCF*	*Contractual Services - Individuals*	42,175.00
		3,000.00	3,000.00	3,000.00	3,000.00	*001981-UNDP*	*TCCF*	*Audio Visual&Print Prod Costs*	12,000.00
	2.2. Raise awareness among the public and private sector to promote 4Rs	450.00	2,700.00	2,700.00	2,025.00	*001981-UNDP*	*TCCF*	*Contractual Services - Individuals*	7,875.00
			20,000.00	10,000.00		*001981-UNDP*	*TCCF*	*Training, Workshops and Conference*	30,000.00
	2.3. Outreach schools and temples through schools and pagoda schemes		30,000.00	30,000.00	15,000.00	*001981-UNDP*	*TCCF*	*Local Consultants*	75,000.00
		450.00	2,700.00	2,700.00	2,025.00	*001981-UNDP*	*TCCF*	*Contractual Services - Individuals*	7,875.00
		2,200.00	3,200.00	3,200.00	3,200.00	*001981-UNDP*	*TCCF*	*Miscellaneous Expenses*	11,800.00
		991	2,000.00	2,000.00	2,000.00	*001981-UNDP*	*TCCF*	*Travel and Meeting*	6,991.00
			2,000.00	2,000.00	2,000.00	*001981-UNDP*	*TCCF*	*Audio Visual& Print Prod Costs*	6,000.00
	Sub-Total for Output 2	**9,501.00**	**102,560.00**	**85,060.00**	**47,595.00**	**-**	**-**	**-**	**244,716**
Output 3: Plastic waste leakage reduced in target provinces and cities. ***Gender marker: GEN2***	*3.1. Install plastic waste equipment (water filtration equipment, bins, water dispensers…etc) to implement circular plastic initiatives to support waste segregation,*	2,410.00	14,460.00	14,460.00	10,845.00	*001981-UNDP*	*TCCF*	*Contractual Services - Individuals*	42,175.00
			106,430.00			*001981-UNDP*		*Supplies*	106,430.00

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
	collection and recycling								
	3.2. Implement "Beat Plastic Pollution Innovation Challenges" and promotion of alternatives and recycling	675.00	4,050.00	4,050.00	3,037.50	*001981-UNDP*	*TCCF*	*Contractual Services - Individuals*	11,812.50
			160,000.00			*001981-UNDP*	*TCCF*	*Contractual Services- Companies*	160,000.00
			2,000.00	2,000.00	2,000.00	*001981-UNDP*	*TCCF*	*Audio Visual&Print Prod Costs*	6,000.00
	3.3. Enhance the knowledge and capacity of subnational governments for sound waste management		9,000.00			*001981-UNDP*	*TCCF*	*Local Consultants*	9,000.00
		2,285.00	13,710.00	13,710.00	10,282.50	*001981-UNDP*	*TCCF*	*Contractual Services - Individuals*	39,987.50
			3,000.00	3,000.00	3,000.00	*001981-UNDP*	*TCCF*	*Contractual Services- Companies*	9,000.00
		1,200.00	3,200.00	3,200.00	2,200.00	*001981-UNDP*	*TCCF*	*Miscellaneous Expenses*	9,800.00
			2,000.00	2,000.00	2,000.00	*001981-UNDP*	*TCCF*	*Training, Workshops and Conference*	6,000.00
			2,000.00	2,000.00	1,700.00	*001981-UNDP*	*TCCF*	*Travel and Meeting*	5,700.00
	Sub-Total for Output 3	6,570.00	319,850.00	44,420.00	35,065.00	-	-	-	**405,905.00**
Output 4: Project Management Costs	*Project Management Costs*	12,500.00	27,500.00	27,500.00	23,000.00	*001981-UNDP*	*TCCF*	*Staff Mgmt Costs - IP Staff*	90,500.00
		690.00	4,140.00	4,140.00	3,105.00	*001981-UNDP*	*TCCF*	*Contractual Services - Individuals*	12,075.00
		120.00	720.00	720.00	540.00	*001981-UNDP*	*TCCF*	*Miscellaneous Expenses*	2,100.00
	Sub-Total for Output 4	**13,310.00**	**32,360.00**	**32,360.00**	**26,645.00**	-	-	-	**104,675.00**
DPC (3%)									27,870

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
General Management Support	GMS 8%								75,919
Coordination Levy (1%)									10,249
Grand total						**-**	**-**	**-**	**1,035,159**

INDIA

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount (USD)
Output 1: Stakeholders engaged to scale up and replicate success results in a gender-sensitive manner. **Gender marker: Gen 2**	1.1. Establish a platform for consultations and networking, standards	103,114	103,114	65,614		UNDP	TCCF		271,842
	1.2 Support 10,000 waste workers to enroll in Government social protection systems	47,927	119,818	71,891		UNDP	TCCF		239,636
	1.3 Awareness and Outreach to 50,000 waste workers on rights and entitlements through Helpline	279,703	115,158	33,564		Ministry of Social Justice and Empowerment/ NSKFDC	TCCF		428,425
	1.4 Create Mobile Facilitation Vans for institutionalising services in the community	26,324	21,547	11,716		UNDP	TCCF		59,587

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount (USD)
	Sub-Total for Output 1	457,068	359,637	182,785					999,490
Output 2: Best Environmental Practices and Best Available Technologies for plastics waste management and circular approaches piloted. **Gender marker: Gen 2**	2.1 Implement pilots on value chains and human rights approaches with Recyclers and Value Chain Actors to source recycled plastic responsibly	170,621	184,520	73,808		UNDP	TCCF		428,949
	2.2 Consultants	66,527	66,527	66,527		UNDP	TCCF		199,581
	2.3 Stakeholder Engagement and Partnership Building	11,982	71,891	71,891		UNDP	TCCF		155,764
	2.4 Technology and Innovation Support	71,891	23,964	23,964		UNDP	TCCF		119,819
	2.5 Contingency Fund	21,567	21,567	21,567		UNDP	TCCF		64,701
	Sub-Total for Output 2	342,588	368,469	257,757					968,814
Output 3: National Capacities, Information and Guidelines on Plastics and Waste Management Strengthened. **Gender marker: Gen 2**	3.1 Awareness and Advocacy Programmes with Govt and Other stakeholders	11,982	11,982	11,982		UNDP	TCCF		35,946
	3.2 Development of national guidelines and policy briefs	7,988	7,988	7,988		UNDP	TCCF		23,964
	3.3 Develop tools and frameworks to report data and transparency	17,973	5,991	5,991		UNDP	TCCF		29,955

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount (USD)
	3.4 Research and Policy Consultant	25,433	25,433	25,433		UNDP	TCCF		76,299
	Sub-Total for Output 3	63,376	51,394	51,394					166,164
Output 4: Information, Outreach and Knowledge Management	4.1 Awareness Campaigns for end users and private sector stakeholders (AV, Influencer Marketing, Social Media, Programme Visibility)	9,985	9,985	9,985		UNDP	TCCF		29,955
	4.2 Project Monitoring and Evaluation (QA visits, baseline, endline, Impact assessment, SES, Reports and Documentation)	61,906	37,942	91,860		UNDP	TCCF		191,708
	4.3 PMU	188,603	179,452	184,835		UNDP	TCCF		552,890
	4.4 Direct Project Cost (3%)	34,763	31,123	24,084		UNDP	TCCF		89,970
	Sub-Total for Output 4	295,257	258,502	310,764					864,523
	Sub-Total (Output 1+2+3+4)	1,158,289	1,038,002	802,700					2,998,991
General Management Support (8%)									239,919
Levy (1%)									32,389
GRAND TOTAL									**3,271,299**

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

INDONESIA

Expected Outputs	Planned Activities	Year 1	Year 2	Year 3	Budget Description	Amount
Output 1: Increased knowledge, skills, and safety of waste workers within CBOs to enhance their role in the circular economy.	1.1 Establish a Baseline on Waste Workers and Plastic Waste Management Practices in Selected Areas		80,000	-	Consultant Fee, Travel, Training	80,000
	1.2 Develop and disseminate educational materials (e.g., handbooks, guidelines, online resources) on sustainable plastic waste management		255,000	130,000	Consultant Fee, Materials & Goods, Supplies, Service Contract - Project Management	385,000
	1.3 Provide occupational safety training and access to better equipment for waste workers.		230,000	125,000	Training, Materials & Goods, Facilities& Administration, Information Technology Equipment	355,000
	Sub-Total for Output 1		565,000	255,000		820,000
Output 2: Improved waste collection systems and recycling rate to support waste workers' livelihoods	2.1 Strengthen waste collection, segregation, and recycling systems through technical assistance, infrastructure support, and operational improvements.		274,488	108,288	Facilities & Administration, Materials & Goods, Supplies	382,776
	2.2 Pilot and scale up best practices in waste collection, ensuring the waste is collected from its source and benefits waste workers directly.		292,653	176,060	Service Contract - Project Management, Training, Materials & Goods, Travel	468,713
	Sub-Total for Output 2		567,141	284,347		851,488
Output 3:	3.1 Facilitating Co-Financing and Multi-Stakeholder		200,000	102,715	Workshops and Conference, Facilities & Administration, Consultant Fee, Travel	302,715

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

	Partnerships through Structured Coordination					
Strengthened financial resilience of waste workers by improving access to funding and sustainable business models	**Sub-Total for Output 3**		200,000	102,715		302,715
Output 4: Strengthened institutional, policy, and regulatory frameworks for integrated and collaborative plastic waste management	4.1 Review and strengthen existing policies and regulations to enhance the rights and protections of waste workers, while promoting their formal integration into the waste management workforce.		165,000	70,000	Consultant Fee, Workshops and Conference, Travel	235,000
	4.2 Strengthen the TKN PSL Secretariat for regulatory advocacy and expand labor protections to integrate waste workers into the formal waste management workforce.		175,000	100,000	Service Contract - Project Management, Facilities & Administration, Travel	275,000
	Sub-Total for Output 4		340,000	170,000		510,000
Output 5: Effective knowledge management, outreach, and monitoring system for plastic waste management.	5.1 Strengthen and integrate existing digital platforms to enhance real-time tracking, reporting, and coordination among waste workers, communities, government agencies, and private sector actors.		170,000	80,000	Information Technology Equipmt, Service Contract - Project Management, Consultant Fee	250,000
	5.2 Implement public engagement campaigns		156,000	77,000	Workshops and Conference, Supplies, Materials & Goods, Travel, Consultant fee	233,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

	through social media, community workshops, and interactive forums to raise awareness, encourage participation, and promote behavior change in waste management practices.					
	5.3 Social and Environmental Assessments (ESMP, ESMF, ESIA)		30,000	20,000	Service Contract - Project Management, Consultant Fee	50,000
	Sub-Total for Output 5		356,000	177,000		533,000
Sub Total Output (1+2+3+4+5)			2,038,141	979,062		3,017,203
DPC (3%)			61,144	29,372		90,516
GMS (8%)			167,943	80,675		248,618
LEVY (1%)			22,672	10,891		33,563
GRAND TOTAL			2,289,900	1,100,000		3,389,900

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

MALDIVES

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
Output 1: Stakeholders engaged, data collected, strategies developed and roadmaps established to replicate and scale up successful results from previous TCCF interventions in a gender-sensitive manner. **Gender marker: 2**	*1.1 Conduct Waste Management Workshops in 3 regions of Maldives (North, Central and South) with key stakeholders to showcase best practices, explore local level context (challenges and opportunities) and discuss standardization of plastic waste management.*	10,000.00					*TCCF*	*Procure technical assistacne (local consutlant) Cost includes travels and other logisitcs*	*10,000*
		10,000.00	10,000.00	10,000.00			*TCCF*	*Travel*	*30,000*
			10,000.00	30,000.00			*TCCF*	*Training, workshop and conference*	*40,000*
		5,000.00	5,000.00	5,000.00				*NPSA position(s) for overall support to the project across activities.*	*15,000*
	Sub-Total for Output 1	**25,000**	**25,000**	**45,000**					**95,000**
Output 2: Best Environmental Practices (BEP) and Best Available Technologies (BAT) for plastics waste management pilot and circular approaches to plastics management	*2.1 Identify, document, and amplify Best Environment Practices at local level through Best Available Technology support grant(s)*			10,000.00				*Photography consultant to document best practices across Maldives (selected islands).*	*10,000*
			1,059.48					*Travel costs associated with M&E and Comms work.*	*1,059,48*
				10,000.00				*Grant(s) for local level interventions to enhance/accelerate waste management practices through best available technologies.*	*10,000*
		5,000.00	5,000.00	5,000.00				*NPSA position(s) for overall support to the project across activities.*	*15,000*
	2.2 Plastic processing (washing, flaking and		20,000.00					*Local consultant to undertake SES*	*20,000.00*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
assessed, replicated, and/or scaled up, and the accompanying capacities strengthened. **Gender Marker: 2**	*palletizing) pilots in Southern Regional Waste Collection Center (covering GA, GDh, Gn, S Atolls) and Northern Waste Collection Center (covering Ha, HDh, Sh, N, R, B, Lh, Atolls) to enhance plastic waste management and recycling in the region*							*Screening, ESIA and formulate ESMP and SEP. 2 sites Addu and Vandhoo.*	
			150,000.00	70,000.00				*Procurement of plastic sorting, washing, flaking and palletizing machine with training. Construction of housing for machine and processed plastic (pallets). Addu and Vandhoo.*	*220,000.00*
			10,000.00	10,000.00				*Travel costs associated with M&E and Comms work. (Including inauguration event).*	*20,000.00*
		5,000.00	5,000.00	5,000.00				*NPSA position(s) for overall support to the project across activities.*	*15,000*
	2.3 Provision of electric vehicles and renewable energy infrastructure to the Waste Management Corporation		80,000.00					*Contractual Services, Companies*	*80,000.00*
			30,000.00	160,000.00				*Contractual Services, Companies*	*190,000.00*
				190,000.00				*Contractual Services, Companies*	*190,000.00*
		5,000.00	5,000.00	5,000.00				*NPSA position(s) for overall support to the project across activities.*	*15,000*
	Sub-Total for Output 2	**15,000.00**	**306,059.48**	**465,000.00**		**-**	**-**	**-**	**786,059.48**
Output 3: Information, Outreach built, and knowledge management implemented. **Gender Marker: 2**	*3.1 Information and Guidelines on Plastics and Waste Management Strengthened on a gender-responsive manner*			9,000.00				*onsultant to develop and conduct gender responsive training for waste management staff.*	*9,000.00*
		5,000.00	5,000.00	5,000.00				*NPSA position(s) for overall support to the project across activities.*	*15,000*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
	3.2 Translate and upload training modules to the local council learning portal.			14,500.00				Company to translate, adapt and upload regional training materials into local council learning portal.	*14,500.00*
		5,000.00	5,000.00	5,000.00				NPSA position(s) for overall support to the project across activities.	*15,000.00*
	Sub-Total for Output 3	**10,000.00**	**10,000.00**	**33,500.00**		**-**	**-**	**-**	***53,500.00***
DPC		37,000	41,627	35,805				For general operational services for processsing project ralated activities.	*114,431*
General Management Support (8%)								As set in the regional project	*83,919*
Coordination Levy (1%)									*11,329*
Grand total									**1,144,239**

NEPAL

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
Output 1: Material Recovery Facilities (MRFs) are equipped with processing and management technologies	1.1 Establish or Strengthen MRFs with processing and management technology	205,000	175,000	136,000		UNDP		Grants, travel, workshop, national consultant	516,000
	1.2 Develop or revise business plans and SOPs for the effective functioning of the MRFs	12,000	9,000	6,000		UNDP		National consultant, workshop, travel	27,000
	Sub-Total Output 1	217,000	184,000	142,000		-	-	-	543,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
Output 2 - Waste workers and communities are empowered with awareness campaigns, skills and livelihood opportunities. ***Gender marker: GEN2***	2.1. Provide trainings and equipment to the waste workers for occupation safety and livelihood support	41,500	40,815	38,690		UNDP		Grants, travel, workshop, national consultant	121,005
	2.2Conduct awareness programs on sustainable waste management including recycling and upcycling.	13,500	14,600	12,386		UNDP		Grants, travel, workshop, national consultant	40,486
	Sub Total Output 2	55,000	55,415	51,076		-	-	-	161,491
Project management	Project Implementation and Management (Staff, equipment, rent, operations cost)	56,788	44,352	36,564		UNDP			137,704
DPC		31,792	32,428	33,076		**UNDP**			97,296
Social and Environmental Safeguards Compliance									9,500
GMS	General Management Support								75,919
Levy (1%)									10,249
Grand total									**1,035,159**

PHILIPPINES

EXPECTED OUTPUTS	***PLANNED ACTIVITIES***	***Planned Budget by Year***			***RESPONSIBLE PARTY***	***PLANNED BUDGET***		
		Y1 (No24-Oct25)	*Y2 (Nov25-Oct26)*	*Y3 (Nov26-Oct27)*		*Funding Source*	*Budget Description*	*Amount*
Output 1: *Inclusive, sector-specific business models successfully developed and*	*1.1 Engage with key LGU officials and offices to scope the inclusive business model for the targeted collection and recovery of plastic waste from specific sources*	20,732	20,732	20,735	*UNDP*	*TCCF*	*LOE of Social Innovation Analyst (50%)*	62,199
						TCCF	*LOE of ALab Head of Solutions Mapping (10%)*	0

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1 (No24-Oct25)	Y2 (Nov25-Oct26)	Y3 (Nov26-Oct27)		Funding Source	Budget Description	Amount
integrated into the existing plastic waste diversion system, enhancing efficiency and sustainability in plastic waste management of the locality. ***Gender marker: 2***	*1.2 Co-create with the LGU, startups, MSMEs, and NGOs of circular business models that are innovative and financially sustainable towards the targeted collection and recovery of plastic waste*	5,000	5,000	5,000	*UNDP*	*TCCF*	*Travel and Accommodation (DSA)*	15,000
		5,000	5,000	3,000	*UNDP*	*TCCF*	*Co-Creation Workshops*	13,000
	1.3 Prototype and test targeted collection and recovery of plastic and other wastes from specific sources linked to the overall waste diversion system of the LGU. (2 winners)	40,000			*UNDP*	*TCCF*	*Seed Capital/Innovation Challenge Fund*	40,000
	1.4 Sustain and scale up plastic recovery business models linked to the overall waste diversion system of the LGU		3,000	3,000	*UNDP*	*TCCF*	*Sustainability Workshops*	6,000
	Sub-Total for Output 1	70,732	33,732	31,735				136,199
Output 2: *Local capacity to improve local plastic waste collection, recovery and recycling strengthened.* ***Gender marker: 2***	*2.1 Inception workshops and baselining*	3,000			*UNDP*	*TCCF*	*International Travel*	3,000
		10,000			*UNDP*	*TCCF*	*Workshops*	10,000
		7,000			*UNDP*	*TCCF*	*Travel and Accommodation (DSA)*	7,000
	2.2 Assess implementation of local policies on plastic, and solid waste management and practices and identify recommendations to mainstream/enhance plastic circular economy and alignment with EPR	5,000	10,000		*UNDP*	*TCCF*	*Individual Consultant*	15,000
		5,000	20,000	10,000	*UNDP*	*TCCF*	*Meetings, Consultations, Workshops*	35,000
						TCCF	*Travel and Accommodation (DSA)*	0

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1 (No24-Oct25)	Y2 (Nov25-Oct26)	Y3 (Nov26-Oct27)		Funding Source	Budget Description	Amount
	Sub-Total for Output 2	30,000	30,000	10,000				70,000
Output 3: Plastic recovery and recycling operations of at least two GEDSI/ informal waste picker groups organized and scaled up. **Gender marker: 3**	3.1 Implement targeted trainings designed to equip GEDSI groups with skills in safe and dignified plastic waste collection, recovery and recycling techniques, entrepreneurial skills and business operations.	25,833	28,333	15,833	UNDP	TCCF	Meetings, Consultations, Workshops	69,999
						TCCF	Travel and Accommodation (DSA)	0
						TCCF	Individual Consultant	0
	3.2 Establish community storage/recovery facilities for plastic collection, recovery, and recycling.	40,000	40,000	10,000	UNDP	TCCF	Equipment	90,000
	3.3 Conduct SESP and ESMP	30,000				TCCF	Individual Consultant	30,000
	Sub-Total for Output 3	95,833	68,333	25,833				189,999
Output 4: Behavioral change modules for the targeted plastic waste sources developed and implemented. **Gender marker: 2**	4.1 Conduct consultations and other field research to understand current behaviors on waste and consumption in target localities	19,523	19,523	19,525	UNDP	TCCF	Travel and Accomodation (DSA)	5,000
							LOE of Social Innovation Analyst (50%)	38,571
						TCCF	Meetings and Workshops	15,000
	4.3 Implement SBCC plan including delivery of training and dissemination of SBCC materials	4,333	4,333	4,333	UNDP	TCCF	AV & Print Production Costs	8,000
						TCCF	Travel and Accommodation (DSA)	5,000
	Sub-Total for Output 4	23,856	23,856	23,858				**71,571**
Output 5: Digital application that enables waste diversion	5.1 Develop an M&E Framework and Reporting system	9,000			UNDP	TCCF	Individual Consultant (Local)	9,000
	5.2 Review and enhance digital waste tracker, and	10,000	10,000	10,000			Individual Consultant	30,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year			RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1 (No24-Oct25)	Y2 (Nov25-Oct26)	Y3 (Nov26-Oct27)		Funding Source	Budget Description	Amount
tracking with incentives or reward system deployed. ***Gender marker: 2***	*connect to LGU monitoring dashboard*							
	5.3 Consultation and trainings on waste digital tracker	5,000	7,500	7,000	*UNDP*	*TCCF*	*Consultation Meetings*	*2,000*
						TCCF	*LOE of Digitalization Specialist (10%)*	*14,500*
						TCCF	*Travel and Accommodation (DSA)*	*3,000*
	Sub-Total for Output 5	**24,000**	**17,500**	**17,000**				***58,500***
Project Management	*Staff Salaries*	43,565	43,565	43,565	*UNDP*	*TCCF*	*Project Manager - NPSA 11*	*130,695*
		23,694	23,694	23,694		*TCCF*	*Project Analyst - NPSA 9*	*71,083*
		17,095	17,095	17,095		*TCCF*	*Communications Associate - NPSA 7*	*51,286*
		14,865	14,861	14,861	*UNDP*	*TCCF*	*Field Coordinator - NPSA 7*	44,587
		7,430	12,780	14,865	*UNDP*	*TCCF*	*Project Operations Associate - NPSA 7*	35,075
	DES Staff	6,666	6,666	6,666	*UNDP*	*TCCF*	*Staff Management Cost*	*20,000*
	DES GOE	5,000	5,000	5,000	*UNDP*	*TCCF*	*Miscelaneous Expenses*	*15,000*
	Supplies	5,000			*UNDP*	*TCCF*	*Office Equipment*	*5,000*
	Sub-Total for Project Management	123,315	123,661	125,746				372,722
General Management Support (8%)								71,919
UN Levy (1%)								*9,709*

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	***PLANNED ACTIVITIES***	***Planned Budget by Year***			***RESPONSIBLE PARTY***	***PLANNED BUDGET***		
		Y1 (No24-Oct25)	*Y2 (Nov25-Oct26)*	*Y3 (Nov26-Oct27)*		*Funding Source*	*Budget Description*	*Amount*
GRAND TOTAL								***980,619***

SRI LANKA

EXPECTED OUTPUTS	**PLANNED ACTIVITIES**	**Planned Budget by Year**				**RESPONSIBLE PARTY**	**PLANNED BUDGET**			
		Y1	Y2	Y3	Y4		Funding Source	Budget Code	Budget Description	Amount
Output 1: Systemic approach to plastic waste management adopted and practiced at the selected LAs. ***Gender marker: 2***	*Activity 1.1 Gather and analyze data on the life cycles of locally important plastics, and the status of their operation within circular economic value chains (emphasis on the green network (Haritha Balakaya) established by the Western Province Waste Management Authority (WPWMA)), including past interventions, key gaps, opportunities, gender concerns, etc.*	12,000.00				UNDP	TCCF	71300	Local Consultants	12,000
		3,000.00				UNDP	TCCF	75700	Training, Workshops and Confer	3,000
		3,250.00				UNDP	TCCF	71600	Travel	3,250
	Activity 1.2 Identify the locally relevant strategies and key entry points to transform local plastic consumption and waste management, enhance linked circular economies to bridge gaps, improve efficiencies, strengthen livelihoods (including for women & vulnerable groups), and reduce plastic pollution.	12,000.00				UNDP	TCCF	71300	Local Consultants	12,000
		3,500.00				UNDP	TCCF	75700	Training, Workshops and Confer	3,500
		3,500.00				UNDP	TCCF	71600	Travel	3,500
	Activity 1.3 Establish and strengthen	2,500.00	2,500.00	2,000.00		UNDP	TCCF	75700	Training, Workshops and Confer	7,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET			
		Y1	Y2	Y3	Y4		Funding Source	Budget Code	Budget Description	Amount
	inclusive multistakeholder engagement mechanisms special focus on resource centers/resource banks at the local level to support the LAs and the WPWMA in implementing plastic pollution prevention plans.	125.00	250.00	125.00		UNDP	TCCF	74500	Miscellaneous Expenses	500
	Monitoring	1,750.00	1,750.00	1,750.00		UNDP	TCCF	71600	Travel	5,250
	Direct Project Cost	4,500.00	4,500.00	4,750.00		UNDP	TCCF	64397	Direct Project Cost	13,750
	Sub-Total for Output 1	**46,125.00**	**9,000.00**	**8,625.00**						**63,750**
Output 2: BAT/BEP options are introduced to implement strategies developed under Output 1 ***Gender marker: 2***	*Activity 2.1 Establish 2 MRF facilities based on PPP, equipped with relevant BAT/BEP interventions essential to demonstrate comprehensive plastic pollution prevention strategies developed for the LAs under 1.2.*		372,500.00			UNDP	TCCF	72500	Supplies	372,500
	Activity 2.2 Improve one existing MRF facility by introducing new BAT/BEPs for plastic waste recycling to strengthen the plastic circular economy value chains (i.e., micro-enterprises) and the business model of the MRF.			47,500.00		UNDP	TCCF	72500	Supplies	47,500
	Activity 2.3 Introduce BAT/BEP to strengthen local resource centers or resource banks (i.e, managed by members of Haritha Balakaya) to promote 3R-based actions at the consumer level, especially focusing on improving source		258,900.00			UNDP	TCCF	72500	Supplies	258,900
			1,000.00	1,000.00		UNDP	TCCF	74200	Audio Visual&Print Prod Costs	2,000
			2,500.00	2,500.00		UNDP	TCCF	71600	Travel	5,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET			
		Y1	Y2	Y3	Y4		Funding Source	Budget Code	Budget Description	Amount
	segregation with the active engagement of households and communities.									
	Activity 2.4 Introduce digital solutions, where possible, to improve the efficacy of circular economic interventions, especially to expand the engagement of women, young people, school children, etc., and their networks to learn from and support each other.		30,000.00			UNDP	TCCF	72500	Supplies	30,000
			991.00	1,000.00		UNDP	TCCF	74200	Audio Visual & Print Prod Costs	1,991
		3,050.00	3,050.00			UNDP	TCCF	71600	Travel	6,100
				500.00		UNDP	TCCF	74500	Miscellaneous Expenses	500
	Monitoring	1,750.00	1,750.00	1,750.00		UNDP	TCCF	71600	Travel	5,250
	Direct Project Cost	4,500.00	4,500.00	4,750.00		UNDP	TCCF	64397	Direct Project Cost	13,750
	Sub-Total for Output 2	**9,300.00**	**675,191.00**	**59,000.00**	**-**					**743,491**
Output 3: Implement a phased campaign over the project period (3 years) on plastic pollution prevention and build capacity of LAs and stakeholders. ***Gender marker: 2***	*Activity 3.1 Use analysis under 1.1. to identify past and ongoing capacity-building and information sharing initiatives and campaigns, their gaps and opportunities, including key intermediaries and parties or individuals who can influence others positively.*	2,000.00	2,000.00	1,000.00		UNDP	TCCF	75700	Training, Workshops and Confer	5,000
		1,000.00	1,500.00	1,500.00		UNDP	TCCF	71600	Travel	4,000
	Activity 3.2 Formulate key campaigning strategies, target groups, messages, options, channels, etc.	8,000.00				UNDP	TCCF	74200	Audio Visual & Print Prod Costs	8,000
	Activity 3.3. Develop the three-year campaign plan allowing periodic monitoring, reviews, and revisions.	10,000.00				UNDP	TCCF	71300	Local Consultants	10,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET			
		Y1	Y2	Y3	Y4		Funding Source	Budget Code	Budget Description	Amount
	Activity 3.4 Implement a plastic pollution prevention campaign across the selected local areas engaging the identified key persons/groups of influence and infomediaries.	11,000.00	11,000.00			UNDP	TCCF	72100	Contractual Services-Companies	22,000
	Activity 3.5 Monitor campaign plan to ensure consistency with expected results and use reviews to respond to changes, stakeholder feedback, and campaign results.		5,000.00	5,000.00		UNDP	TCCF	72100	Contractual Services-Companies	10,000
		500.00	1,500.00	1,000.00		UNDP	TCCF	75700	Training, Workshops and Confer	3,000
		1,000.00	2,000.00	2,000.00		UNDP	TCCF	71600	Travel	5,000
	Activity 3.6 Develop a capacity building and training plan based on gaps and strengths identified under 1.1.	10,000.00				UNDP	TCCF	71300	Local Consultants	10,000
	Activity 3.7 Conduct training and capacity building targeting the identifies stakeholders and actors, including facilitating links (i.e., with financing opportunities to adopt BAT/BEP).	2,000.00	2,500.00	2,000.00		UNDP	TCCF	75700	Training, Workshops and Confer	6,500
		1,500.00	1,550.00	500.00		UNDP	TCCF	71600	Travel	3,550
				500.00		UNDP	TCCF	74500	Miscellaneous Expenses	500
	Monitoring	1,750.00	1,750.00	1,750.00		UNDP	TCCF	71600	Travel	5,250
	Direct Project Cost	4,500.00	4,500.00	4,750.00		UNDP	TCCF	64397	Direct Project Cost	13,750
	Sub-Total for Output 3	**53,250.00**	**33,300.00**	**20,000.00**	**-**					**106,550**
Output 4: Implement a phased campaign over the project period (3 years) on plastic	*Activity 4.1 Extract lessons and best practices, including gender related learning, focusing on but not limiting to, monitoring and reviews.*	23,000.00	22,000.00	24,000.00		UNDP	TCCF	71400	Contractual Services - Individuals	69,000
			10,000.00			UNDP	TCCF	71300	Local Consultants	10,000
		2,000.00	3,000.00	3,000.00		UNDP	TCCF	71600	Travel	8,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET			
		Y1	Y2	Y3	Y4		Funding Source	Budget Code	Budget Description	Amount
pollution prevention and build capacity of LAs and stakeholders. ***Gender marker: 2***	*Activity 4.2 Develop inclusive knowledge/information sharing tools and guidelines.*	1,000.00	2,000.00	2,000.00		UNDP	TCCF	74200	Audio Visual&Print Prod Costs	5,000
	Activity 4.3 Develop knowledge-sharing material and strategies/plans.		10,000.00			UNDP	TCCF	72100	Contractual Services-Companies	10,000
		2,500.00	2,500.00	3,200.00		UNDP	TCCF	72500	Supplies	8,200
		5,000.00	5,000.00	5,000.00		UNDP	TCCF	75700	Training, Workshops and Confer	15,000
		4,000.00	4,000.00	2,000.00		UNDP	TCCF	71600	Travel	10,000
	Activity 4.4 Implement knowledge-sharing plans targeting all 341 LAs in Sri Lanka and all key stakeholders.		7,500.00	7,500.00		UNDP	TCCF	75700	Training, Workshops and Confer	15,000
			5,000.00	5,000		UNDP	TCCF	71600	Travel	10,000
				500		UNDP	TCCF	74500	Miscellaneous Expenses	500
	Monitoring	1,750	1,750	1,750		UNDP	TCCF	71600	Travel	5,250
	Direct Project Cost	4,500	4,500	4,750		UNDP	TCCF	64397	Direct Project Cost	13,750
	Sub-Total for Output 4	**43,750**	**77,250**	**58,700**	**-**					**179,700**
Evaluation *(as relevant)*				5,500		UNDP	TCCF	71200	International Consultant	5,500
GMS (8%)										87,919.26
Levy (1%)										11,869.10
Total Direct Cost		176,488	858,320	163,971						1,198,779

VIET NAM[16]

[16] needs to adjust its annual work plan to match the schedule of transfer from TCCF, that is Year 1-3. There would not be Year 4.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
Output 1.2: Promote stakeholder engagement, knowledge exchange, awareness raising, and innovation *Gender marker: Gen2*	*1.2.1 Promote sharing of lesson learnt, experiences and best practices on EPR, waste sorting at source, alternative materials, and related topics through regional conferences and national dialogues through NPAP platform.*		9,000	9,000	9,000	UNDP	TCCF		27,000
	1.2.2 Foster collaboration among innovation enablers to develop NPAP plastic innovation ecosystem through plastic innovation mapping, capacity building, and innovator-investment matchmaking.		21,633	21,633	21,633	UNDP	TCCF		64,900
	1.2.3. Invest in nurturing the incubation of at least 06 locally-led innovation solutions addressing plastic pollution through the NPAP platform, in collaboration with academia and experts in innovation and entrepreneurship.		40,000	40,000	40,000	UNDP	TCCF		120,000
	MONITORING								
								Sub-Total for Output 1.2	**211,900**
Output 2.1: Deployment of waste-back-to-shore scheme in 3 fishing ports	*2.2.1 Assess waste management and design plastic-waste-back-to-shore schemes for the selected three fishing ports for consultation and agreement with localities.*	15,000	30,000			UNDP	TCCF		45,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
Gender marker: Gen 2	*2.2.2 Draft regulation, develop training materials and organize training programme on plastic waste collection for fishermen and relevant stakeholders.*		25,000	25,000	25,000	UNDP	TCCF		75,000
	2.2.3 Implement the pilots of plastic-waste-back-to-shore schemes at the selected fishing ports, including (i) delivery of tools and infrastructure for waste collection and recycling, (ii) establishing a mechanism to collect, transport, and sort plastics and other recyclables at ports, engaging informal waste workers, (iii) tracking volume of plastic waste collected, (iv) executing communication activities to support the initiative, (v) monitoring and evaluation.		74,667	74,667	74,666	UNDP	TCCF		224,000
	2.2.4 Monitor and evaluate the pilot implementation, develop exist strategy for sustainability and replication.		10,000	10,000	8,991	UNDP	TCCF		28,991
	Sub-Total for Output 2.1								**372,991**
Output 2.2: Pilot implementation of harmonized plastic responsible sourcing	*2.2.1 Conduct mapping of plastic recycling in the North for selection of specific recycled plastic value chains to be targeted within the Project.*		20,000			UNDP	TCCF		20,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
Gender marker: Gen 2	*2.2.2 Conduct baseline survey to assess the current status, gaps, and opportunities implementation of the Responsible Sourcing Framework in selected recycled plastic value chains, connected to 1-2 specific recyclers.*		50,000			UNDP	TCCF		50,000
	2.2.3 Develop and implement a harmonized responsible sourcing framework within the plastic recycling value chains, delivering benefits to informal waste workers		40,000	40,000	59,600	UNDP	TCCF		139,600
	Sub-Total for Output 2.2								**209,600**
Output 3.6. Support the implementation of the regulation on waste sorting at source regulation	*3.6.1. Review waste sorting at source plans issued by Hanoi and HCMC, develop recommendations for improvement and implementation.*		15,000			UNDP	TCCF		15,000
	3.6.2 Provide additional support to infrastructure such as bins/bags in selected districts/wards of Ha Noi and HCMC, in synergy with other programs run by UNDP.			90,000		UNDP	TCCF		90,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
	3.6.3 Develop innovative measures to monitor compliance, implement incentive programs for communities, businesses, and individual who consistently comply with waste sorting regulations.			30,000		UNDP	TCCF		30,000
	3.6.4 Provide training for municipal workers, waste collectors, and enforcement officers on the waste sorting process and the importance of compliance.			17,000		UNDP	TCCF		17,000
	Sub-Total for Output 3.6								**152,000**
Output 4.5: Two national communication campaigns *Gender marker: Gen 2*	*4.5.1 Conduct campaigns to raise awareness on plastic waste pollution at the national level and in Ha Noi, Ho Chi Minh city and other cities (to be identified after consulting with government partners)*		50,000			UNDP	TCCF		50,000
	4.5.2 Organize city level campaigns/initiative targeting schools, business, shopping centers to promote waste sorting at source and engage local joint forces for tackling plastic pollution			50,000		UNDP	TCCF		50,000
	Sub-Total for Output 4.5								**100,000**
Output 4.6. Project Monitoring and Evaluation	*4.6.1. Develop an M&E framework, conduct baseline studies, and document lessons learned and success stories.*		11,000			UNDP	TCCF		11,000

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

EXPECTED OUTPUTS	PLANNED ACTIVITIES	Planned Budget by Year				RESPONSIBLE PARTY	PLANNED BUDGET		
		Y1	Y2	Y3	Y4		Funding Source	Budget Description	Amount
Gender marker: Gen 2	*4.6.2. Conduct terminal evaluations and organize workshops to share results and lessons learned.*				18,900	UNDP	TCCF		18,900
	Sub-Total for Output 4.6								**29,900**
Direct implementation	Staff cost, travel, desk cost, ISS		40,867	40,867	40,867				122,600
General Management Support (8%)									95,919
UNRC Coordination Levy (1%)									12,949
TOTAL									**1,307,859**

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

VIII. GOVERNANCE AND MANAGEMENT ARRANGEMENTS

The project will be implemented following DIM modality. There is one joint Multi-Country Project Board that oversees the project as the most senior, dedicated oversight body for the project. The two main roles of the project board are as follows:

1. **High-level oversight of the execution of the project by the Implementing Partne**r (as explained in the "Provide Oversight" section of UNDP POPP). This is the primary function of the project board. The Project Board reviews evidence of project performance based on monitoring, evaluation and reporting, including progress reports, monitoring missions' reports, evaluations, risk logs, quality assessments, and the combined delivery report. The Project Board is the main body responsible for taking corrective actions as needed to ensure the project achieves the desired results. Its function includes oversight of annual (and as-needed) assessments of any major risks to the project, and related decisions/agreements on any management actions or remedial measures to address them effectively.
   The Project Board also carries the role of quality assurance of the project taking decision informed by, among other inputs, the project quality assessment. In this role the Board is supported by the quality assurer, whose function is to assess the quality of the project against the corporate standard criteria. This function is performed by a UNDP programme or monitoring evaluation officer to maintain independence from the project manager.
2. **Approval of key project execution decisions** (as explained in the "Manage Change" section of the PPM). The Project Board has an equally important, secondary role in approving certain adjustments above provided tolerance levels, including substantive programmatic revisions (major/minor amendments), budget revisions, requests for suspension or extension and other major changes (subject to additional funding partner/donor requirements).

The Project Board is responsible for making management decisions by consensus when required, including the approval of project plans and revisions, and the project manager's tolerances. The Project Board approves annual work plans and reviews updates to the project risk log.
The Project Board will meet at least on an annual basis,and may meet more often if required. Its responsibilities include:

- Provide overall guidance and direction to the project, ensuring it remains within any specified constraints, and promote gender equality and social inclusion (LNOB) in the project implementation;
- Revie project performance based on monitoring, evaluation and reporting, including standard quality assurance checks, progress reports, risk logs, spot checks/audit reports and the combined delivery report;
- Address any high-level project issues as raised by the project manager and project assurance;
- Provide guidance on emerging and/or pressing project risks and agree on possible mitigation and management actions to address specific risks (including ensuring compliance with UNDP's Social and Environmental Standards, Fraud/corruption, Sexual Exploitation and Abuse and Sexual Harrassment policies);
- Agree or decide on project manager's tolerances as required, within the parameters set by UNDP (Manage Change in the PPM) and the donor, and provide direction and decisions for exceptional situations when the project manager's tolerances are exceeded;
- Advise on major and minor amendments to the project within the parameters set by UNDP and the donor;
- Agree or decide on a project suspension or cancellation, if required;
- Provide high-level direction and recommendations to the project management unit to ensure that the agreed deliverables are produced satisfactorily according to plans;
- Receive and address project level grievance, including overseeing whatever specific compliance and stakeholder response (or grievance) mechanisms have been put in place so that individuals and communities potentially affected by the project have access to effective mechanisms and procedures for raising concerns about the social and environmental performance of the project;
- Engage in the low value grant selection process where there is no Grant Selection Committee, as guided by the Low Value Grants – UNDP Operational Guide.

The Project Board has three categories of formal members (e.g. voting members:

1. **Project Director/Executive:** This is an individual(s) who represents ownership of the project and chairs the Project Board. The Project Executive is: Manager, GPN and Regional Programme
2. **Beneficiary Representative(s):** This is an individual(s) representing the interest of those groups of stakeholders who will ultimately benefit from the project. Their primary function within the Board is to

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

ensure the realization of project results from the perspective of project beneficiaries. The Beneficiary Representatives are: Resident Representatives (or designate) from participating Country Offices, representing the National Advisory Groups they chair.

3. **Development Partner(s):** Individuals representing the interest of the parties concerned that provide funding, strategic guidance and/or technical expertise to the project. The Development Partner representative(s) is: Xiaofang Zhou, Director of Chemicals and Waste Hub, BPPS, UNDP.

Project Advisory Group:
At the country level, Senior Management of the individual CO will set up a Project Advisory Group at the child project level to ensure coordination between various donor and government-funded projects and programmes, and ensure that community and other relevant stakeholders are consulted and included in the decision making related to the project implementation and coordination at national and sub national levels. The National Advisory Group will include direct and indirect beneficiaries of the Project. The national Project Advisory bodies do not supersede the authority of the Regional Project Board, which retains the functions and responsibilities of the Project Board as described above and is the decision-making body of all the child projects under the multi-country project. The national Project Advisory bodies provide inputs and recommendations to support the Project Board's decision making.

Project Assurance:
UNDP performs quality assurance and supports the Project Board, by carrying out objective and independent project oversight and monitoring functions, including compliance with the risk management and social and environmental standards of UNDP. This role ensures appropriate project management milestones are completed, and conflict of interest issues are monitored and addressed. The project assurance function is independent of project execution.
Each participating country office will provide project assurance under the direction of their respective Senior Management. A designated Programme/ M&E Officer in each Country Office will play the project assurance role in line with UNDP corporate rules and regulations. Each individual country office will follow similar structures of project QA. The UNDP BPPS Environment team provides technical quality assurance and strategic oversight of the project, in partnership with the Country Office Support and Quality Assurance (COSQA) team through the respective country desk officers. They will provide their inputs directly to the Regional Programme Management Support Unit, who in turn reports to the Project Board, as well as providing project assurance for the regional component.


Project Management:
Regional: The Bangkok Regional Hub acts as the Coordinating Office and houses the Regional Project Management Team. The Regional Project Management Team for this project, will consist of a Regional Project Coordinator, a communication specialist to provide overall coordination with TCCF and a programme associate to provide administrative and programme support to the Regional Project Management Team.

The Regional Project Coordinator coordinates, on behalf of the Project Board, the day-to-day collaborative efforts at the overall project level. The Regional Project Coordinator plays a key role in coordinating and incorporating the programmatic contributions of all partner countries and is responsible for:


- Compiling joint project reports, with specific inputs from each partner country
- Facilitating communication and coordination among partners
- Preparing and convening the project board meetings
- Facilitating joint activities, as needed, and
- Coordinating and commissioning project evaluations.

The Regional Project Coordinator also manages the regional component of the multi-country project. *Country-level:* Each CO will have a dedicated Project Manager that will be responsible for the day-to-day management of the project, managing all project inputs, supervising project staff, responsible parties, consultants and sub-contractors as well as coordinate the procurement and in country coordination. The project manager will present key deliverables and documents to the board for their review and approval, including progress reports, annual work plans, adjustments to tolerance levels and risk registers.

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

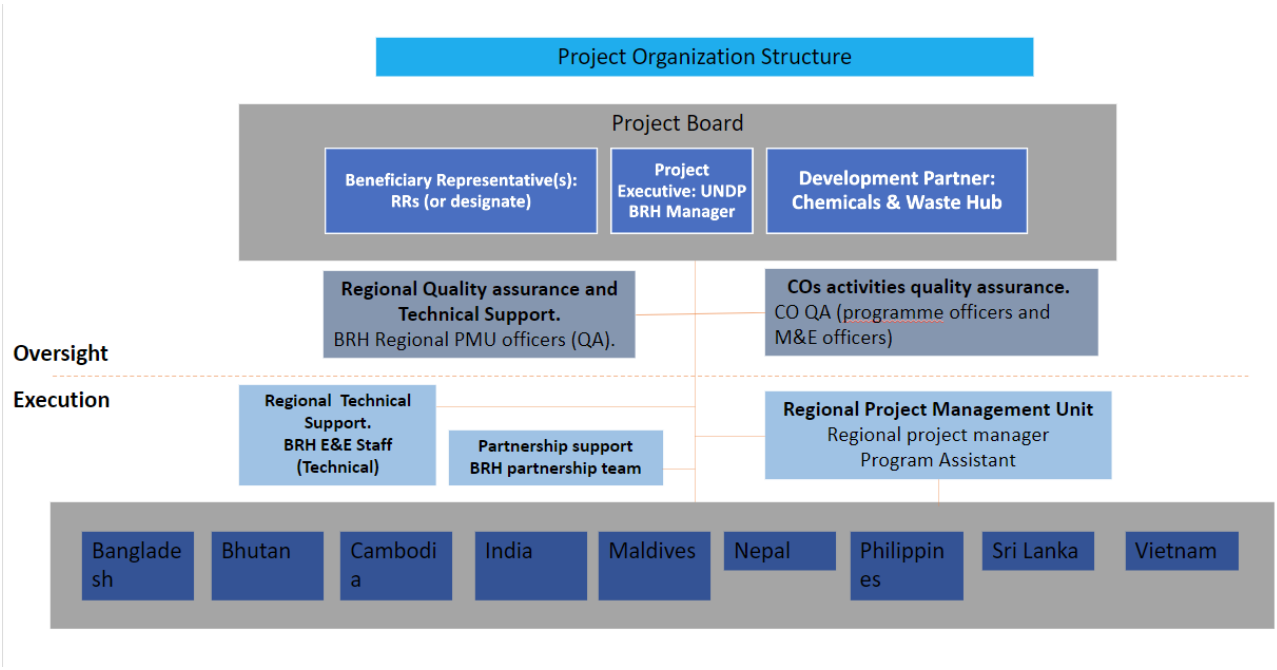

Revised Project Organization Structure

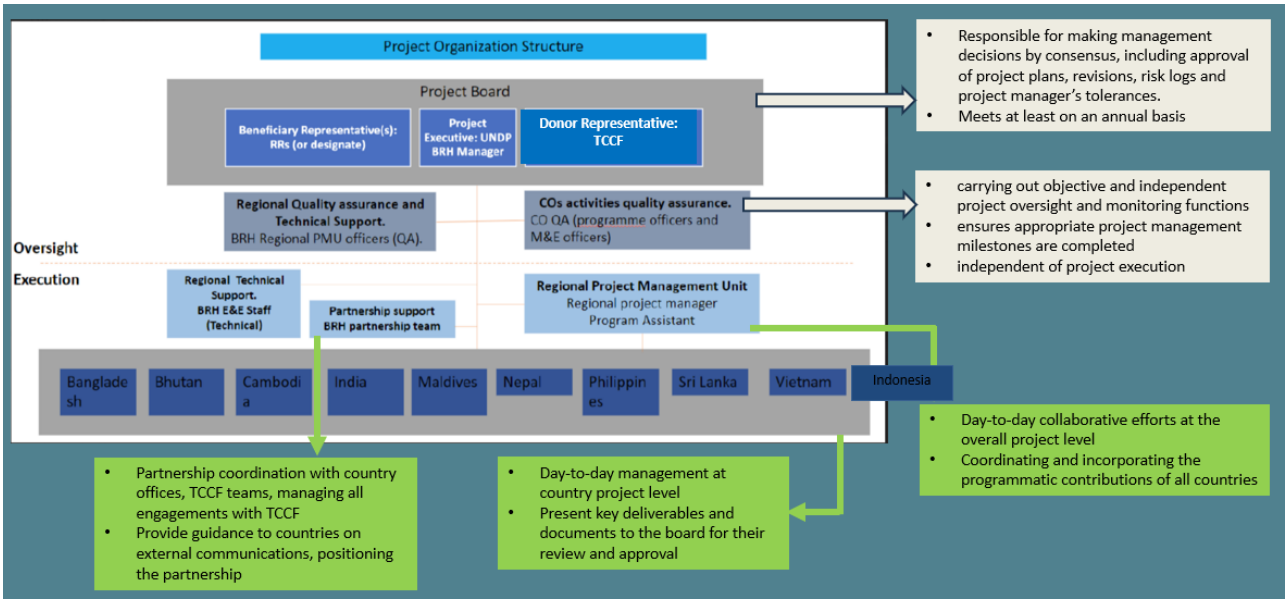

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

IX. LEGAL CONTEXT

Global and Regional Projects

This project forms part of an overall programmatic framework under which several separate associated country level activities will be implemented. When assistance and support services are provided from this Project to the associated country level activities, this document shall be the "Project Document" instrument referred to in: (i) the respective signed SBAAs for the specific countries; or (ii) in the Supplemental Provisions to the Project Document attached to the Project Document in cases where the recipient country has not signed an SBAA with UNDP, attached hereto and forming an integral part hereof. All references in the SBAA to "Executing Agency" shall be deemed to refer to "Implementing Partner."

This project will be implemented by [name of entity] ("Implementing Partner") in accordance with its financial regulations, rules, practices and procedures only to the extent that they do not contravene the principles of the Financial Regulations and Rules of UNDP. Where the financial governance of an Implementing Partner does not provide the required guidance to ensure best value for money, fairness, integrity, transparency, and effective international competition, the financial governance of UNDP shall apply**.**

X. RISK MANAGEMENT

1. UNDP as the Implementing Partner will comply with the policies, procedures and practices of the United Nations Security Management System (UNSMS.)

2. UNDP as the Implementing Partner will undertake all reasonable efforts to ensure that none of the [project funds][17] [UNDP funds received pursuant to the Project Document][18] are used to provide support to individuals or entities associated with terrorism , that the recipients of any amounts provided by UNDP hereunder do not appear on the United Nations Security Council Consolidated Sanctions List, and that no UNDP funds received pursuant to the Project Document are used for money laundering activities. The United Nations Security Council Consolidated Sanctions List can be accessed via https://www.un.org/securitycouncil/content/un-sc-consolidated-list. This provision must be included in all sub-contracts or sub-agreements entered into under this Project Document.

3. Social and environmental sustainability will be enhanced through application of the UNDP Social and Environmental Standards (http://www.undp.org/ses) and related Accountability Mechanism (http://www.undp.org/secu-srm).

4. UNDP as the Implementing Partner will: (a) conduct project and programme-related activities in a manner consistent with the UNDP Social and Environmental Standards, (b) implement any management or mitigation plan prepared for the project or programme to comply with such standards, and (c) engage in a constructive and timely manner to address any concerns and complaints raised through the Accountability Mechanism. UNDP will seek to ensure that communities and other project stakeholders are informed of and have access to the Accountability Mechanism.

5. In the implementation of the activities under this Project Document, UNDP as the Implementing Partner will handle any sexual exploitation and abuse ("SEA") and sexual harassment ("SH") allegations in accordance with its regulations, rules, policies and procedures.

6. All signatories to the Project Document shall cooperate in good faith with any exercise to evaluate any programme or project-related commitments or compliance with the UNDP Social and Environmental Standards. This includes providing access to project sites, relevant personnel, information, and documentation.

7. UNDP as the Implementing Partner will ensure that the following obligations are binding on each responsible party, subcontractor, and sub-recipient:

a. Consistent with the Article III of the SBAA *[or the Supplemental Provisions to the Project Document]*, the responsibility for the safety and security of each responsible party, subcontractor and sub-recipient and its personnel and property, and of UNDP's property in such responsible party's, subcontractor's and sub-recipient's custody, rests with such responsible party, subcontractor and sub-recipient. To this end, each responsible party, subcontractor and sub-recipient shall:

[17] To be used where UNDP is the Implementing Partner

[18] To be used where the UN, a UN fund/programme or a specialized agency is the Implementing Partner

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

i. put in place an appropriate security plan and maintain the security plan, taking into account the security situation in the country where the project is being carried;
ii. assume all risks and liabilities related to such responsible party's, subcontractor's and sub-recipient's security, and the full implementation of the security plan.

b. UNDP reserves the right to verify whether such a plan is in place, and to suggest modifications to the plan when necessary. Failure to maintain and implement an appropriate security plan as required hereunder shall be deemed a breach of the responsible party's, subcontractor's and sub-recipient's obligations under this Project Document.

c. Each responsible party, subcontractor and sub-recipient (each a "sub-party" and together "sub-parties") acknowledges and agrees that UNDP will not tolerate sexual harassment and sexual exploitation and abuse of anyone by the sub-parties, and other entities involved in Project implementation, either as contractors or subcontractors and their personnel, and any individuals performing services for them under the Project Document.
(a) In the implementation of the activities under this Project Document, each sub-party shall comply with the standards of conduct set forth in the Secretary General's Bulletin ST/SGB/2003/13 of 9 October 2003, concerning "Special measures for protection from sexual exploitation and sexual abuse" ("SEA").
(b) Moreover, and without limitation to the application of other regulations, rules, policies and procedures bearing upon the performance of the activities under this Project Document, in the implementation of activities, each sub-party, shall not engage in any form of sexual harassment ("SH"). SH is defined as any unwelcome conduct of a sexual nature that might reasonably be expected or be perceived to cause offense or humiliation, when such conduct interferes with work, is made a condition of employment or creates an intimidating, hostile or offensive work environment. SH may occur in the workplace or in connection with work. While typically involving a pattern of conduct, SH may take the form of a single incident. In assessing the reasonableness of expectations or perceptions, the perspective of the person who is the target of the conduct shall be considered.

d. In the performance of the activities under this Project Document, each sub-party shall (with respect to its own activities), and shall require from its sub-parties (with respect to their activities) that they, have minimum standards and procedures in place, or a plan to develop and/or improve such standards and procedures in order to be able to take effective preventive and investigative action. These should include: policies on sexual harassment and sexual exploitation and abuse; policies on whistleblowing/protection against retaliation; and complaints, disciplinary and investigative mechanisms. In line with this, sub-parties will and will require that their respective sub-parties will take all appropriate measures to:
(i) Prevent its employees, agents or any other persons engaged to perform any services under this Project Document, from engaging in SH or SEA;
(ii) Offer employees and associated personnel training on prevention and response to SH and SEA, where sub-parties have not put in place its own training regarding the prevention of SH and SEA, sub-parties may use the training material available at UNDP;
(iii) Report and monitor allegations of SH and SEA of which any of the sub-parties have been informed or have otherwise become aware, and status thereof;
(iv) Refer victims/survivors of SH and SEA to safe and confidential victim assistance; and
(v) Promptly and confidentially record and investigate any allegations credible enough to warrant an investigation of SH or SEA. Each sub-party shall advise UNDP of any such allegations received and investigations being conducted by itself or any of its sub-parties with respect to their activities under the Project Document, and shall keep UNDP informed during the investigation by it or any of such sub-parties, to the extent that such notification (i) does not jeopardize the conduct of the investigation, including but not limited to the safety or security of persons, and/or (ii) is not in contravention of any laws applicable to it. Following the investigation, the relevant sub-party shall advise UNDP of any actions taken by it or any of the other entities further to the investigation.

e. Each sub-party shall establish that it has complied with the foregoing, to the satisfaction of UNDP, when requested by UNDP or any party acting on its behalf to provide such confirmation. Failure of the relevant sub-party to comply of the foregoing, as determined by UNDP, shall be considered grounds for suspension or termination of the Project.

f. Each responsible party, subcontractor and sub-recipient will ensure that any project activities undertaken by them will be implemented in a manner consistent with the UNDP Social and Environmental Standards and shall ensure that any incidents or issues of non-compliance shall be reported to UNDP in accordance with UNDP Social and Environmental Standards.

g. Each responsible party, subcontractor and sub-recipient will take appropriate steps to prevent misuse of funds, fraud, corruption or other financial irregularities, by its officials, consultants, subcontractors and sub-recipients in implementing the project or programme or using the UNDP funds. It will ensure

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

that its financial management, anti-corruption, anti-fraud and anti money laundering and countering the financing of terrorism policies are in place and enforced for all funding received from or through UNDP.

h. The requirements of the following documents, then in force at the time of signature of the Project Document, apply to each responsible party, subcontractor and sub-recipient: (a) UNDP Policy on Fraud and other Corrupt Practices (b) UNDP Anti-Money Laundering and Countering the Financing of Terrorism Policy; and (c) UNDP Office of Audit and Investigations Investigation Guidelines. Each responsible party, subcontractor and sub-recipient agrees to the requirements of the above documents, which are an integral part of this Project Document and are available online at www.undp.org.

i. In the event that an investigation is required, UNDP will conduct investigations relating to any aspect of UNDP programmes and projects. Each responsible party, subcontractor and sub-recipient will provide its full cooperation, including making available personnel, relevant documentation, and granting access to its (and its consultants', subcontractors' and sub-recipients') premises, for such purposes at reasonable times and on reasonable conditions as may be required for the purpose of an investigation. Should there be a limitation in meeting this obligation, UNDP shall consult with it to find a solution.

j. Each responsible party, subcontractor and sub-recipient will promptly inform UNDP as the Implementing Partner in case of any incidence of inappropriate use of funds, or credible allegation of fraud, corruption other financial irregularities with due confidentiality.
Where it becomes aware that a UNDP project or activity, in whole or in part, is the focus of investigation for alleged fraud/corruption, each responsible party, subcontractor and sub-recipient will inform the UNDP Resident Representative/Head of Office, who will promptly inform UNDP's Office of Audit and Investigations (OAI). It will provide regular updates to the head of UNDP in the country and OAI of the status of, and actions relating to, such investigation.

k. Choose one of the three following options:
Option 1: UNDP will be entitled to a refund from the responsible party, subcontractor or sub-recipient of any funds provided that have been used inappropriately, including through fraud corruption, other financial irregularities or otherwise paid other than in accordance with the terms and conditions of this Project Document. Such amount may be deducted by UNDP from any payment due to the responsible party, subcontractor or sub-recipient under this or any other agreement. Recovery of such amount by UNDP shall not diminish or curtail any responsible party's, subcontractor's or sub-recipient's obligations under this Project Document.

Option 2: Each responsible party, subcontractor or sub-recipient agrees that, where applicable, donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities which are the subject of the Project Document, may seek recourse to such responsible party, subcontractor or sub-recipient for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud corruption or other financial irregularities or otherwise paid other than in accordance with the terms and conditions of the Project Document.

Option 3: UNDP will be entitled to a refund from the responsible party, subcontractor or sub-recipient of any funds provided that have been used inappropriately, including through fraud corruption or other financial irregularities, or otherwise paid other than in accordance with the terms and conditions of the Project Document. Such amount may be deducted by UNDP from any payment due to the responsible party, subcontractor or sub-recipient under this or any other agreement.

Where such funds have not been refunded to UNDP, the responsible party, subcontractor or sub-recipient agrees that donors to UNDP (including the Government) whose funding is the source, in whole or in part, of the funds for the activities under this Project Document, may seek recourse to such responsible party, subcontractor or sub-recipient for the recovery of any funds determined by UNDP to have been used inappropriately, including through fraud, corruption or other financial irregularities, or otherwise paid other than in accordance with the terms and conditions of the Project Document.

Note: The term "Project Document" as used in this clause shall be deemed to include any relevant subsidiary agreement further to the Project Document, including those with responsible parties, subcontractors and sub-recipients.

l. Each contract issued by the responsible party, subcontractor or sub-recipient in connection with this Project Document shall include a provision representing that no fees, gratuities, rebates, gifts, commissions or other payments, other than those shown in the proposal, have been given, received,

Docusign Envelope ID: 9DD26F48-82E2-4A4A-9E4C-9D5F80BCC32C

or promised in connection with the selection process or in contract execution, and that the recipient of funds from it shall cooperate with any and all investigations and post-payment audits.

m. Should UNDP refer to the relevant national authorities for appropriate legal action any alleged wrongdoing relating to the project or programme, the Government will ensure that the relevant national authorities shall actively investigate the same and take appropriate legal action against all individuals found to have participated in the wrongdoing, recover and return any recovered funds to UNDP.

n. Each responsible party, subcontractor and sub-recipient shall ensure that all of its obligations set forth under this section entitled “Risk Management” are passed on to its subcontractors and sub-recipients and that all the clauses under this section entitled “Risk Management Standard Clauses” are adequately reflected, *mutatis mutandis*, in all its sub-contracts or sub-agreements entered into further to this Project Document.

XI. ANNEXES (SEPARATELY)

ANNEX 1: PROJECT QUALITY ASSURANCE REPORT (SUBMITTED SEPARATELY in Quantum+)

ANNEX 2: SOCIAL AND ENVIRONMENTAL SCREENING (SUBMITTED SEPARATELY in Quantum+)

ANNEX 3: PROJECT RISK REGISTER

ANNEX 4: PROCUREMENT PLAN

ANNEX 5: BREAKDOWN OF PARTNERSHIP TARGET INDICATOR BY AREA AND BY COUNTRY
